




Job Name: 26-1577 - Elkhorn Elementary Redesign Job Location: Frankfort, KY 40601 Contractor: Louisville Paving and Construction					Plant: 100 5/5/2026 1:40:52 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: MH4-6 SS-MH											
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red T/n						
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-350 F/C FSD 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO					0 lb 270 lb 1738 lb 2911 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb ----- Structure Total: 6680 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. CONBLOCK CDA RED ADMIXTURE REQUIRED 6. NO STEPS 7. HOE MC-350 FRAME & COVER "SANITARY FSD" SUPPLIED BY ICAST				
Rim: 756.51' Rim to Invert: 4.85' Slack: 1.2" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	751.66'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	751.76'	243°	123"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

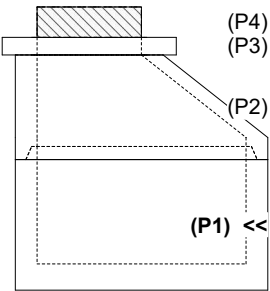


RIGHT-SIDE UP VIEW (int. dimensions)

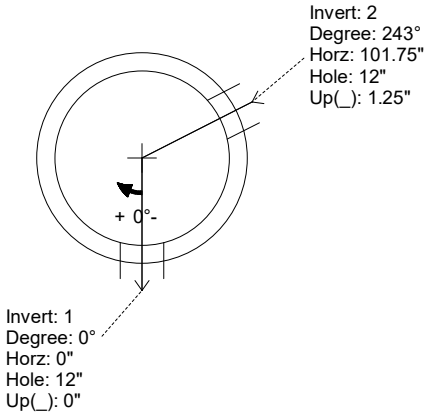

UPSIDE-DOWN VIEW (int. dimenions)

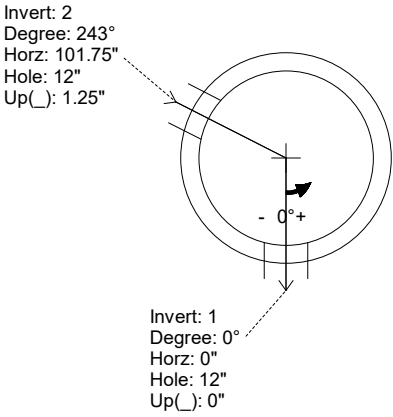


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1577 - Elkhorn Elementary Redesign Job Location: Frankfort, KY 40601 Contractor: Louisville Paving and Construction					Plant: 100 5/5/2026 1:40:52 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: MH4-6 SS-MH											
P1 MH048BA24CDARED MH BASE w/ConBlock-CDA Red T/n											
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-350 F/C FSD 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO Structure Total: 6680 lb						0 lb 270 lb 1738 lb 2911 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb ----- 6680 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. CONBLOCK CDA RED ADMIXTURE REQUIRED 6. NO STEPS 7. HOE MC-350 FRAME & COVER "SANITARY FSD" SUPPLIED BY ICAST			
Rim: 756.51' Rim to Invert: 4.85' Slack: 1.2" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	751.66'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	751.76'	243°	123"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

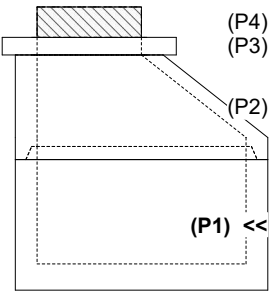


RIGHT-SIDE UP VIEW (int. dimensions)

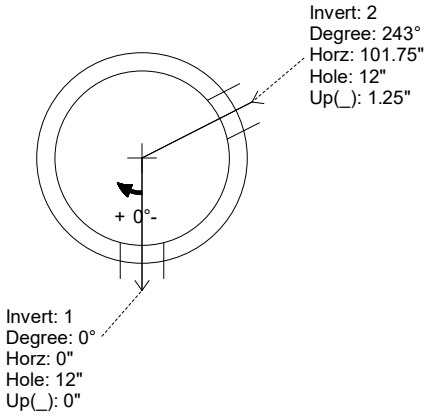

UPSIDE-DOWN VIEW (int. dimenions)

INVERT CHANNEL DRAWING

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
