

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Pee wee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

7/22/2026 12:46:27 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 335-112 DBI3

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 37"
1) 36" x 36" - Conseal CS-102 1.00"
2) Hole - 18

Structure Total: 5801 lb

Structure Notes:

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




Rim: 808.32' Rim to Invert: 3.82' Slack: 0.84" Sump: 0" Step Position: 90°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	804.5'	30°	30.625"	15" CMP	16"	Hole 18	18"	20.785"	-1.5"	-9"
Invert 2	804.5'	245°	22.75"	15" CMP	16"	Hole 18	18"	19.861"	-1.5"	8"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

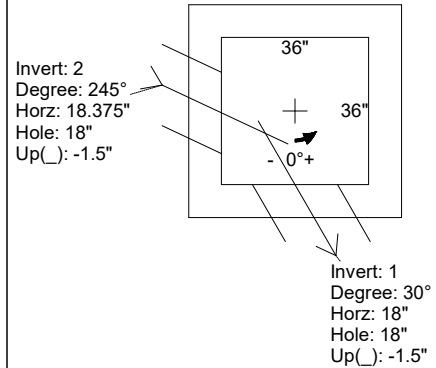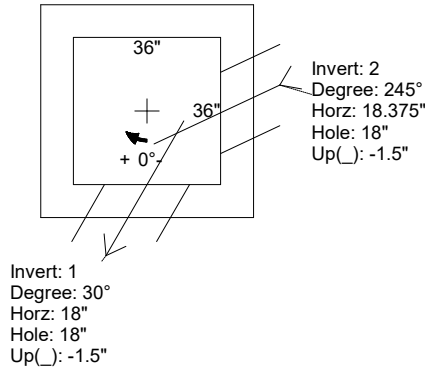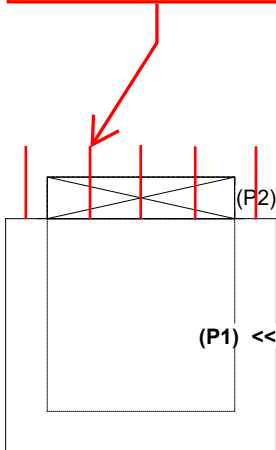

INSIDE WALL DIMENSIONS

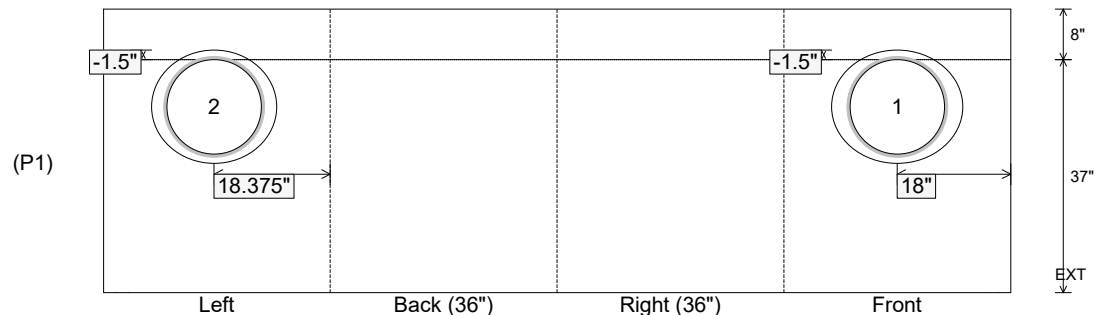

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 37"
Height (Ext): 45"

Weight (Net): 5801 lb
Volume (Net): 1.48cu.yd
