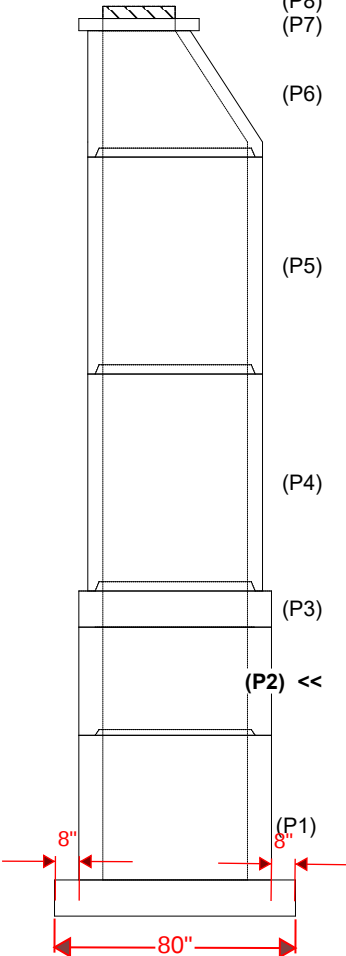
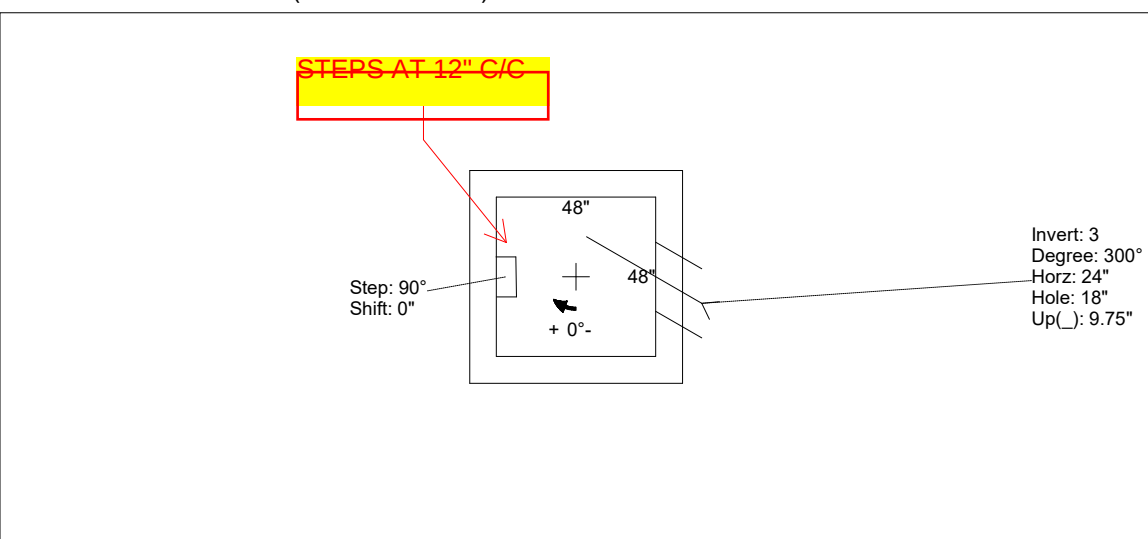
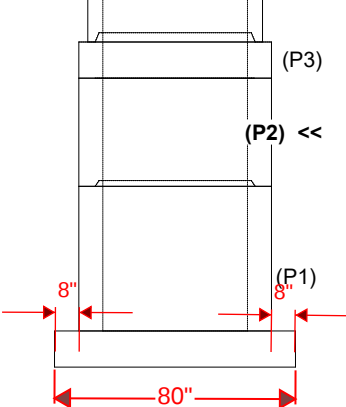
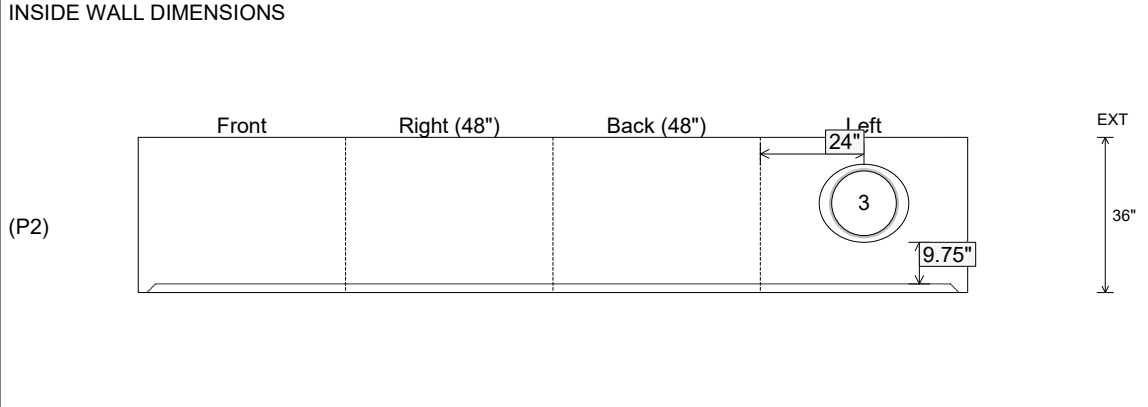


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.	Plant: 100 7/23/2026 3:01:03 PM	Tech: Jared - F PC: T. Ryan	
Structure ID: 37887-149 MHC			
P2 BX4848-08RVF		BOX RISER 8inW F/G	

P8) 24" - CASTING HEIGHT - 4" P7) 24" - GRADE RING F/F - 4" P6) 48" - ECC CONE w/ 24" HOLE F/G - 42" P5) 48" - MH RISER T/G - 72" P4) 48" - MH RISER T/G - 72" P3) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 12" P2) 48" x 48" - BOX RISER 8inW F/G - 36" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF T/n - 48" 2) 48" x 48" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 40 1) Hole - 18 24) MH Step ML-10-TDS-NCR - 10"	0 lb 270 lb 3200 lb 5030 lb 5030 lb 2302 lb 5216 lb 11975 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 33023 lb	Structure Notes: ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-206 F/C (KY TY1)). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE(8"WD x 12" THICK). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - RISER/WALLS (As.12) - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..
Rim: 764.77' Rim to Invert: 24.32' Slack: 1.84" Sump: 0" Step Position: 90°		

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3	745.55'	300°	36.625"	15" CMP	16"	Hole 18	18"	20.785"	9.75"	-12"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

	RIGHT-SIDE UP VIEW (int. dimensions)			
				
	INSIDE WALL DIMENSIONS			
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 5216 lb Volume (Net): 1.33cu.yd
