

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 48"


Rim to Invert: 4.7'

Floor Height: 8"

Slack: 0.4"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 9473 lb

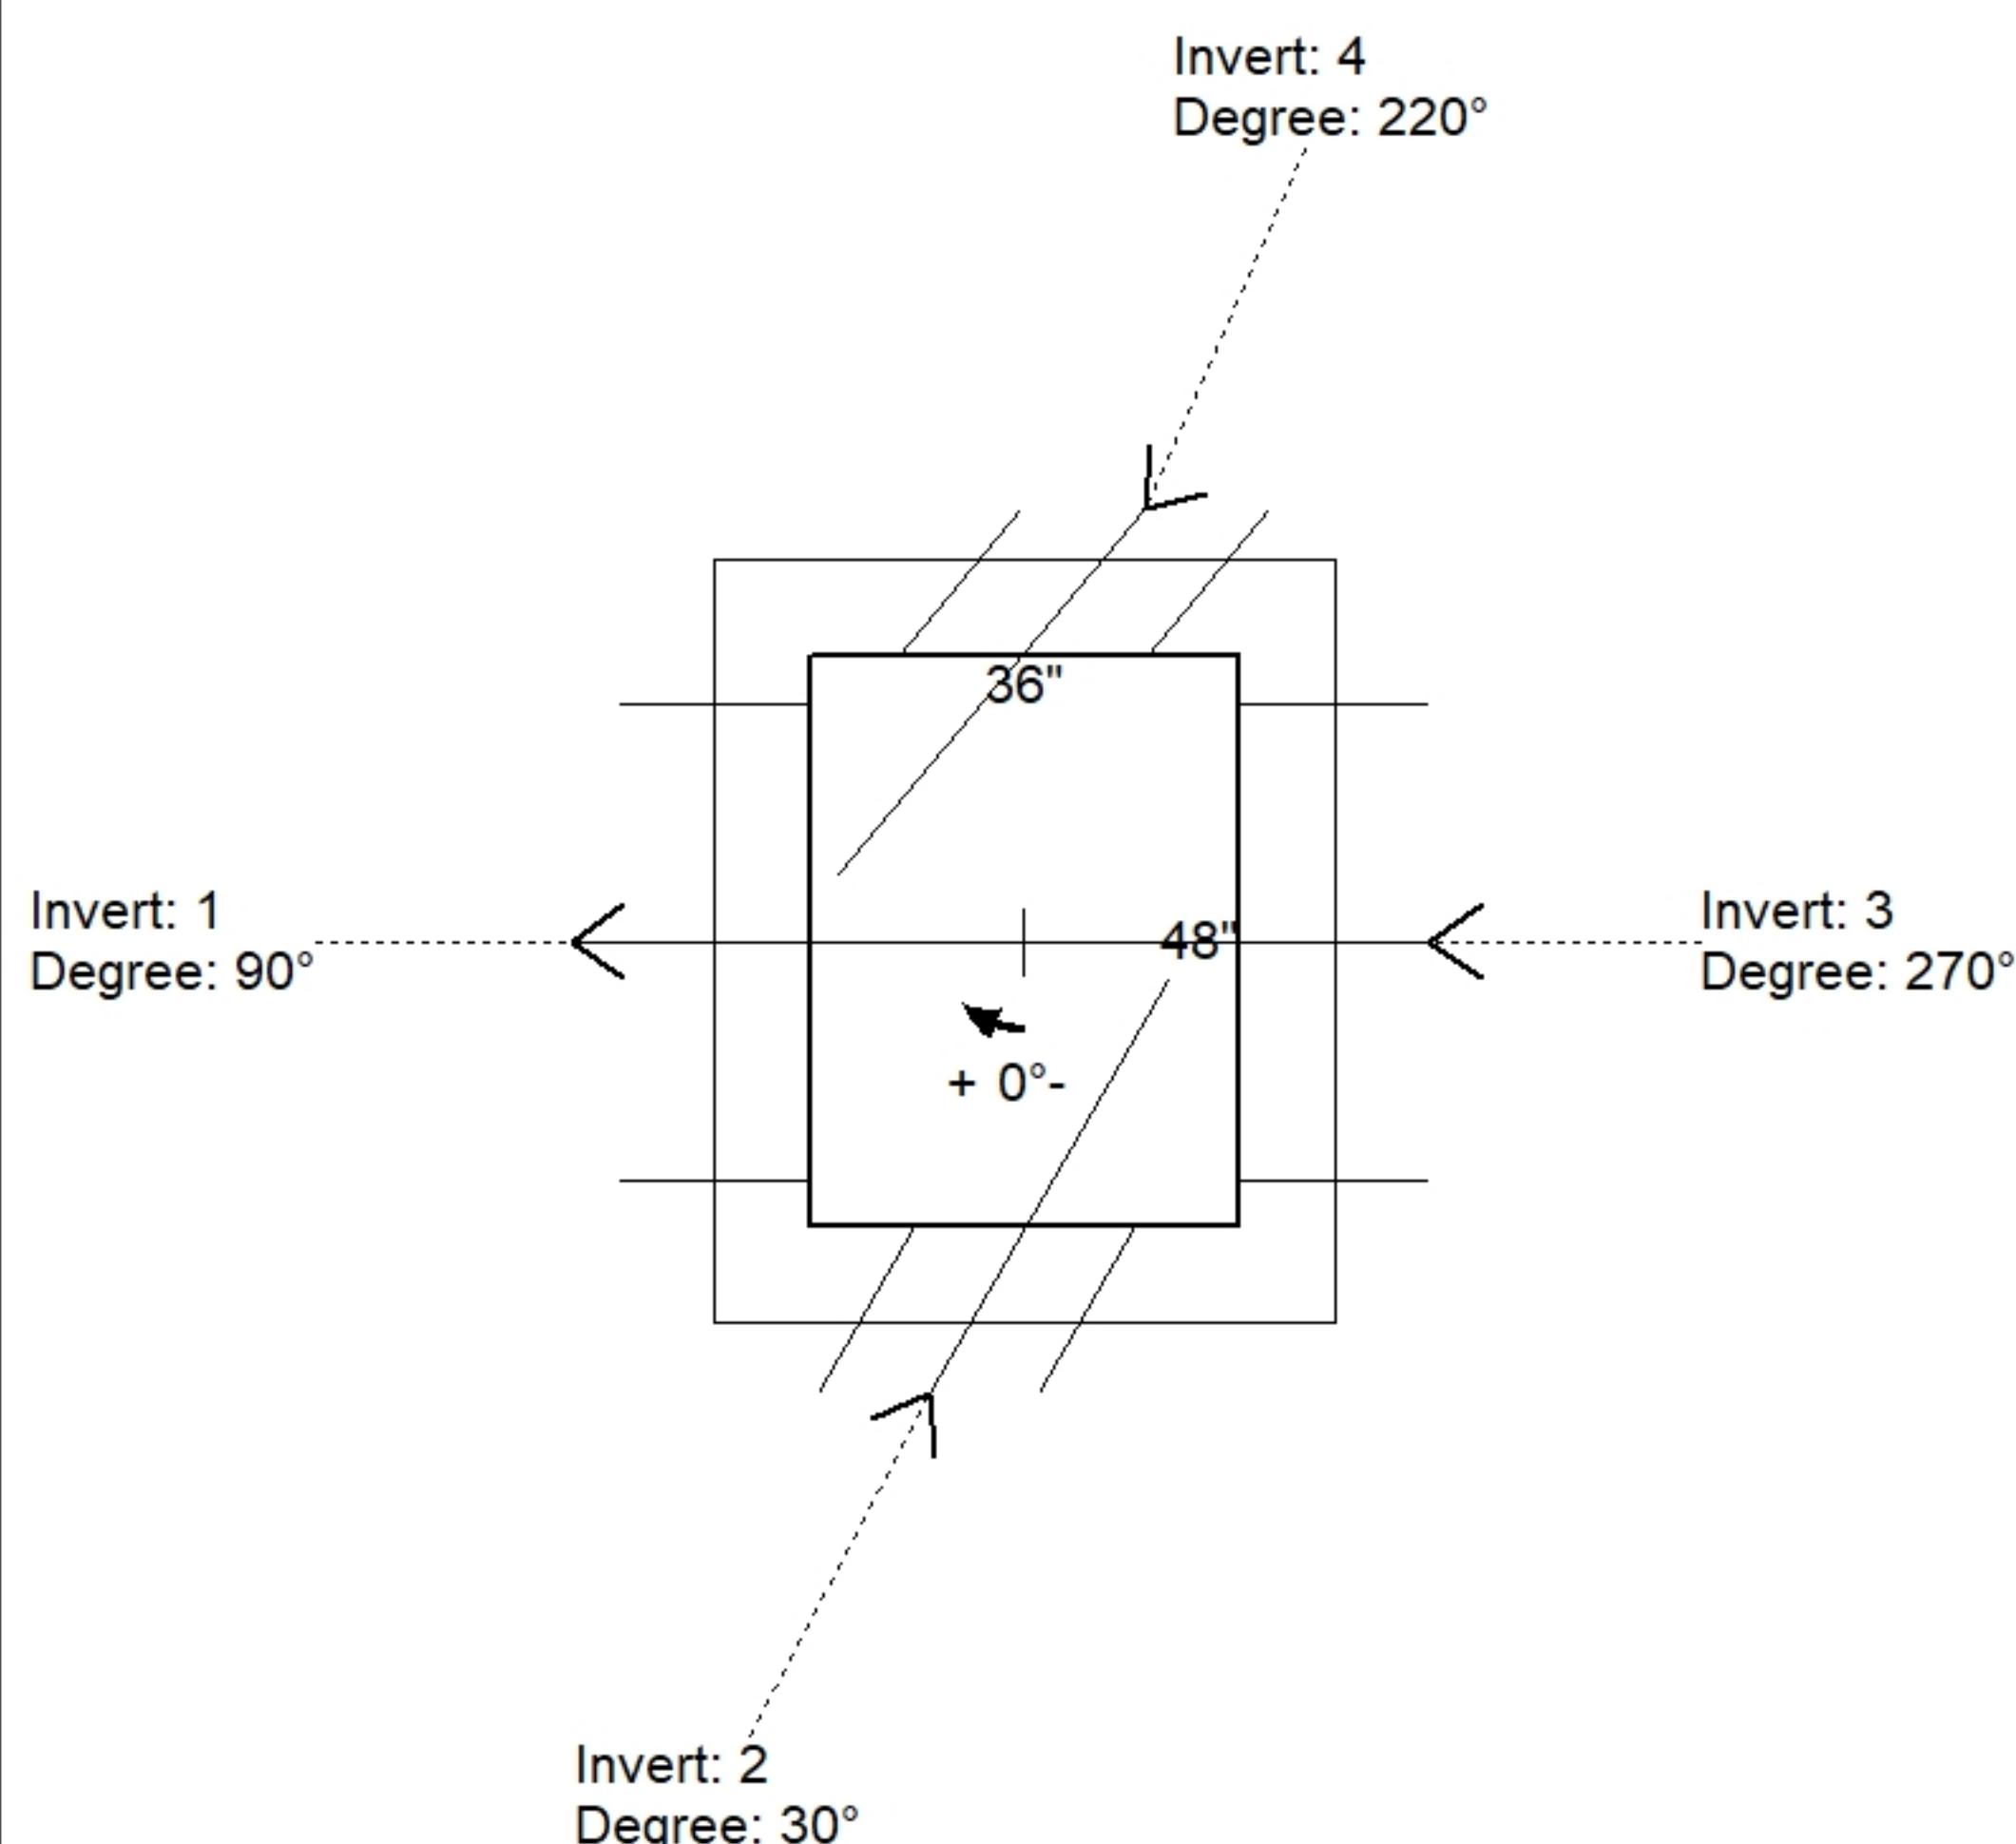


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	748.66'							
Reducer								
Invert 1	743.96'	90°	36" CMP	37"	40"	Hole 40	-2"	P1
Invert 2	744.04'	30°	12" CMP	13"	16"	Hole 16	-1.04"	P1
Invert 3	744.04'	270°	36" CMP	37"	40"	Hole 40	-1.04"	P1
Invert 4	744.04'	220°	12" CMP	13"	16"	Hole 16	-1.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

36" x 48" - CB FLAT TOP 8"W SOLID - 12" - (P2)

36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 44" - (P1)

Default - Interior Dimensions

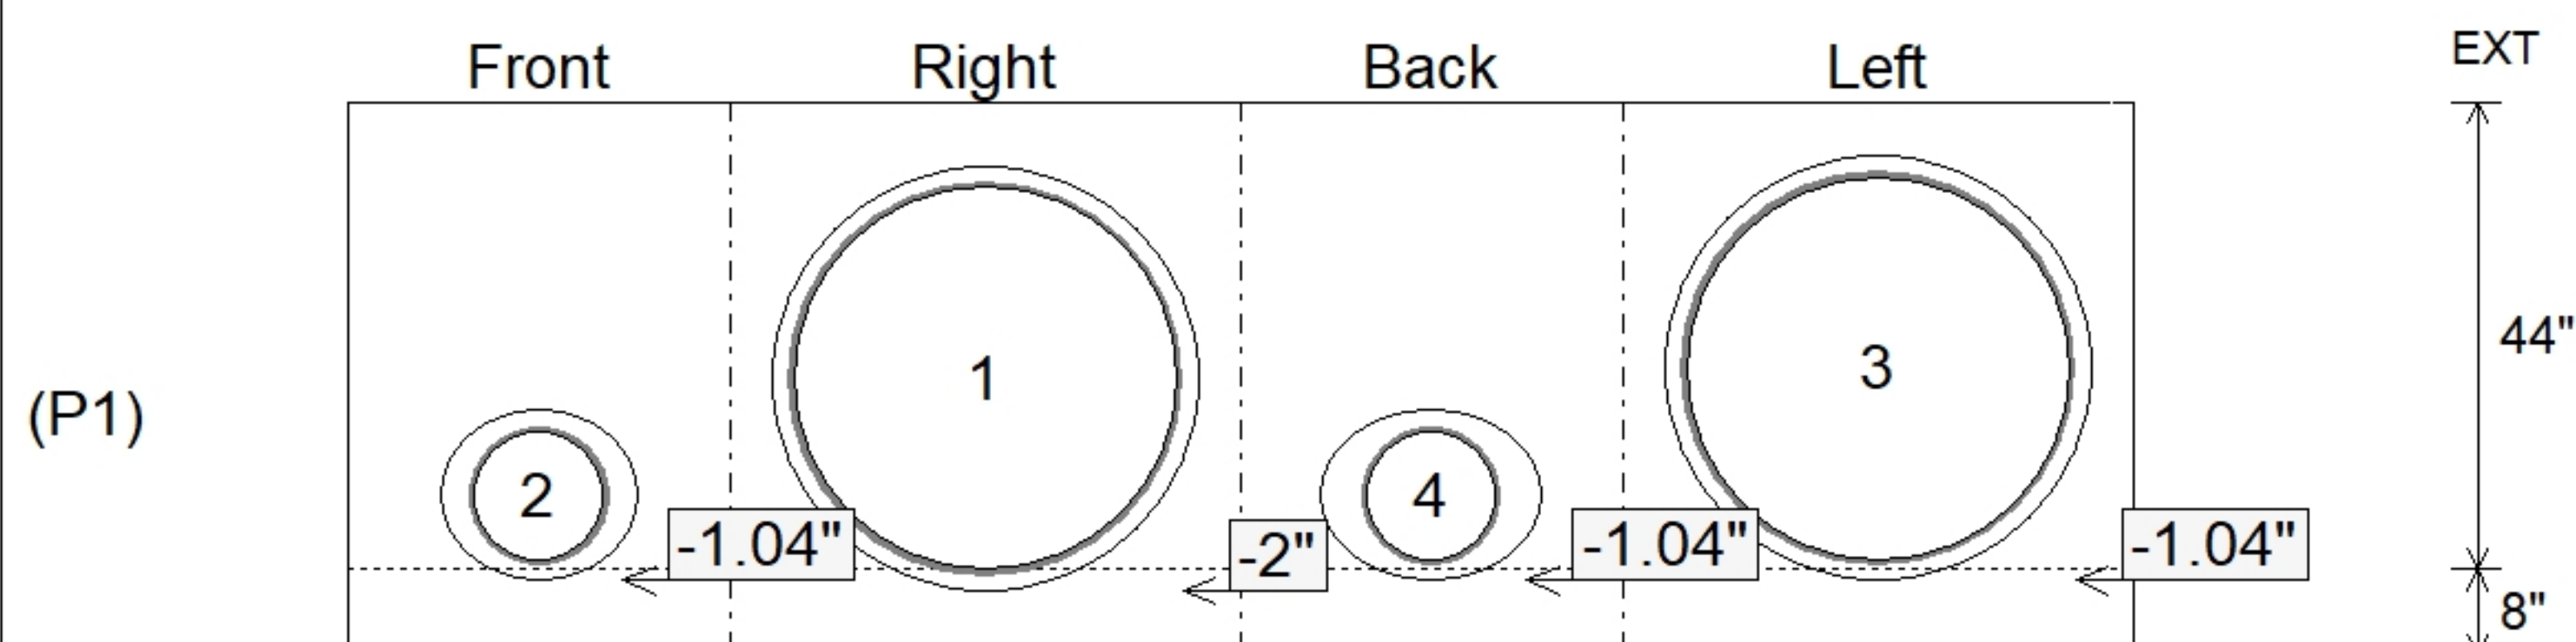

SUBMITTAL
APPROVED BY:
