

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.09'

Floor Height: 8"

Slack: 3.08"

**** KYTC STATE PROJECT ****

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).


REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

- P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22
1) Hole - 18
1) Hole - 6

3400 lb
5270 lb
3996 lb
206 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 12872 lb

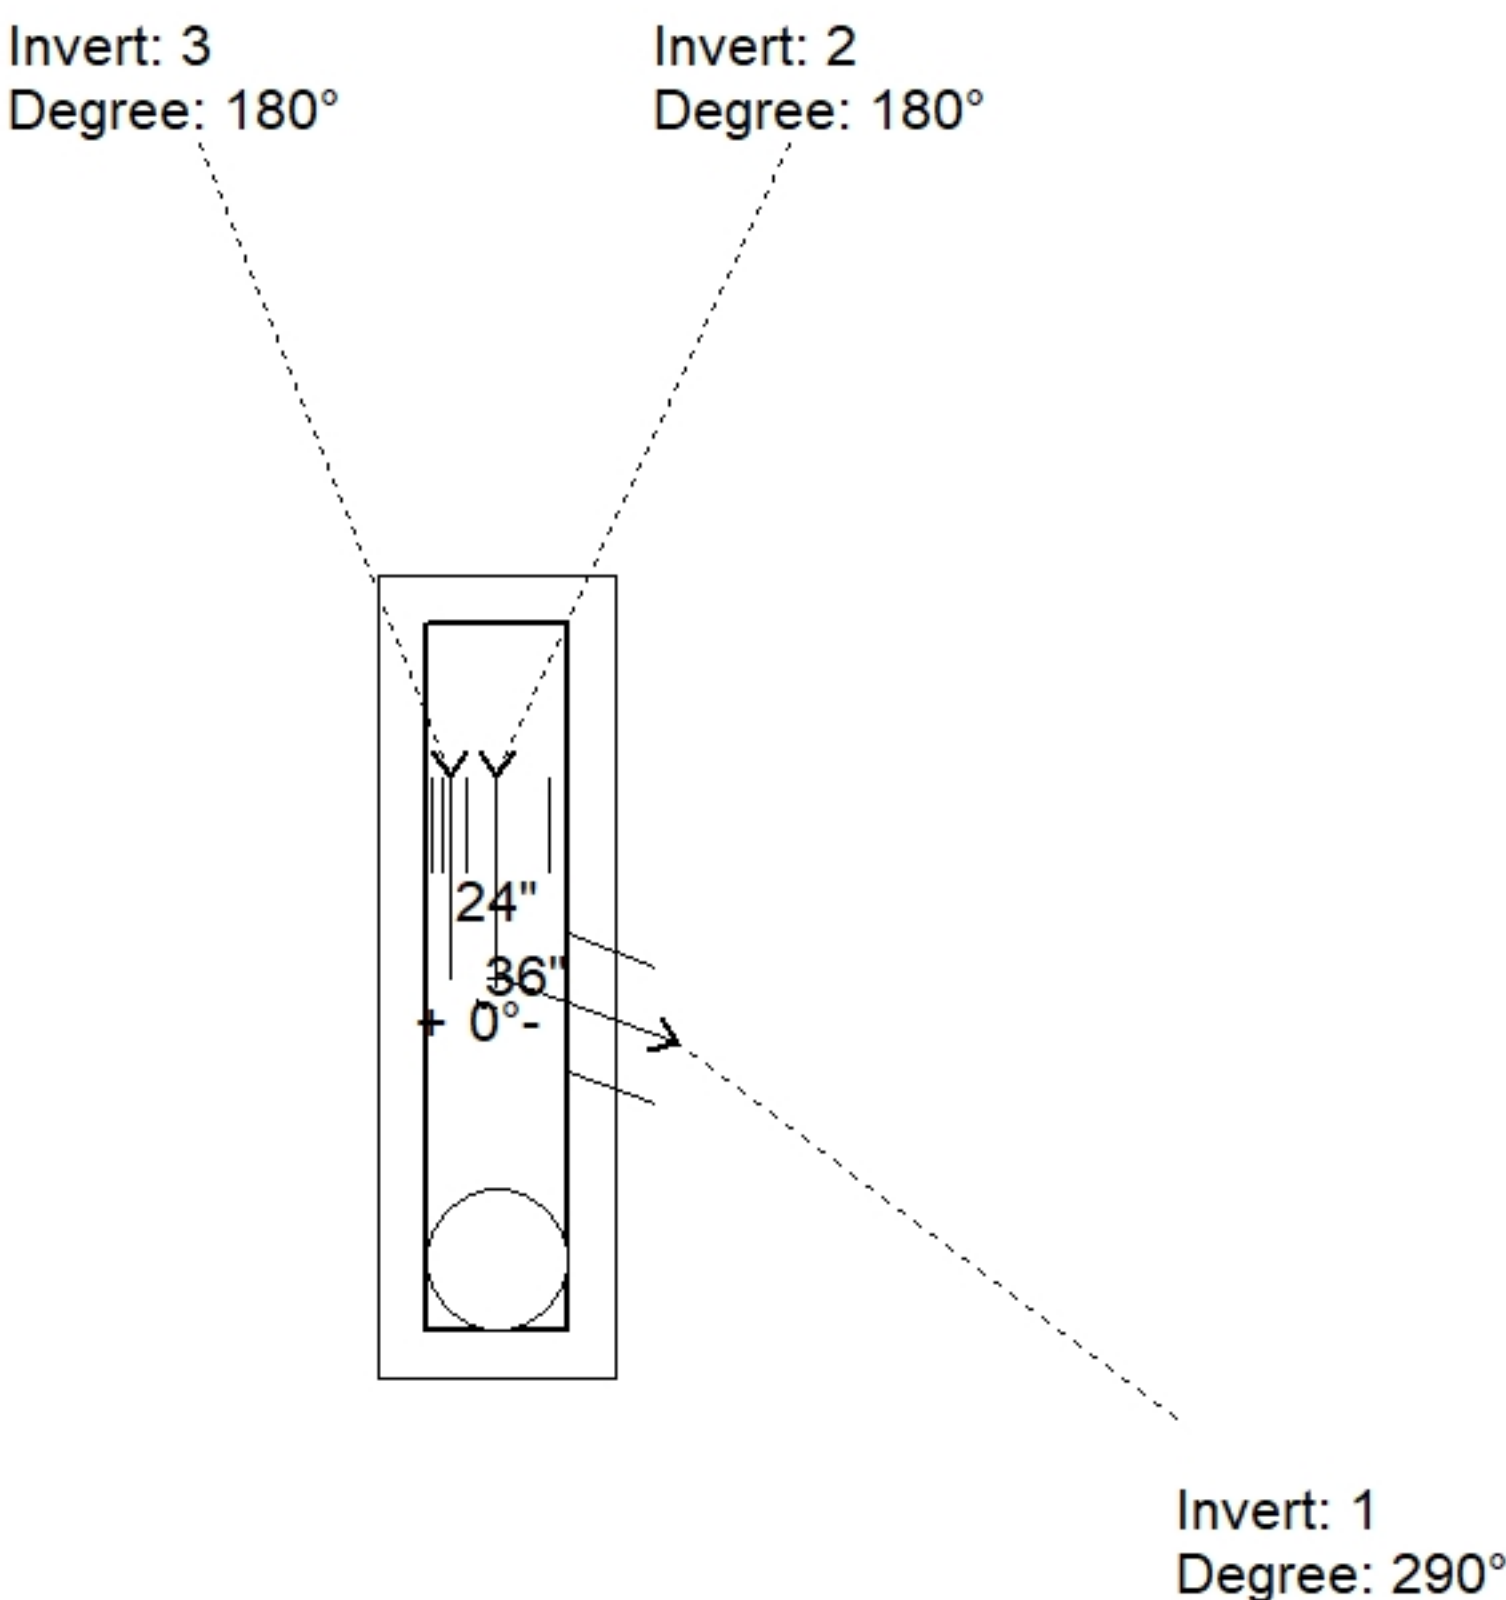


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	780.38'							
Reducer								
Invert 1	775.29'	290°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	775.37'	180°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 3	777.04'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	20"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF - 30" - (P1)

Default - Interior Dimensions

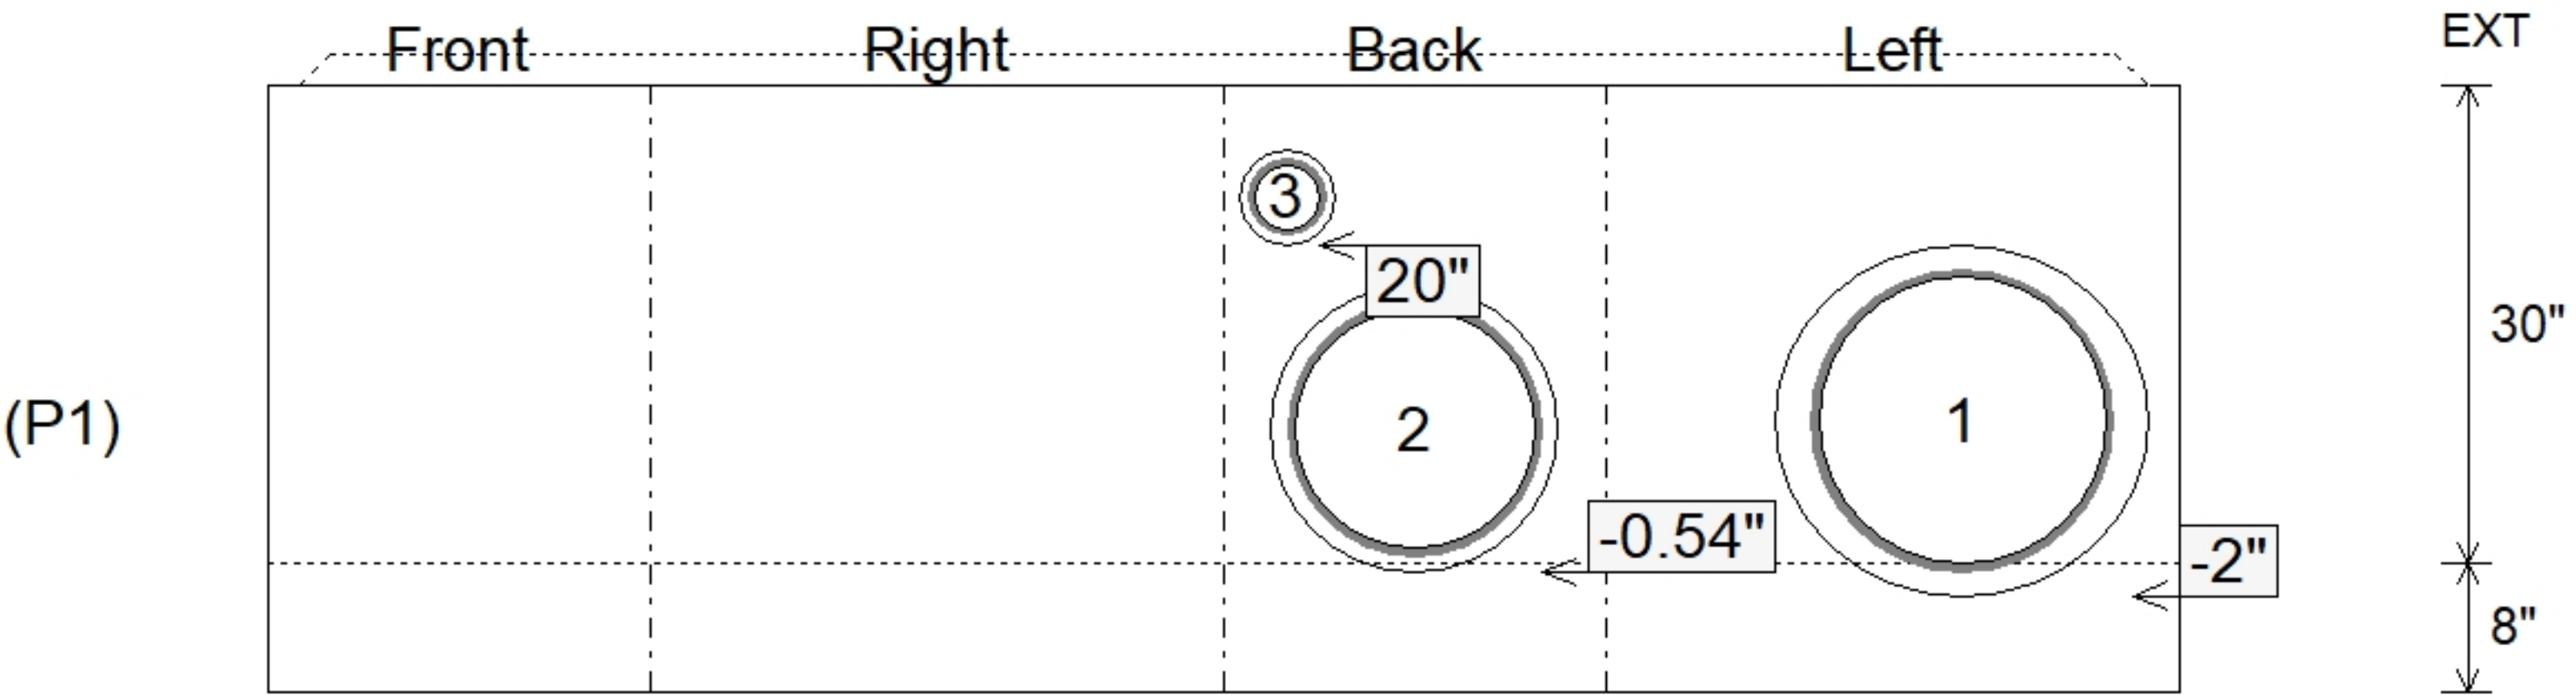

Submittal Drawing
7/28/2026 3:10:51 PM

SUBMITTAL
APPROVED BY:
