

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 4.83'

Floor Height: 8"


Slack: 3.96"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"	3398 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"	5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"	3859 lb
1) CASTING - HOE KY-206 F/C (KY CBI A)	206 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb
1) Hole - 6	0 lb

Structure Total: 12733 lb

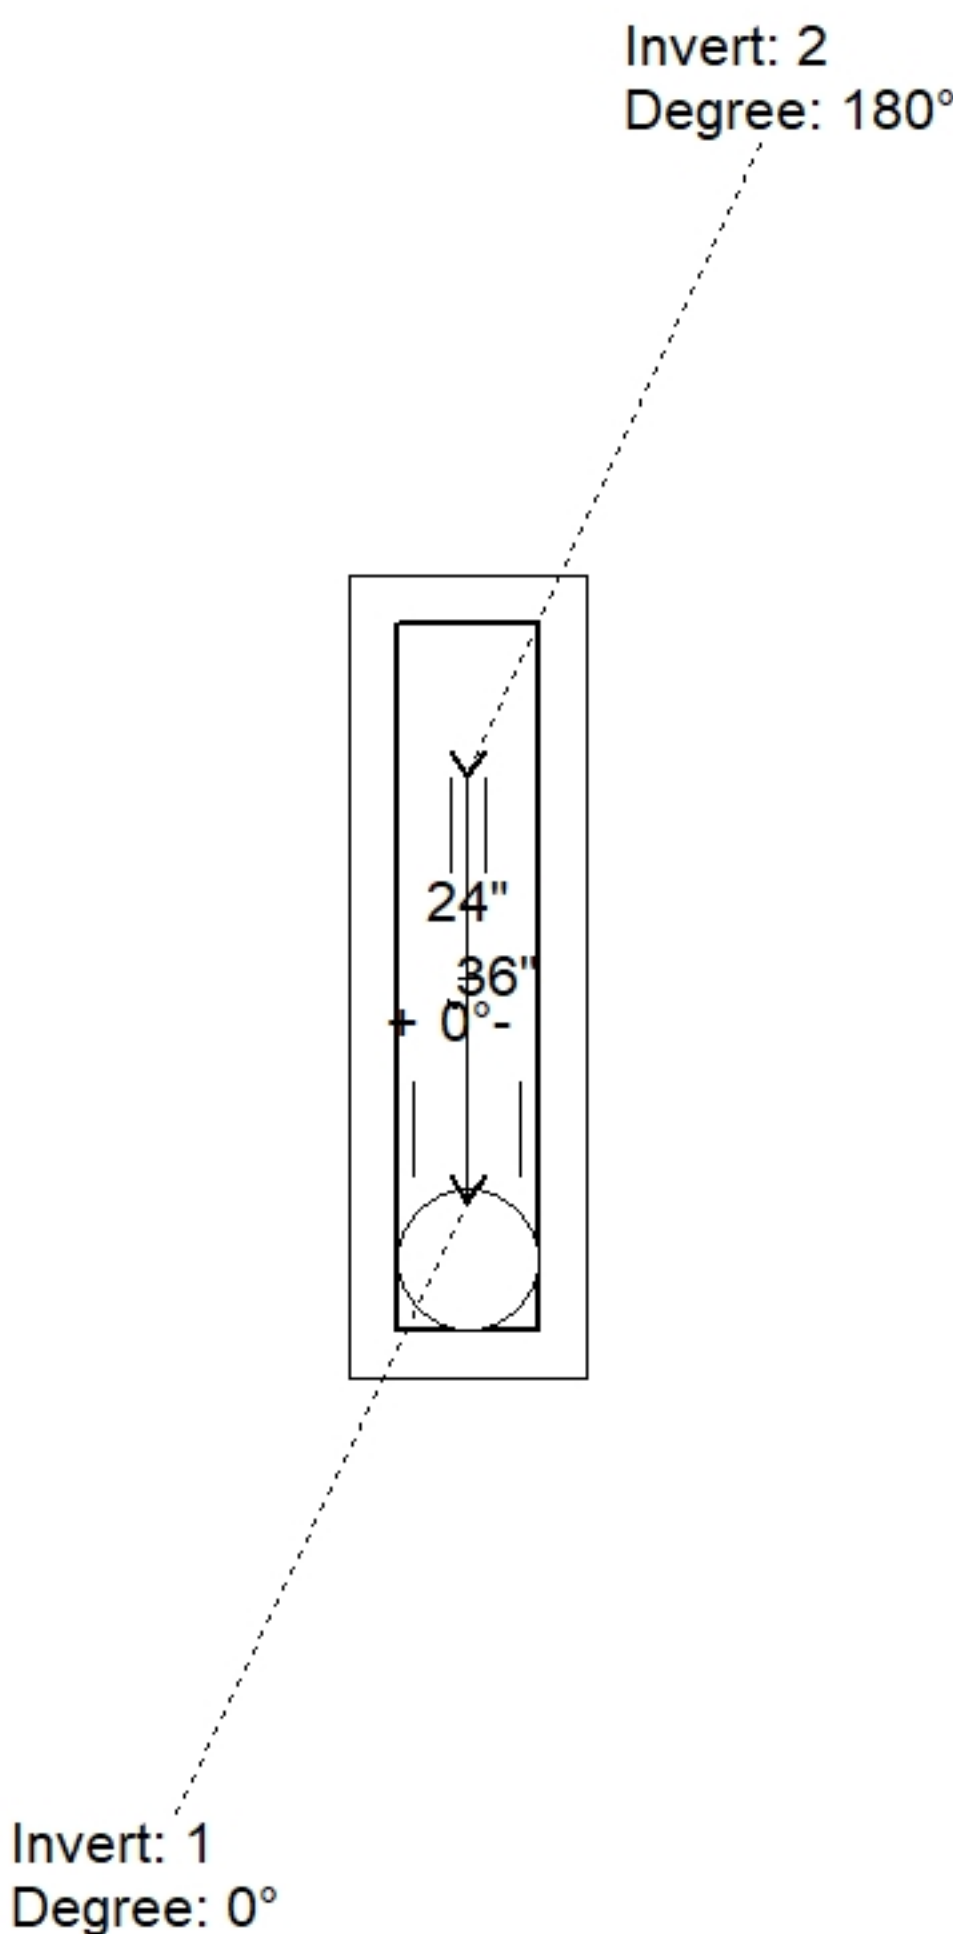


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	790.83'							
Reducer								
Invert 1	786'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	787.42'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	16.04"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" - (P1)

Default - Interior Dimensions

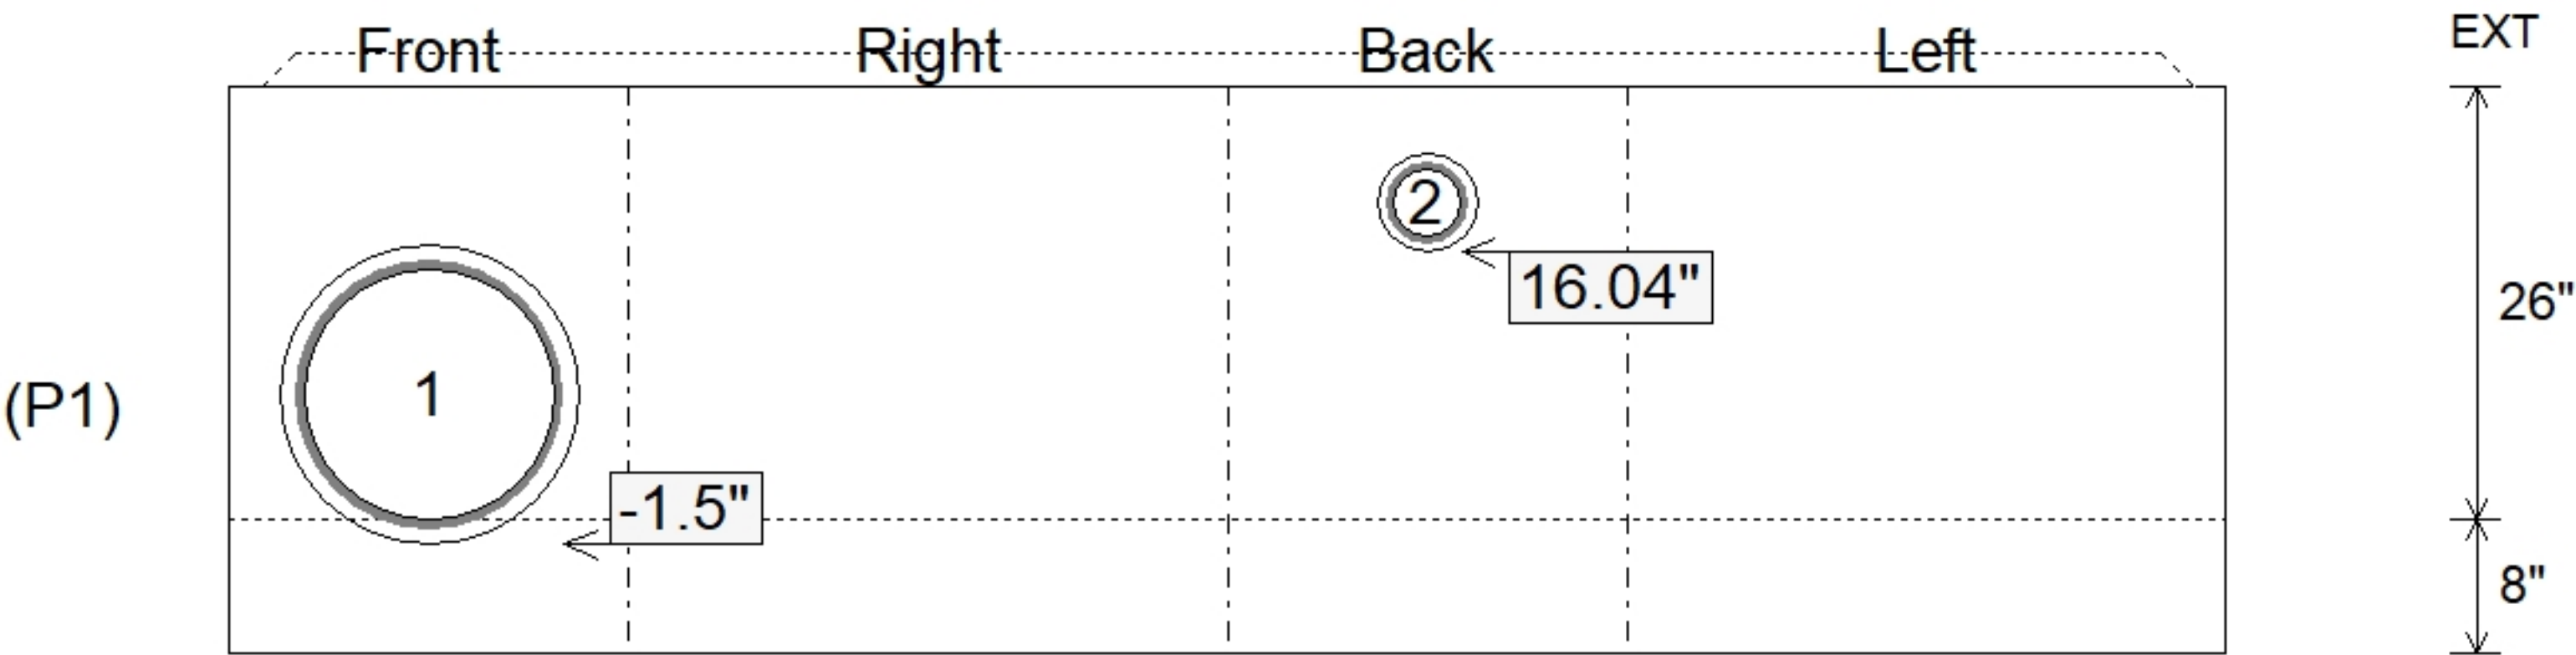

Submittal Drawing
7/28/2026 3:11:08 PM

SUBMITTAL
APPROVED BY:
