

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"


Rim to Invert: 7.62'

Floor Height: 8"

Slack: 3.44"


- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 16659 lb

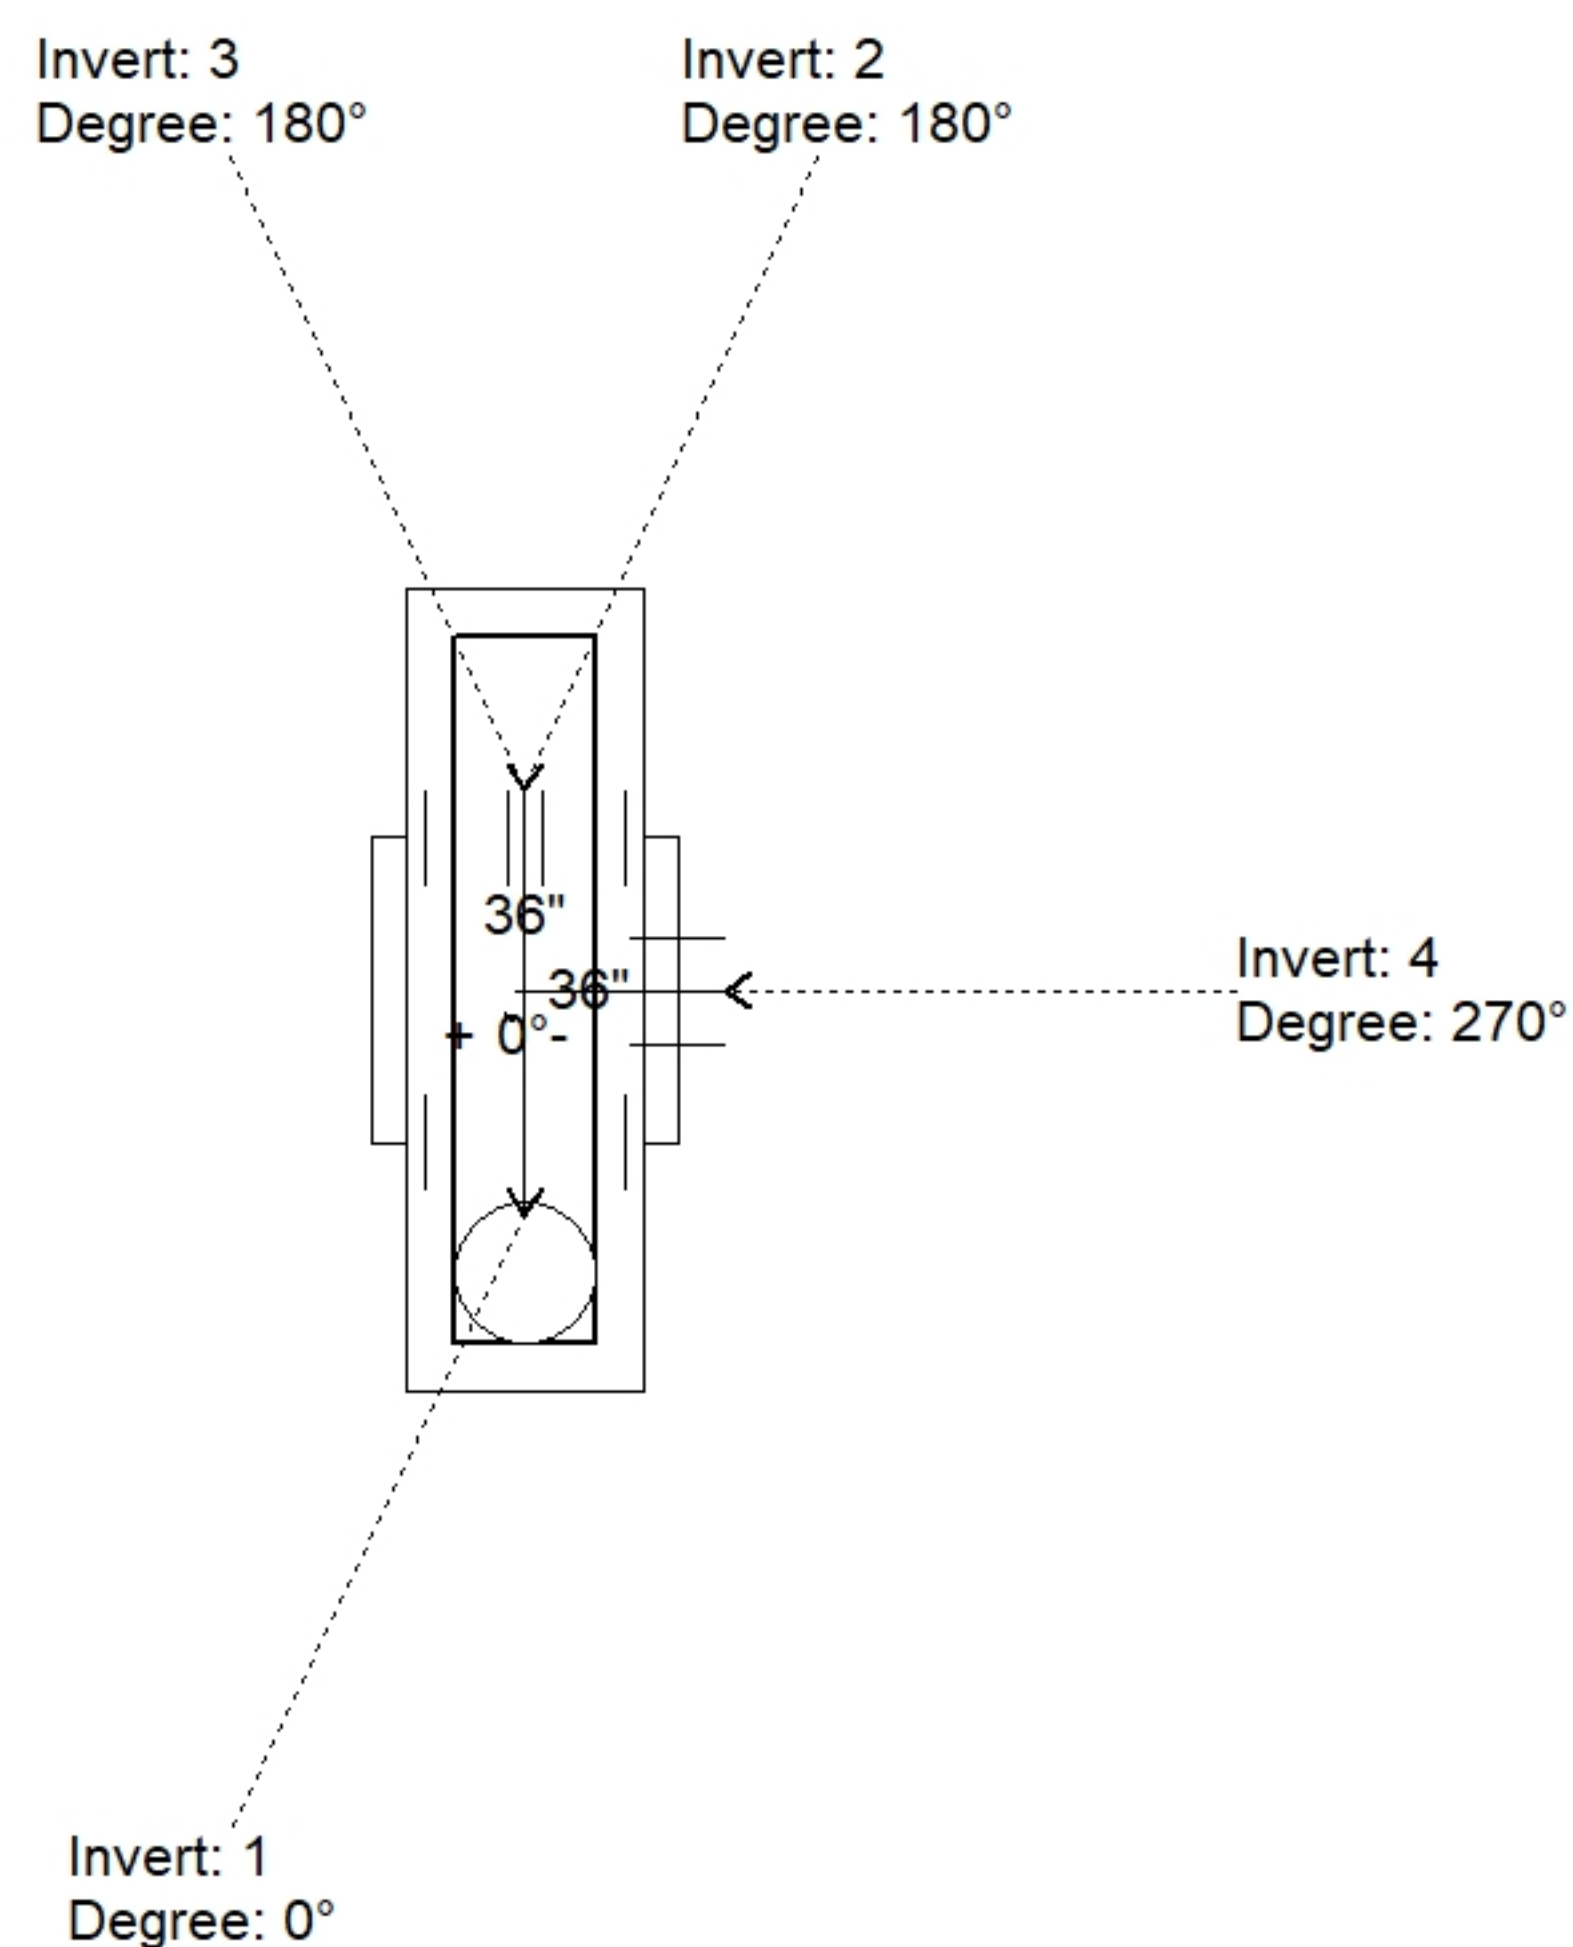

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	807.99'							
Reducer	804.703'							
Invert 1	800.37'	0°	30" CMP	31"	34"	Hole 34	-2"	P1
Invert 2	800.45'	180°	30" CMP	31"	34"	Hole 34	-1.04"	P1
Invert 3	803.95'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	41.96"	P1
Invert 4	800.45'	270°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 52" - (P1)

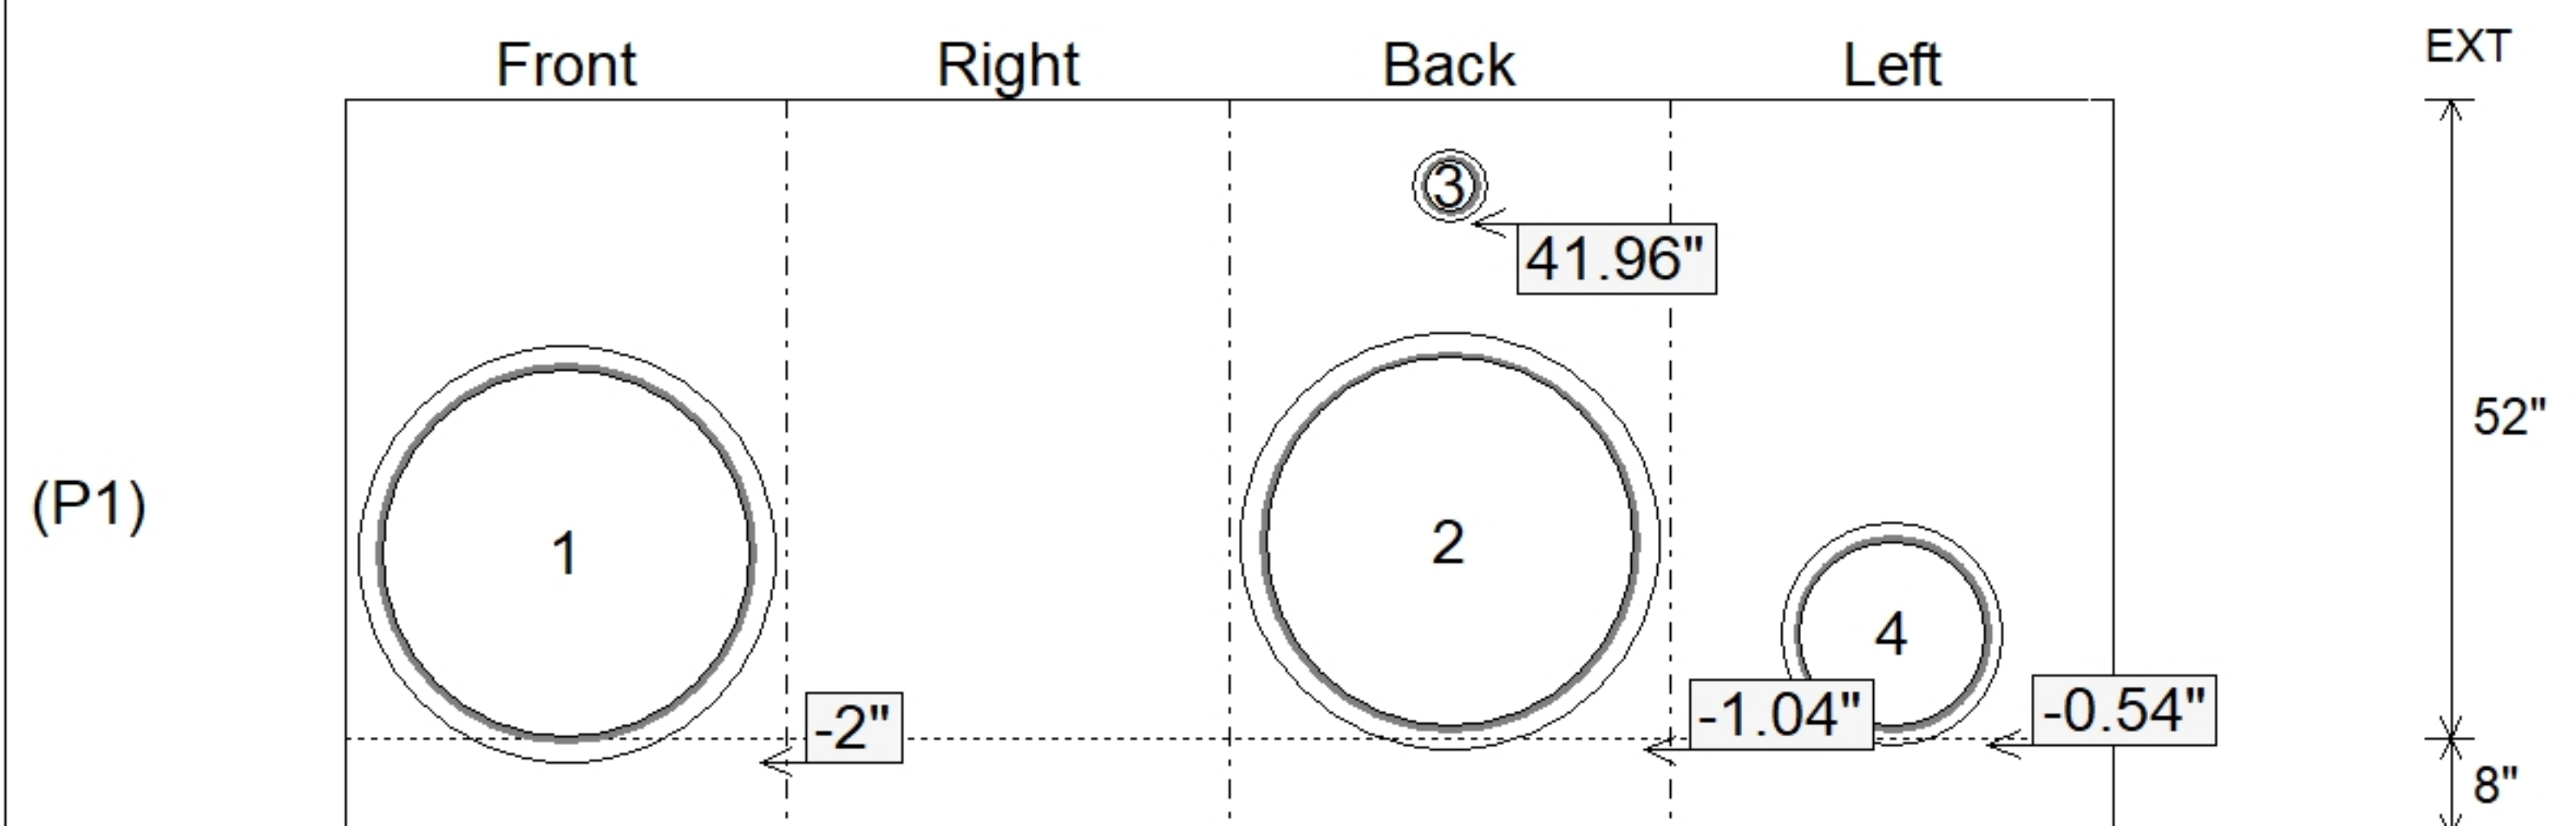

SUBMITTAL
APPROVED BY:
