


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.				Plant: 100 7/24/2026 2:04:10 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 16846-41 CBIA-35										
P1 BX3648-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 51" 1) CASTING - HOE KY-206 F/C (KY CBIA) 1) 36" x 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 34 1) Hole - 6					3400 lb 5270 lb 1654 lb 7780 lb 206 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 829.3' Rim to Invert: 7.53' Slack: 3.36" Sump: 0" Step Position:					Structure Total: 18310 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	821.77'	65°	28.75"	30" CMP	31"	Hole 34	34"	37.515"	-2"	8"
Invert 2	821.85'	0°	26"	30" CMP	31"	Hole 34	34"	34"	-1"	0"
Invert 3	825.27'	0°	26"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	41"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

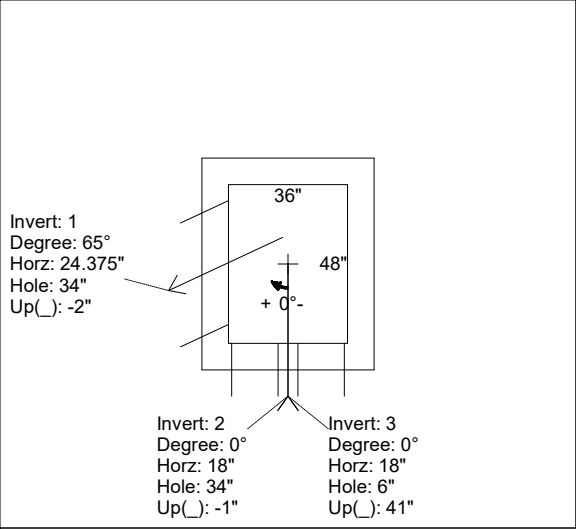


Invert: 1
Degree: 65°
Horz: 24.375"
Hole: 34"
Up(_): -2"

Invert: 2
Degree: 0°
Horz: 18"
Hole: 34"
Up(_): -1"

Invert: 3
Degree: 0°
Horz: 18"
Hole: 6"
Up(_): 41"

UPSIDE-DOWN VIEW (int. dimensions)

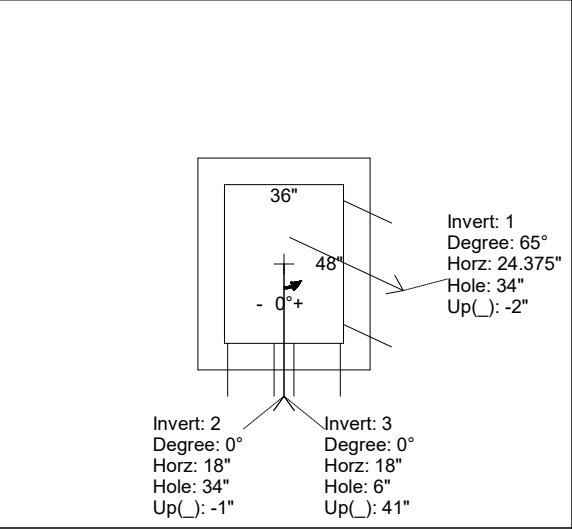

Invert: 1
Degree: 65°
Horz: 24.375"
Hole: 34"
Up(_): -2"

Invert: 2
Degree: 0°
Horz: 18"
Hole: 34"
Up(_): -1"

Invert: 3
Degree: 0°
Horz: 18"
Hole: 6"
Up(_): 41"


Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"


Height (Int): 51"
Height (Ext): 59"

Weight (Net): 7780 lb
Volume (Net): 1.99cu.yd

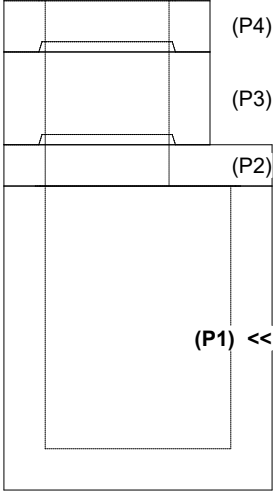

(P1) <<

INSIDE WALL DIMENSIONS

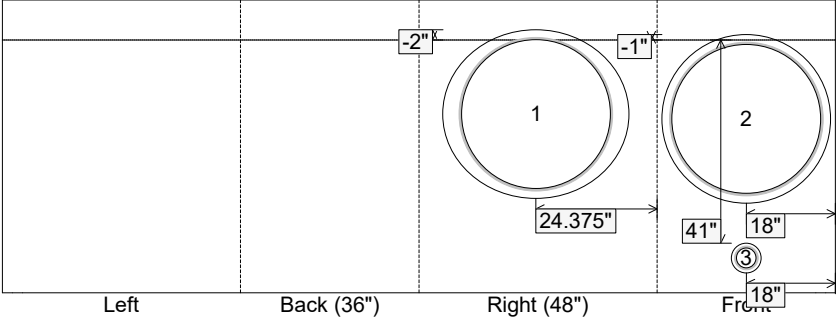

Left Back (36") Right (48") Front

EXT
