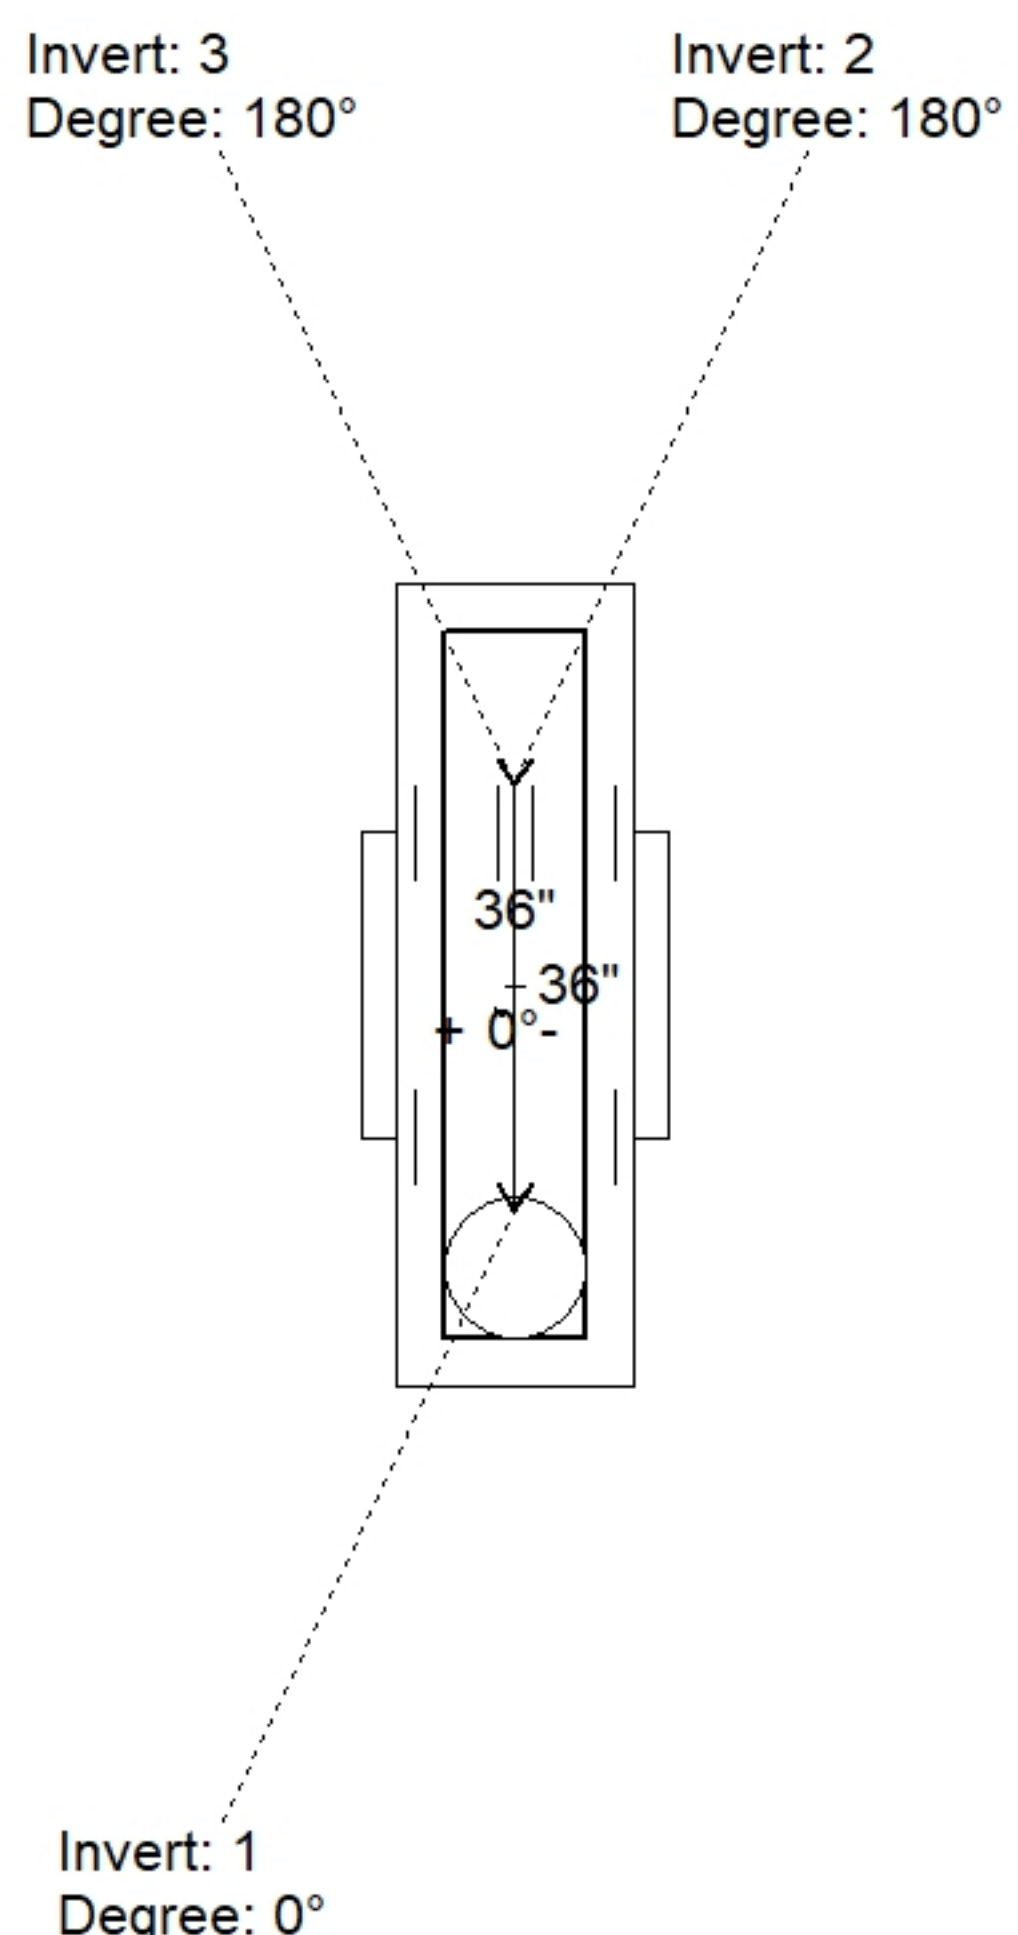
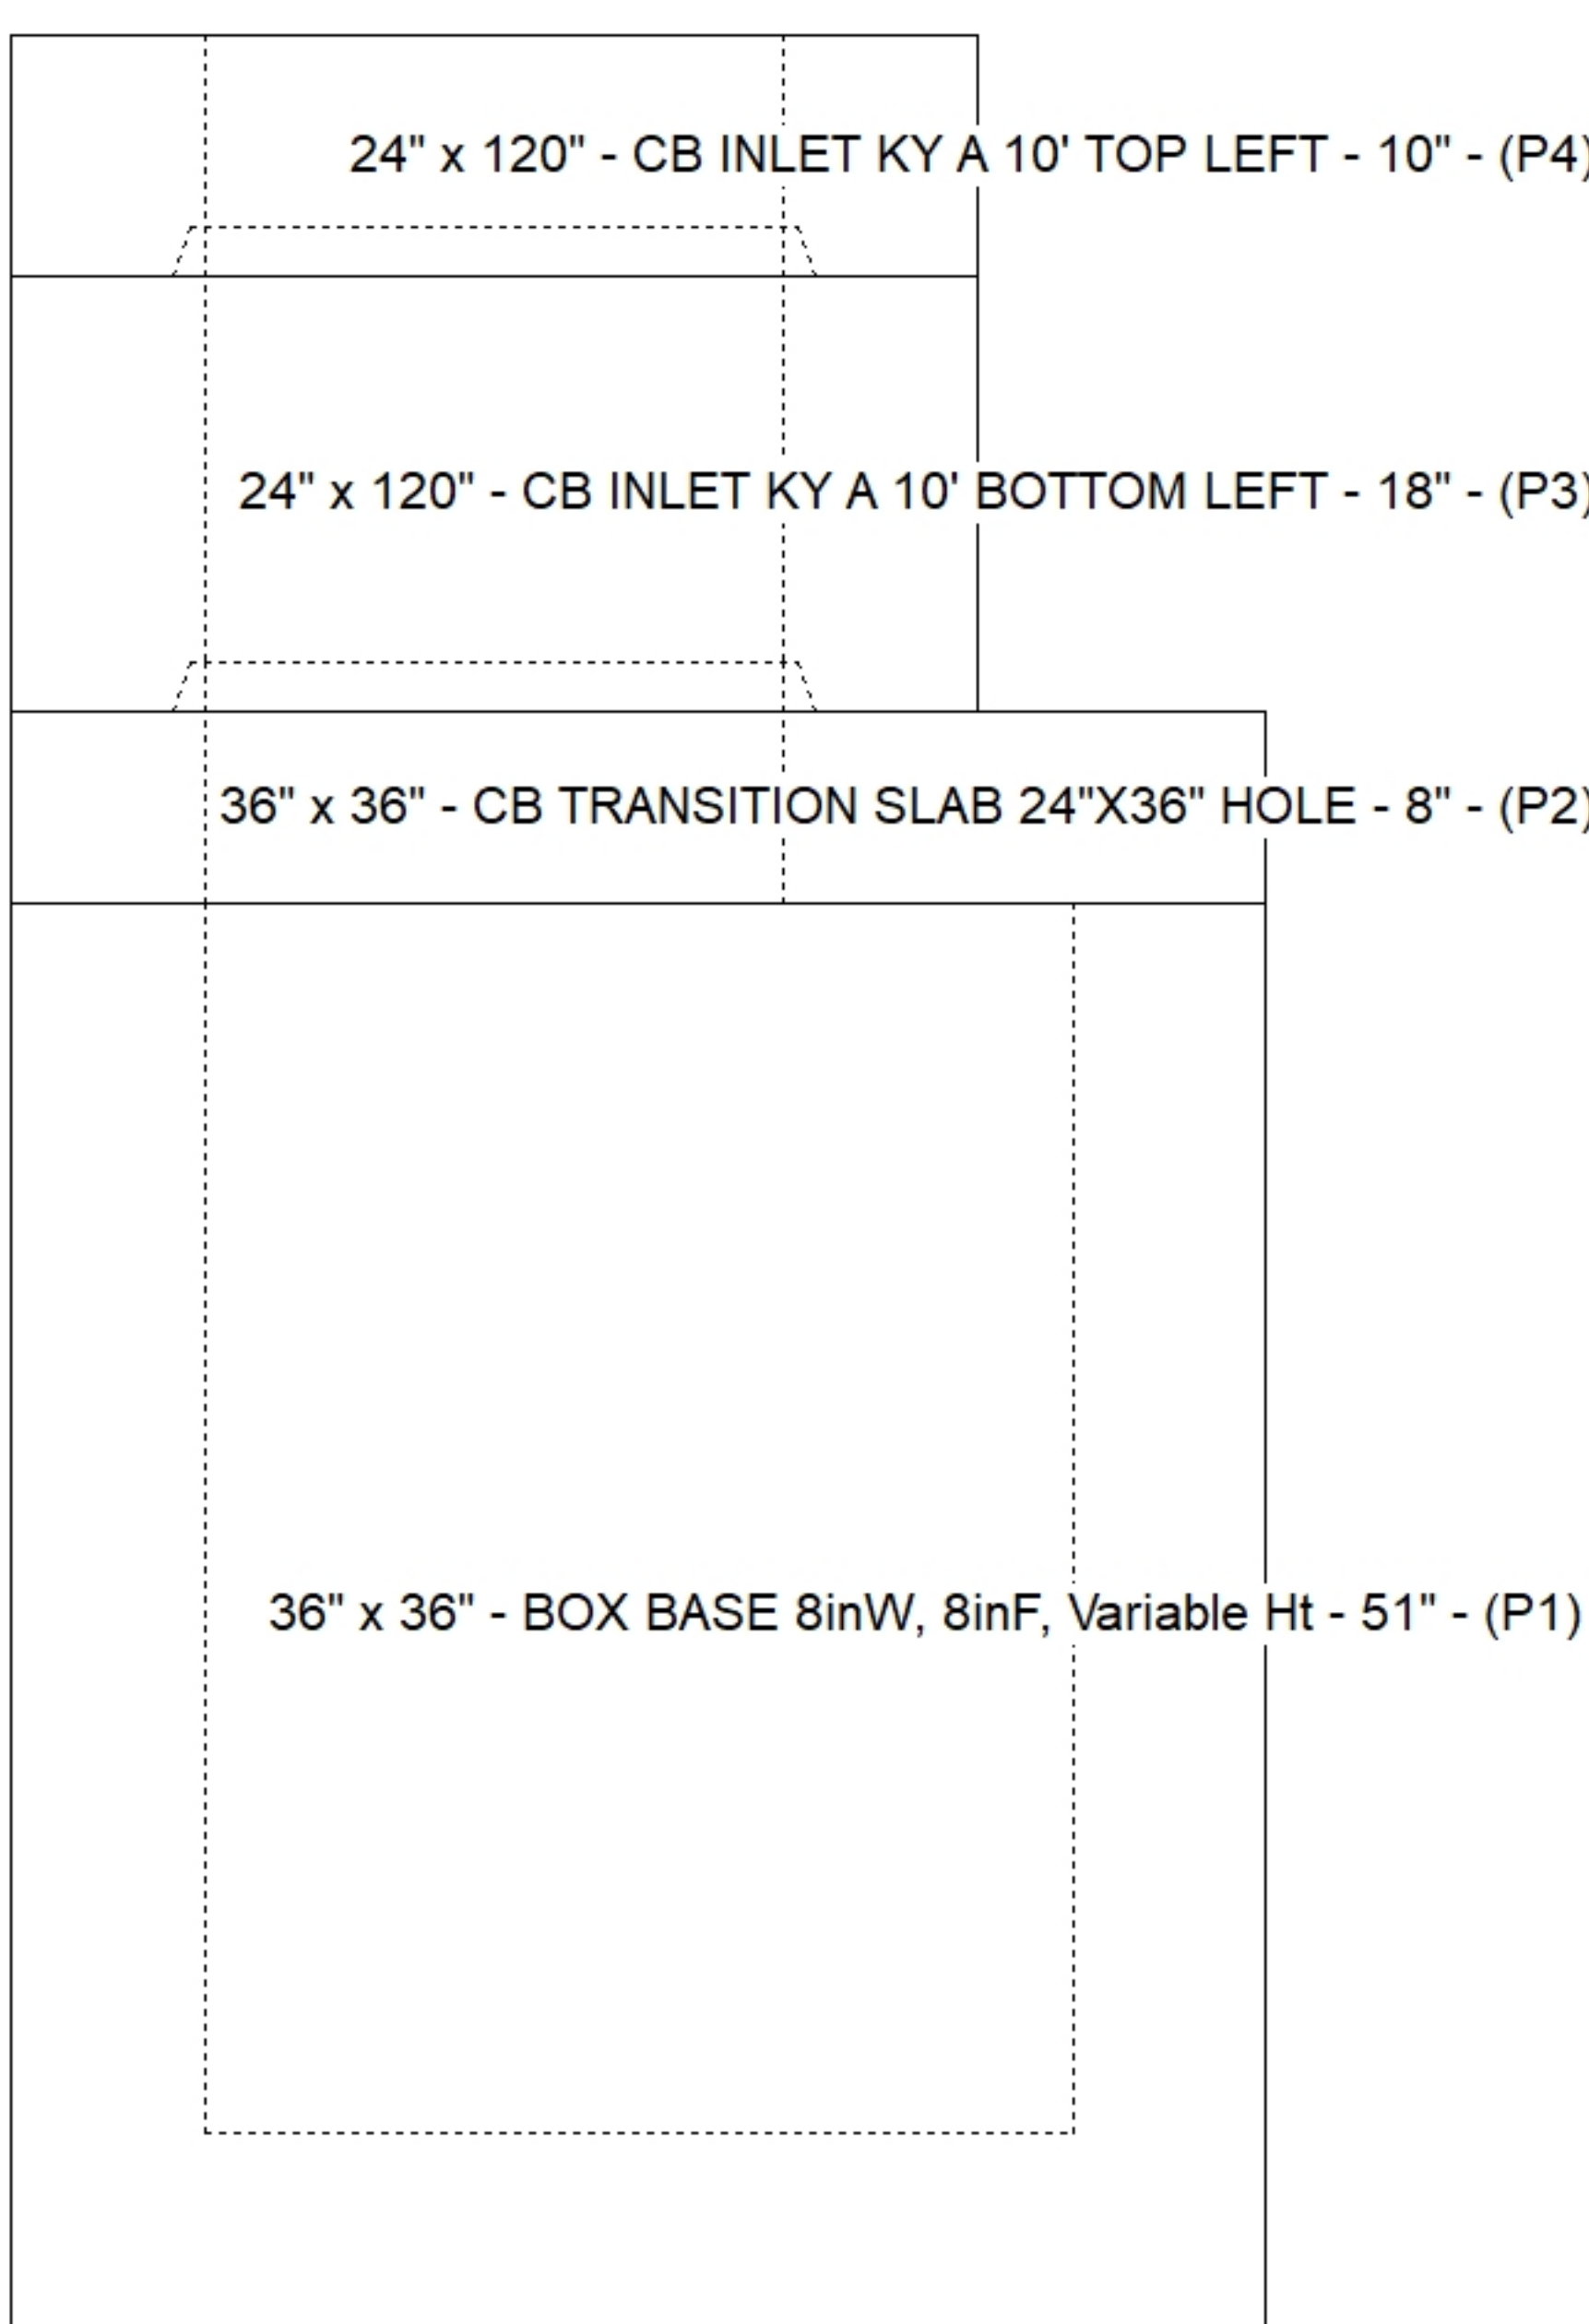
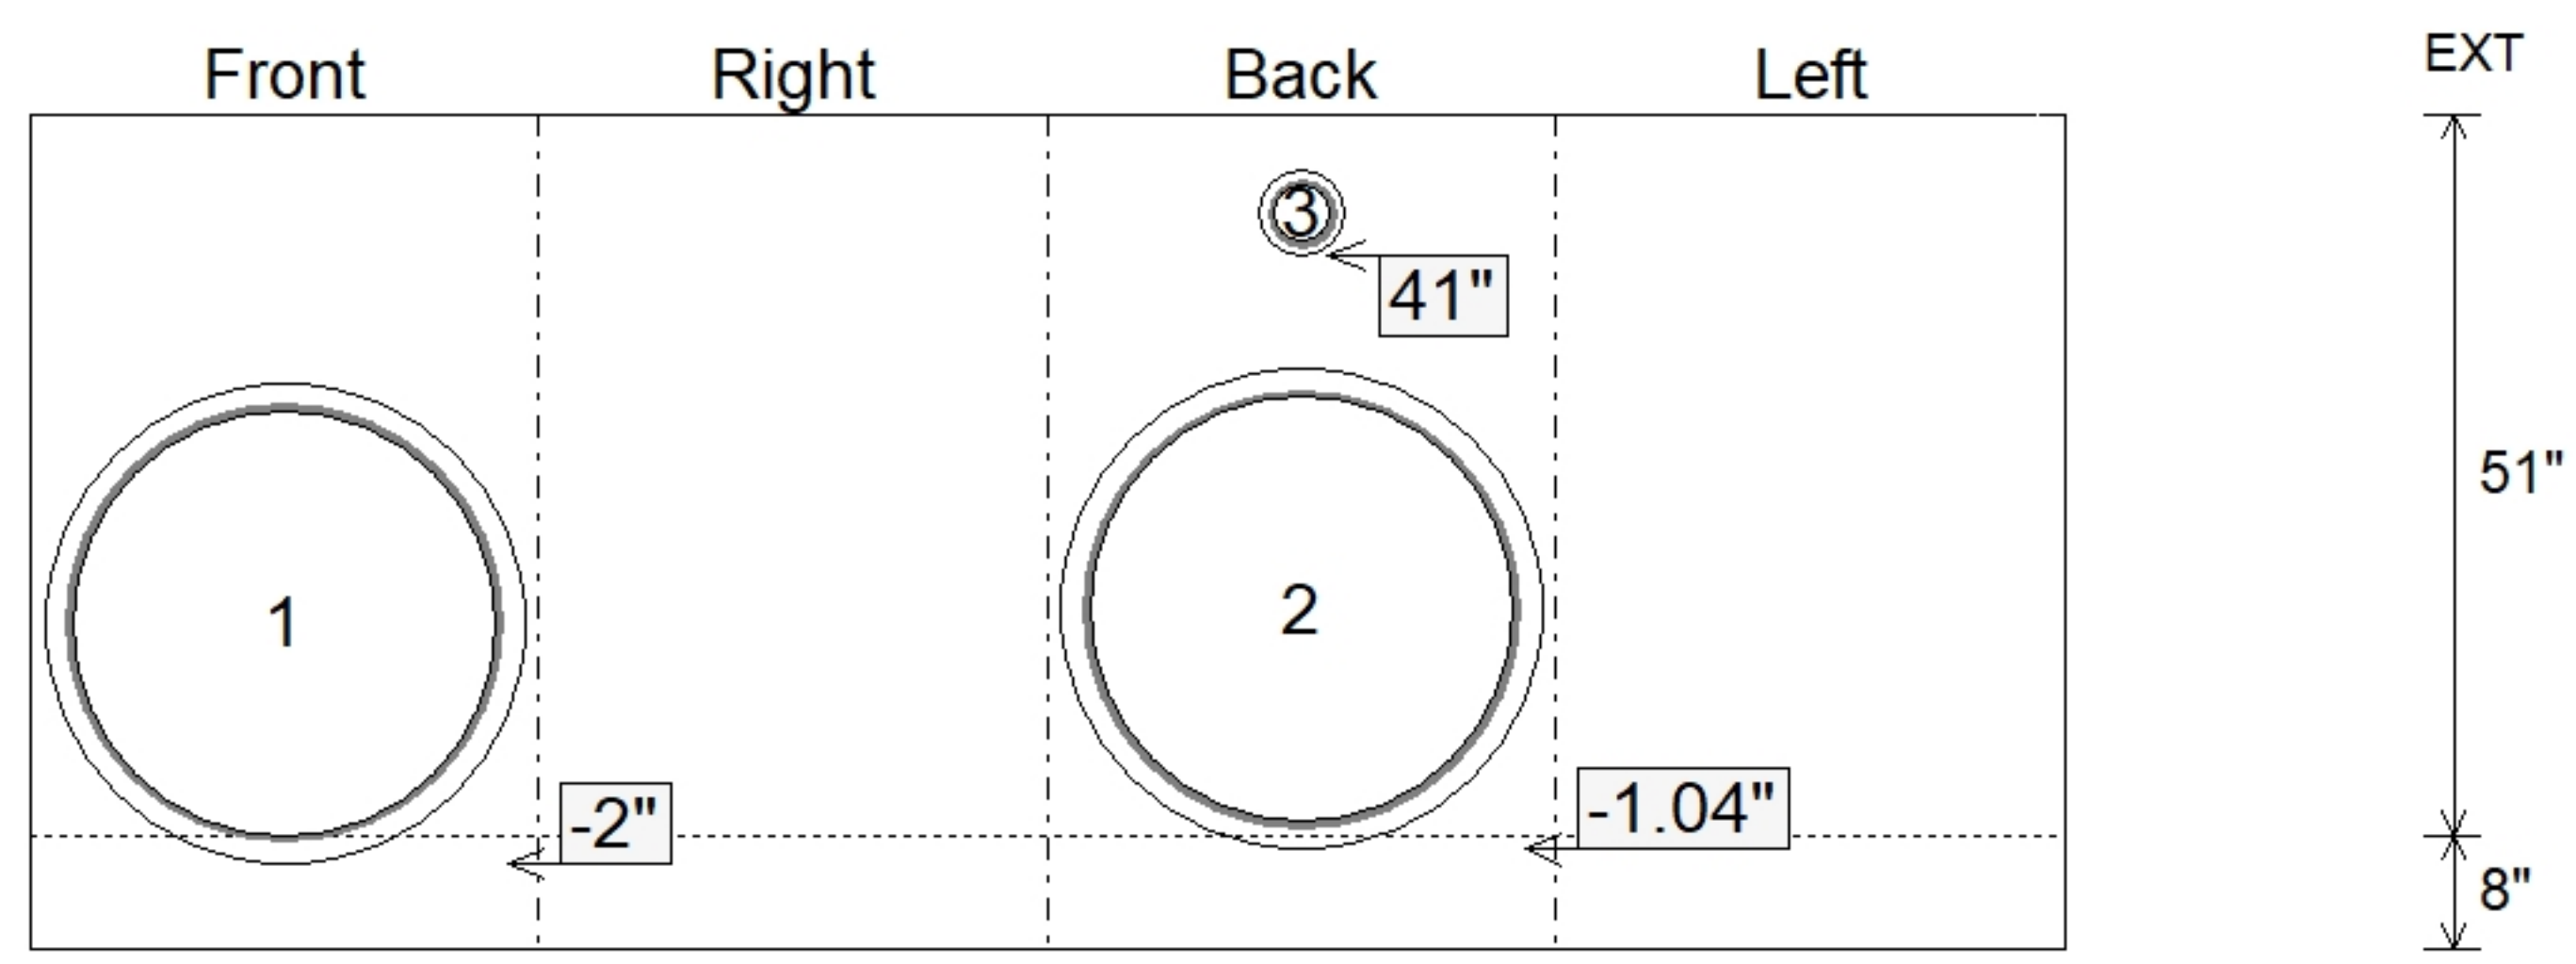


Job Name: 26-1635 - KYTC Oldham Co (261505) - P2 Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.				PC: T. Ryan TECH: Jared - F Plant: 100																																																																																																						
Structure ID: 16950-42 CBIA-36 Spec: KYTC Type: CBI TYPE A (10') Size: 36" x 36" Rim: 833.55' Invert: 826.04' Rim to Invert: 7.51' Sump: 0" Floor (Top): 826.04' Floor Height: 8" Floor (Bot): 825.373' Overall Height: 7.917' Slack: 3.12"																																																																																																										
Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				STRUCTURE SUMMARY: P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10" 3400 lb P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" 5270 lb P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8" 1235 lb P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 51" 6603 lb 1) CASTING - HOE KY-206 F/C (KY CBI A) 206 lb 1) 36" x 36" - Conseal CS-102 1.00" 0 lb 1) 24" x 36" - Conseal CS-102 1.00" 0 lb 2) Hole - 34 0 lb 1) Hole - 6 0 lb Structure Total: 16714 lb																																																																																																						
				<table><tr><th>Position</th><th>Elev</th><th>Angle</th><th>Pipe</th><th>Pipe OD</th><th>Hole</th><th>Connector</th><th>Up ()</th><th>Ref</th></tr><tr><td>Rim</td><td>833.55'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Reducer</td><td>830.29'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 1</td><td>826.04'</td><td>0°</td><td>30" CMP</td><td>31"</td><td>34"</td><td>Hole 34</td><td>-2"</td><td>P1</td></tr><tr><td>Invert 2</td><td>826.12'</td><td>180°</td><td>30" CMP</td><td>31"</td><td>34"</td><td>Hole 34</td><td>-1.04"</td><td>P1</td></tr><tr><td>Invert 3</td><td>829.54'</td><td>180°</td><td>4" HDPE (perf pipe)</td><td>4.8"</td><td>6"</td><td>Hole 6</td><td>41"</td><td>P1</td></tr><tr><td>Invert 4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 5</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 6</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 7</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 8</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr></table>				Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref	Rim	833.55'								Reducer	830.29'								Invert 1	826.04'	0°	30" CMP	31"	34"	Hole 34	-2"	P1	Invert 2	826.12'	180°	30" CMP	31"	34"	Hole 34	-1.04"	P1	Invert 3	829.54'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	41"	P1	Invert 4									Invert 5									Invert 6									Invert 7									Invert 8								
Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref																																																																																																		
Rim	833.55'																																																																																																									
Reducer	830.29'																																																																																																									
Invert 1	826.04'	0°	30" CMP	31"	34"	Hole 34	-2"	P1																																																																																																		
Invert 2	826.12'	180°	30" CMP	31"	34"	Hole 34	-1.04"	P1																																																																																																		
Invert 3	829.54'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	41"	P1																																																																																																		
Invert 4																																																																																																										
Invert 5																																																																																																										
Invert 6																																																																																																										
Invert 7																																																																																																										
Invert 8																																																																																																										
				Default - Interior Dimensions 																																																																																																						
Submittal Drawing 7/28/2026 3:11:03 PM				SUBMITTAL APPROVED BY:																																																																																																						
