



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:39:19 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 13829-126 DBI4 - 1A											
P1 BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht T/n									
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW F/G - 30" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht T/n - 53" 2) 36" x 48" - Conseal CS-102 1.00" 2) Hole - 34						0 lb 4028 lb 8131 lb 0 lb 0 lb ----- 0 lb Structure Total: 12159 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 4 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY OTHERS (HOE KY-410 (DBI4)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 754.48' Rim to Invert: 7.64' Slack: 0.68" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	746.84'	90°	32"	30" CMP	31"	Hole 34	34"	34"	-2"	0"	
Invert 2	746.92'	270°	32"	30" CMP	31"	Hole 34	34"	34"	-1"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

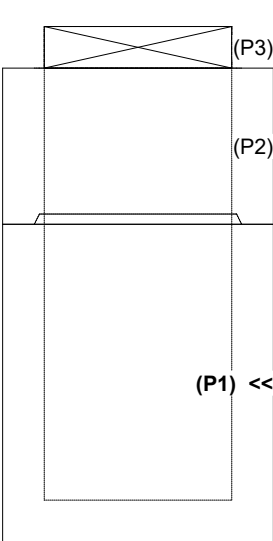

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

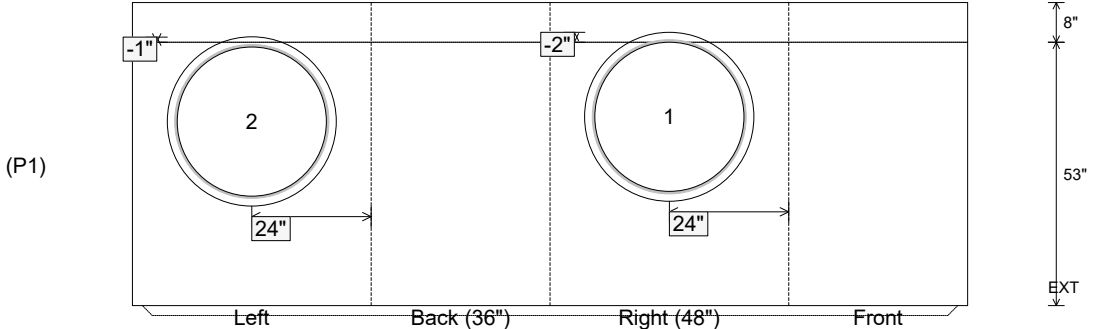

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 53" Height (Ext): 61"	Weight (Net): 8131 lb Volume (Net): 2.08cu.yd
----------------------------------	---------------------------------	--	--	--
