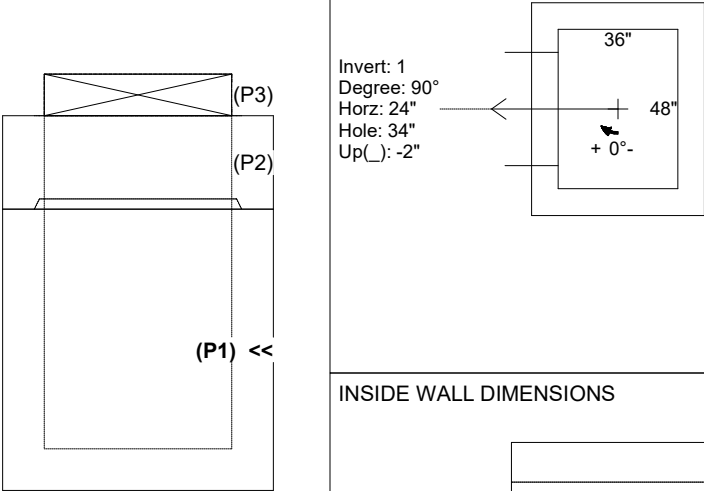

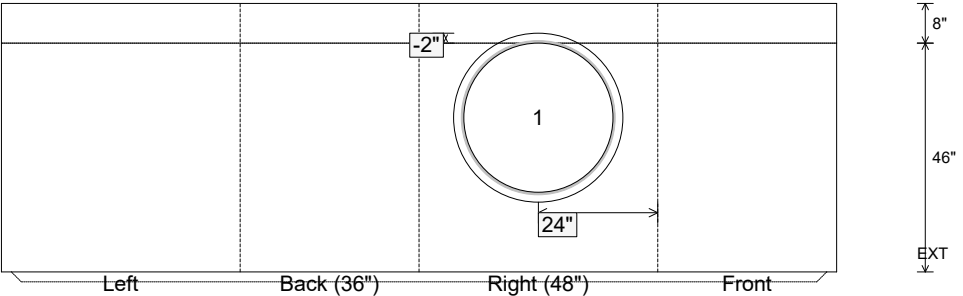


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:39:21 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 17100-129 DBI4 - 37A											
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW F/G - 18" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht T/n - 46" 2) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 34						0 lb 2417 lb 7801 lb 0 lb 0 lb ----- 0 lb Structure Total: 10217 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 4 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY OTHERS (HOE KY-410 (DBI4)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 839.97'		Rim to Invert: 6'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	833.97'	90°	32"	30" CMP	31"	Hole 34	34"	34"	-2"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 46" Height (Ext): 54"		Weight (Net): 7801 lb Volume (Net): 1.99cu.yd		
