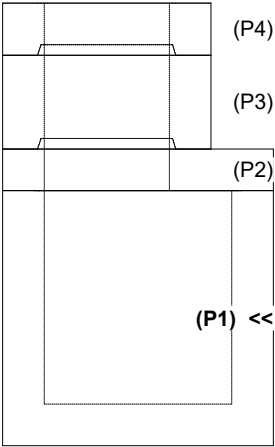
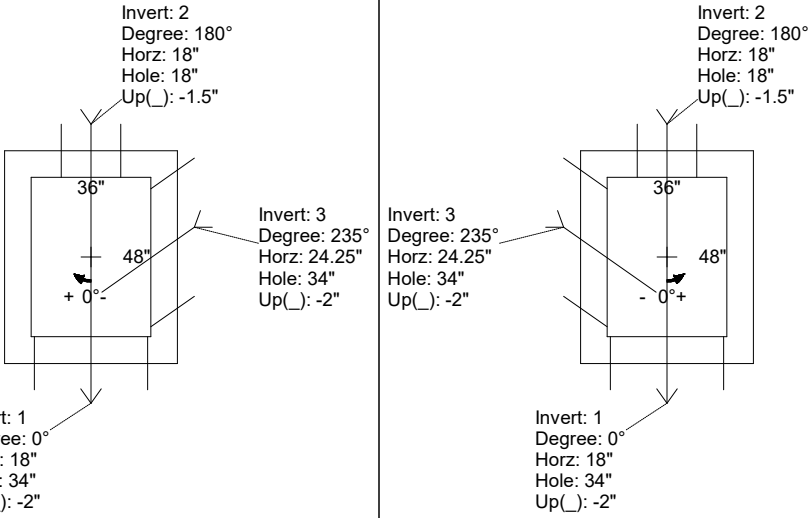
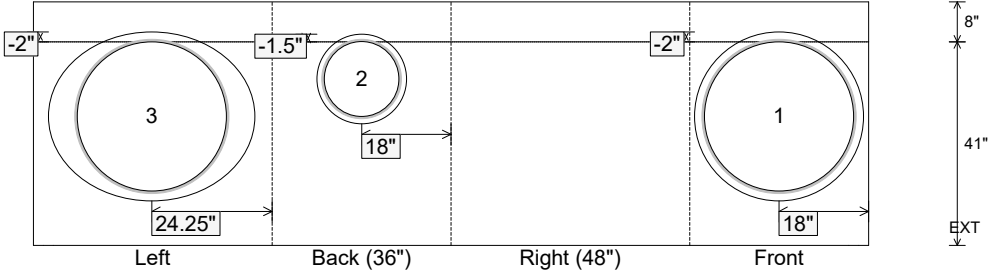


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:29:03 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 35475-57 CBIA											
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 41" 1) CASTING - HOE KY-206 F/C (KY CBIA) 1) 36" x 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 34 1) Hole - 18						3400 lb 5270 lb 1654 lb 6214 lb 206 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 16744 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 789.96' Rim to Invert: 6.67' Slack: 3.04" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	783.29'	0°	26"	30" CMP	31"	Hole 34	34"	34"	-2"	0"	
Invert 2	783.29'	180°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 3	783.29'	235°	26.625"	30" CMP	31"	Hole 34	34"	41.506"	-2"	10.5"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimensions)					
											
INSIDE WALL DIMENSIONS											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 41" Height (Ext): 49"		Weight (Net): 6214 lb Volume (Net): 1.59cu.yd		
