


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:29:03 AM		Tech: Jared - F PC: T. Ryan			
Structure ID: 35531-58 CBIA										
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n						
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 41" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22					3398 lb 5270 lb 5247 lb 206 lb 0 lb 0 lb ----- Structure Total: 14120 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 791.32' Rim to Invert: 6.07' Slack: 3.84" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	785.25'	50°	19.625"	18" CMP	19"	Hole 22	22"	28.719"	-2"	8"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

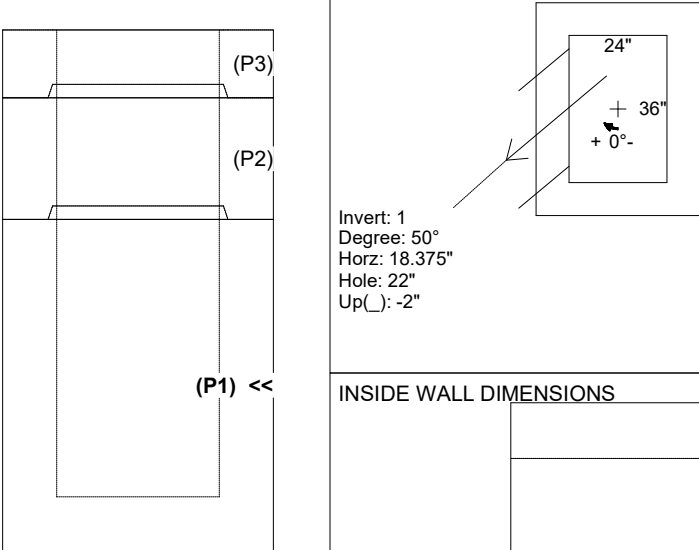

Invert: 1
Degree: 50°
Horz: 18.375"
Hole: 22"
Up(_): -2"


(P1) <<

UPSIDE-DOWN VIEW (int. dimenions)

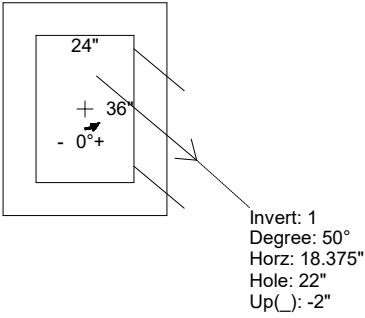

Invert: 1
Degree: 50°
Horz: 18.375"
Hole: 22"
Up(_): -2"

INSIDE WALL DIMENSIONS

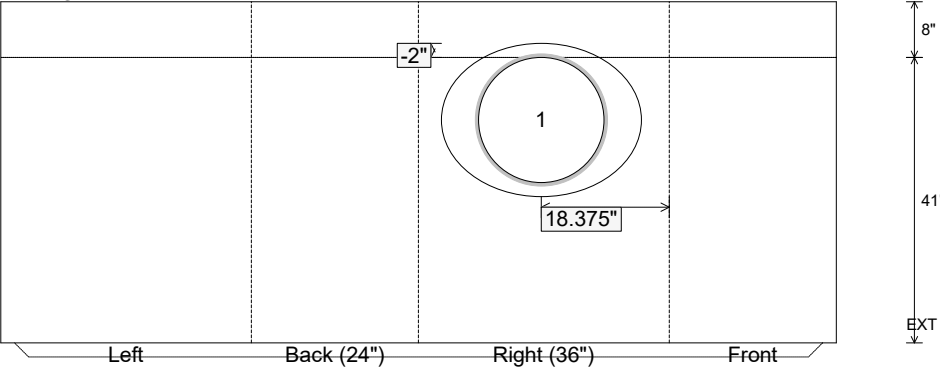

(P1)

Left Back (24") Right (36") Front

8"

41"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 41" Height (Ext): 49"	Weight (Net): 5247 lb Volume (Net): 1.34cu.yd
----------------------------------	---------------------------------	--	--	--
