

Job Name: 26-1635 - KYTC Oldham Co (261505)

Job Location: Peewee Valley, KY

Contractor: Cleary Construction, Inc.

Plant: 100

7/27/2026 11:36:25 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: 36310-110 DBI3

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"

P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 34"

1) 36" x 36" - Conseal CS-102 1.00"

1) Hole - 18

0 lb

5661 lb

0 lb

0 lb

Structure Total: 5661 lb

Structure Notes:

KYTC STATE PROJECT

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C).

4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 808.67'

Rim to Invert: 3.5'

Slack: 0"


Sump: 0"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	805.17'	0°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

#5 DOWELS @ 12" O.C. STUBBED 20" OUT THE TOP OF THE WALLS

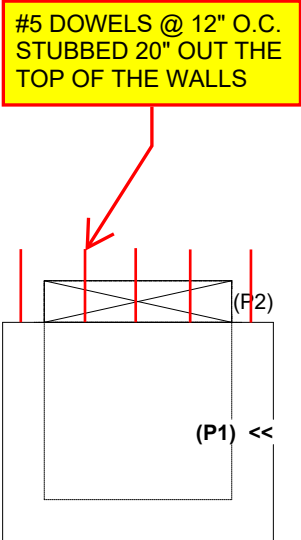

Invert: 1


Degree: 0°

Horz: 18"

Hole: 18"

Up(_): -1.5"

UPSIDE-DOWN VIEW (int. dimensions)



Invert: 1


Degree: 0°

Horz: 18"

Hole: 18"

Up(_): -1.5"

INSIDE WALL DIMENSIONS

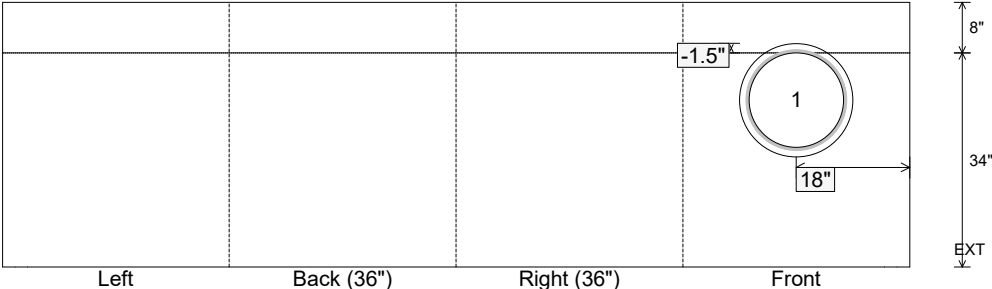

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 34"

Height (Ext): 42"

Weight (Net): 5661 lb

Volume (Net): 1.45cu.yd
