

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Peewee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

7/27/2026 11:36:26 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: 38900-113 DBI3

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28"
1) 36" x 36" - Conseal CS-102 1.00"
2) Hole - 22"

Structure Total: 4613 lb

Structure Notes:

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C).
4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




Rim: 776.85' Rim to Invert: 3' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	773.85'	0°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	773.85'	270°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

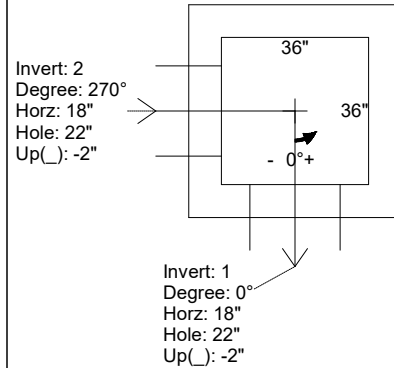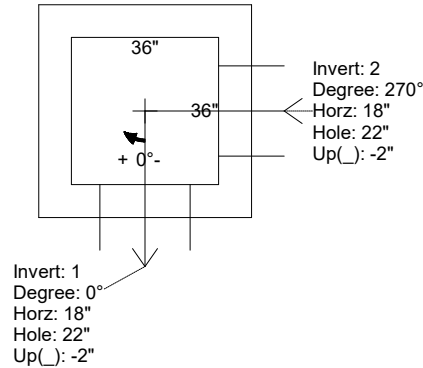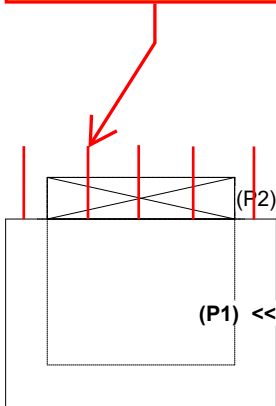

INSIDE WALL DIMENSIONS

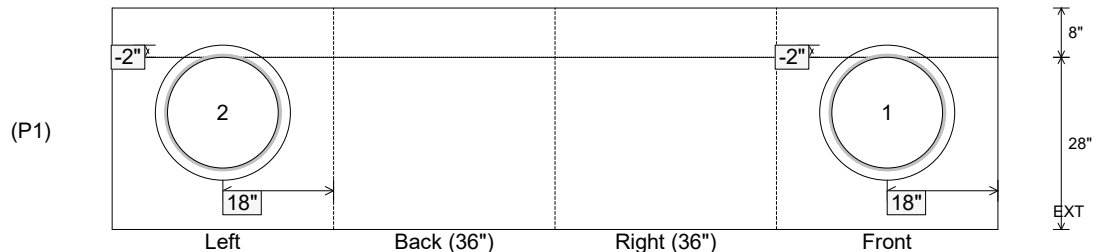

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 28"
Height (Ext): 36"

Weight (Net): 4613 lb
Volume (Net): 1.18cu.yd
