




Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 1:46:15 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 48325-70 CBIA											
P1 BX2436-08BA42 BOX BASE 8inW, 8inF T/n											
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 42" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 18						3398 lb 5270 lb 5253 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 14127 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 821.46' Rim to Invert: 6.17' Slack: 4.04" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	815.29'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	815.29'	170°	18.5"	15" CMP	16"	Hole 18	18"	18.278"	-1.5"	3"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

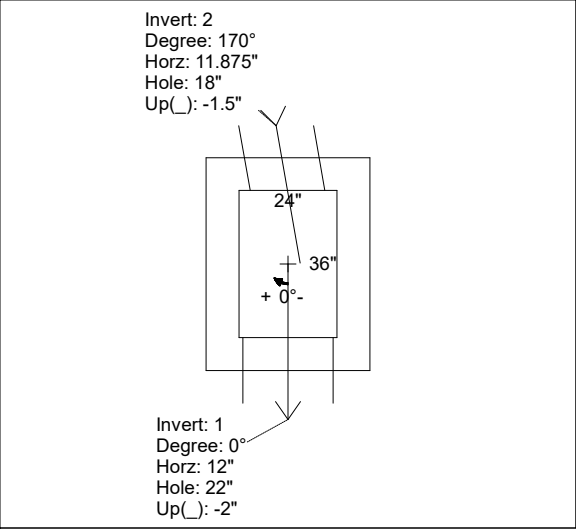

RIGHT-SIDE UP VIEW (int. dimensions)

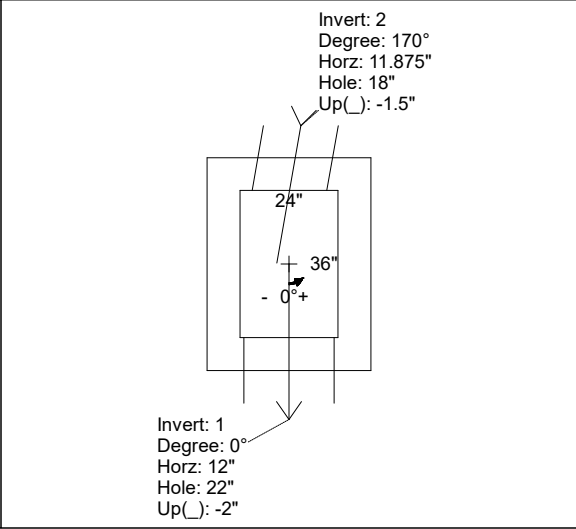

UPSIDE-DOWN VIEW (int. dimensions)

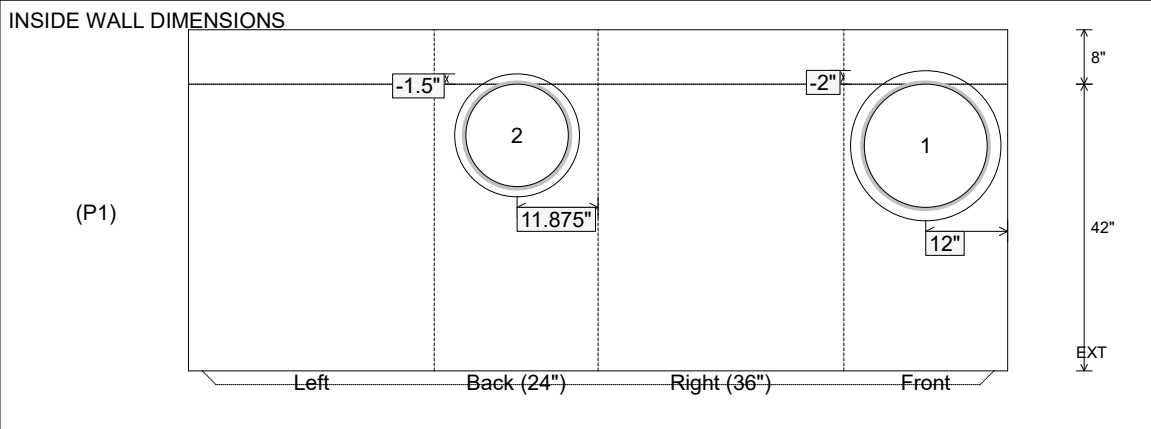

INSIDE WALL DIMENSIONS

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 42"
Height (Ext): 50"

Weight (Net): 5253 lb
Volume (Net): 1.34cu.yd
