



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 1:46:16 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 48540-72 CBIA											
P1		BX2436-08BA48		BOX BASE 8inW, 8inF T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 48" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22 1) Hole - 18					3398 lb 5270 lb 5613 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 14487 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 820.79' Rim to Invert: 6.54' Slack: 2.48" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	814.25'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	815.41'	90°	26"	15" CMP	16"	Hole 18	18"	18"	12.375"	0"	
Invert 3	814.25'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

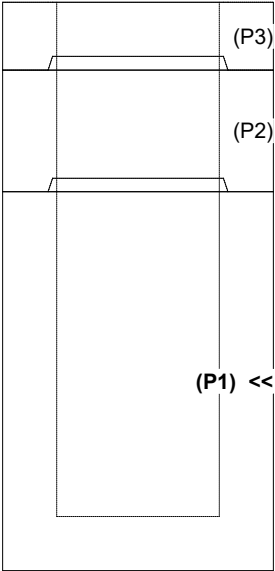

UPSIDE-DOWN VIEW (int. dimensions)

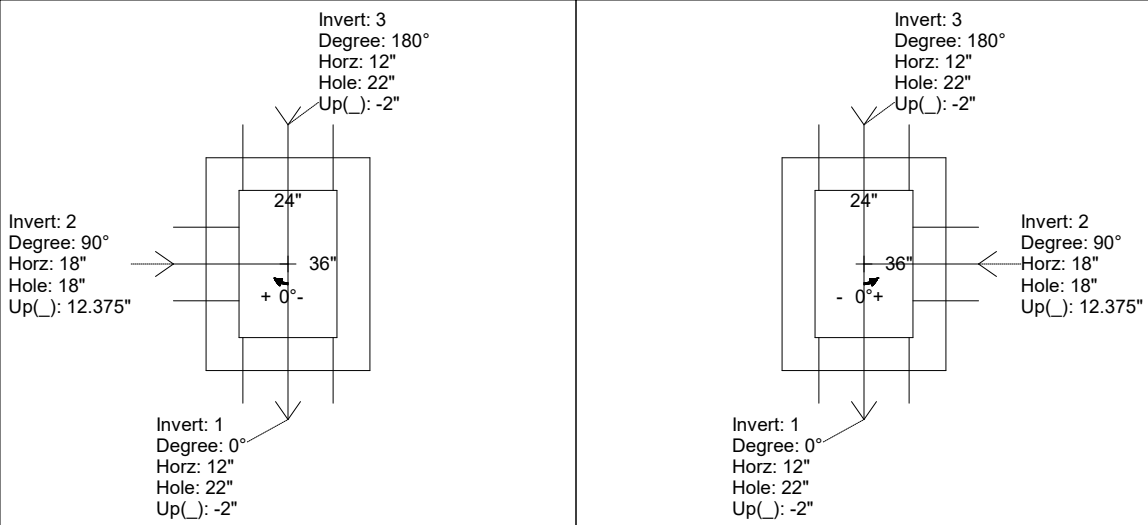

INSIDE WALL DIMENSIONS

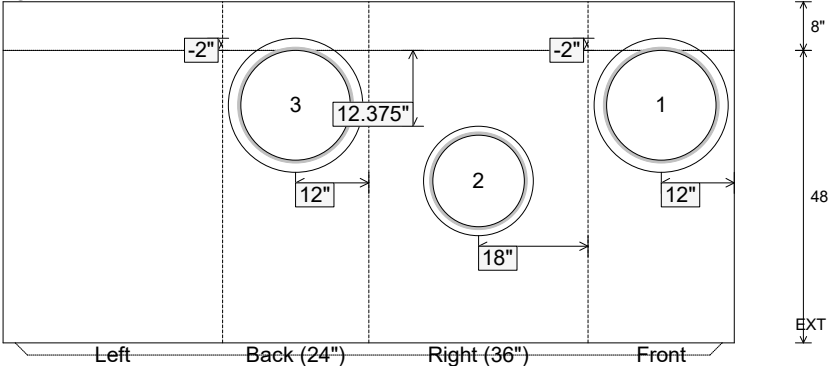

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 5613 lb Volume (Net): 1.43cu.yd
----------------------------------	---------------------------------	--	--	--
