

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 48"

Rim to Invert: 5.37'

Floor Height: 8"

Slack: 0.44"

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 4 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
4. CASTING SUPPLIED BY OTHERS (HOE KY-410 (DBI4)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:



P2) 36" x 48" - P.I.P. - BY OTHERS - 8'

P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 56"

- 1) 36" x 48" - Conseal CS-102 1.00"
- 2) Hole - 40


0 lb
8276 lb
0 lb
0 lb

Structure Total: 8276 lb

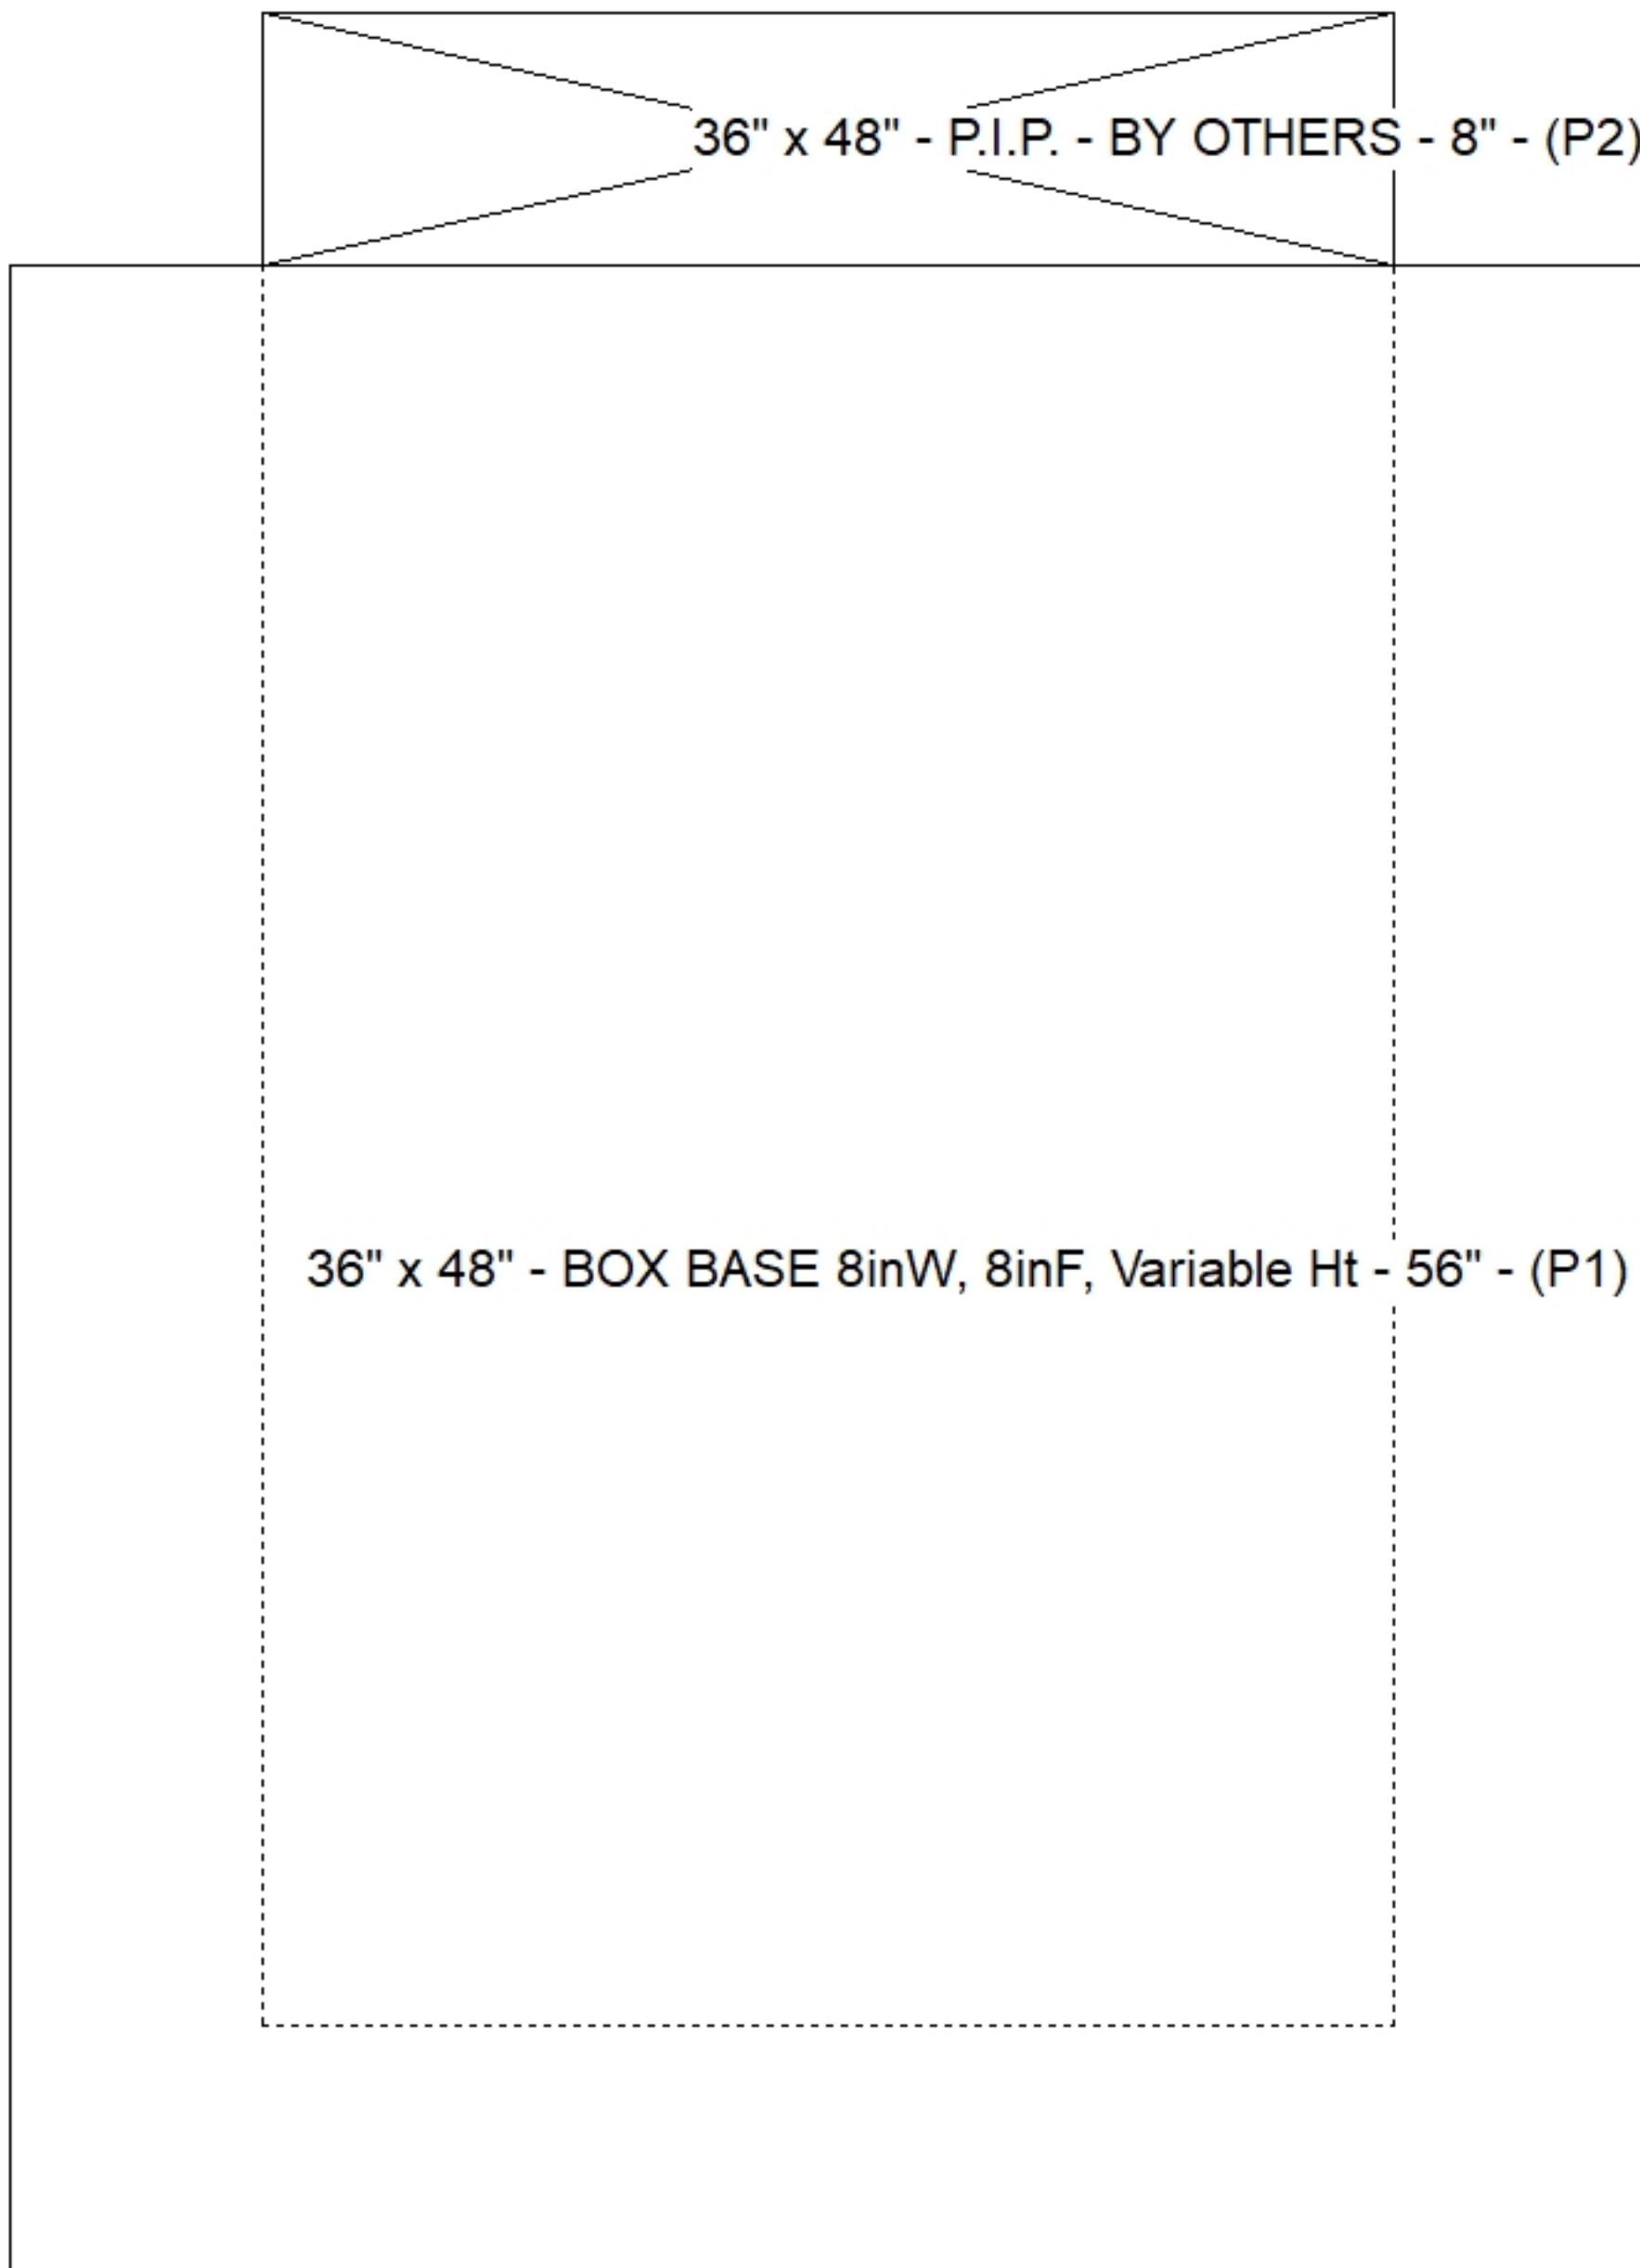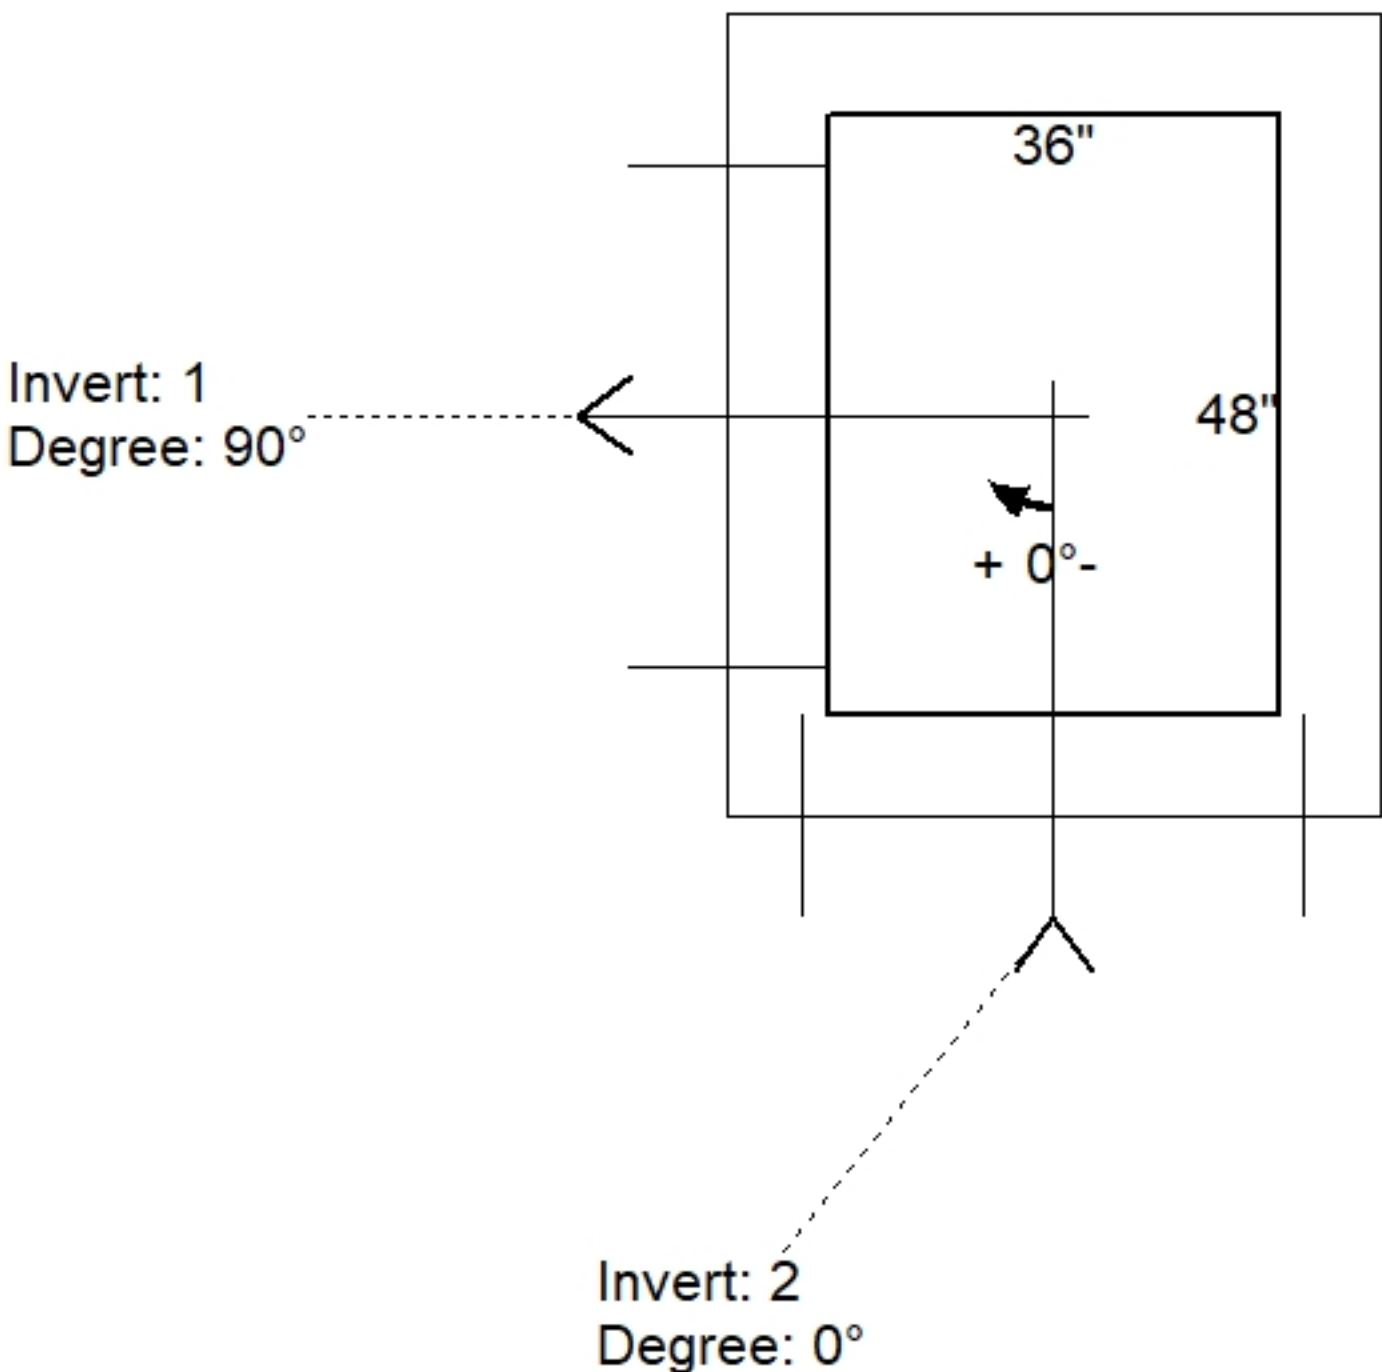

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	751.47'							
Reducer								
Invert 1	746.1'	90°	36" CMP	37"	40"	Hole 40	-2"	P1
Invert 2	746.18'	0°	36" CMP	37"	40"	Hole 40	-1.04"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

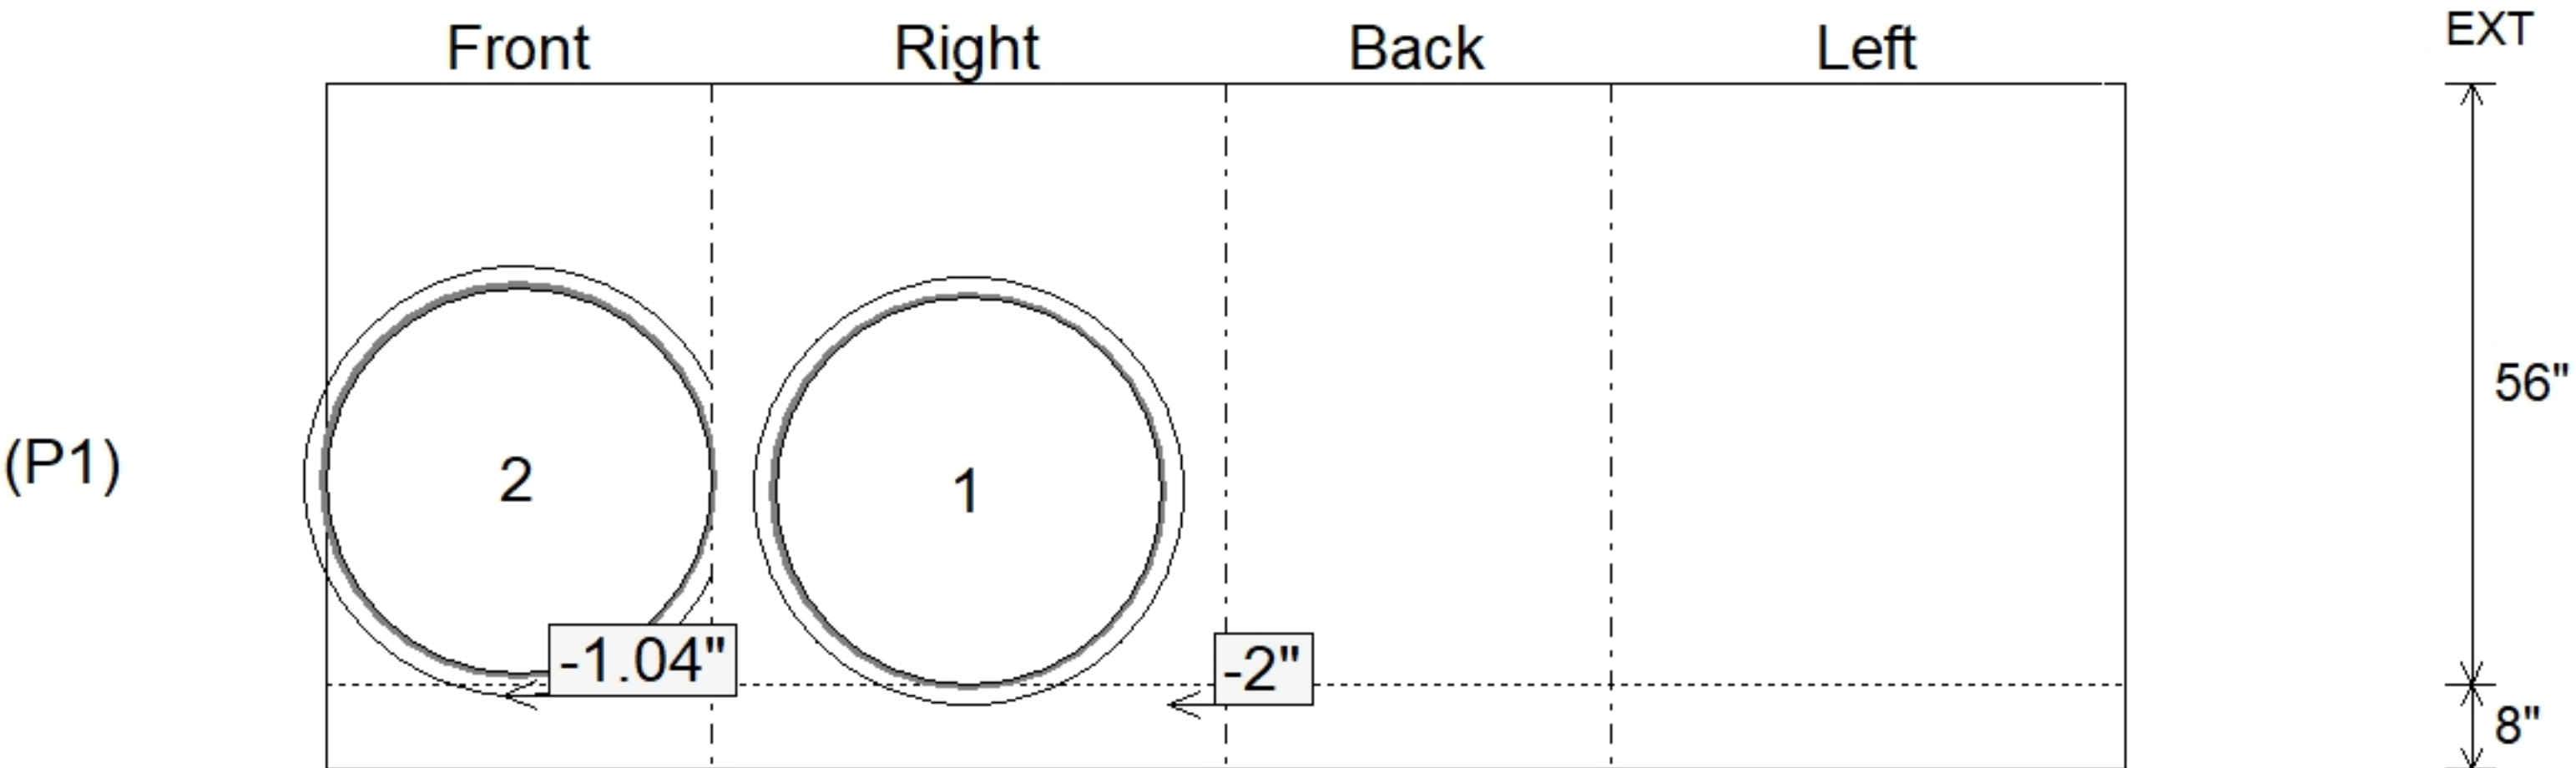

Submittal Drawing
7/29/2026 12:08:56 PM

SUBMITTAL
APPROVED BY:
