

**Contractor: Cleary Construction, Inc.**

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 6.07'


Floor Height: 8"

Slack: 2.84"


REINFORCING PER ASTM A615 (GRADE 60).  
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.  
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.  
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

-----  
12400 H-


Structure Total: 13480 lb

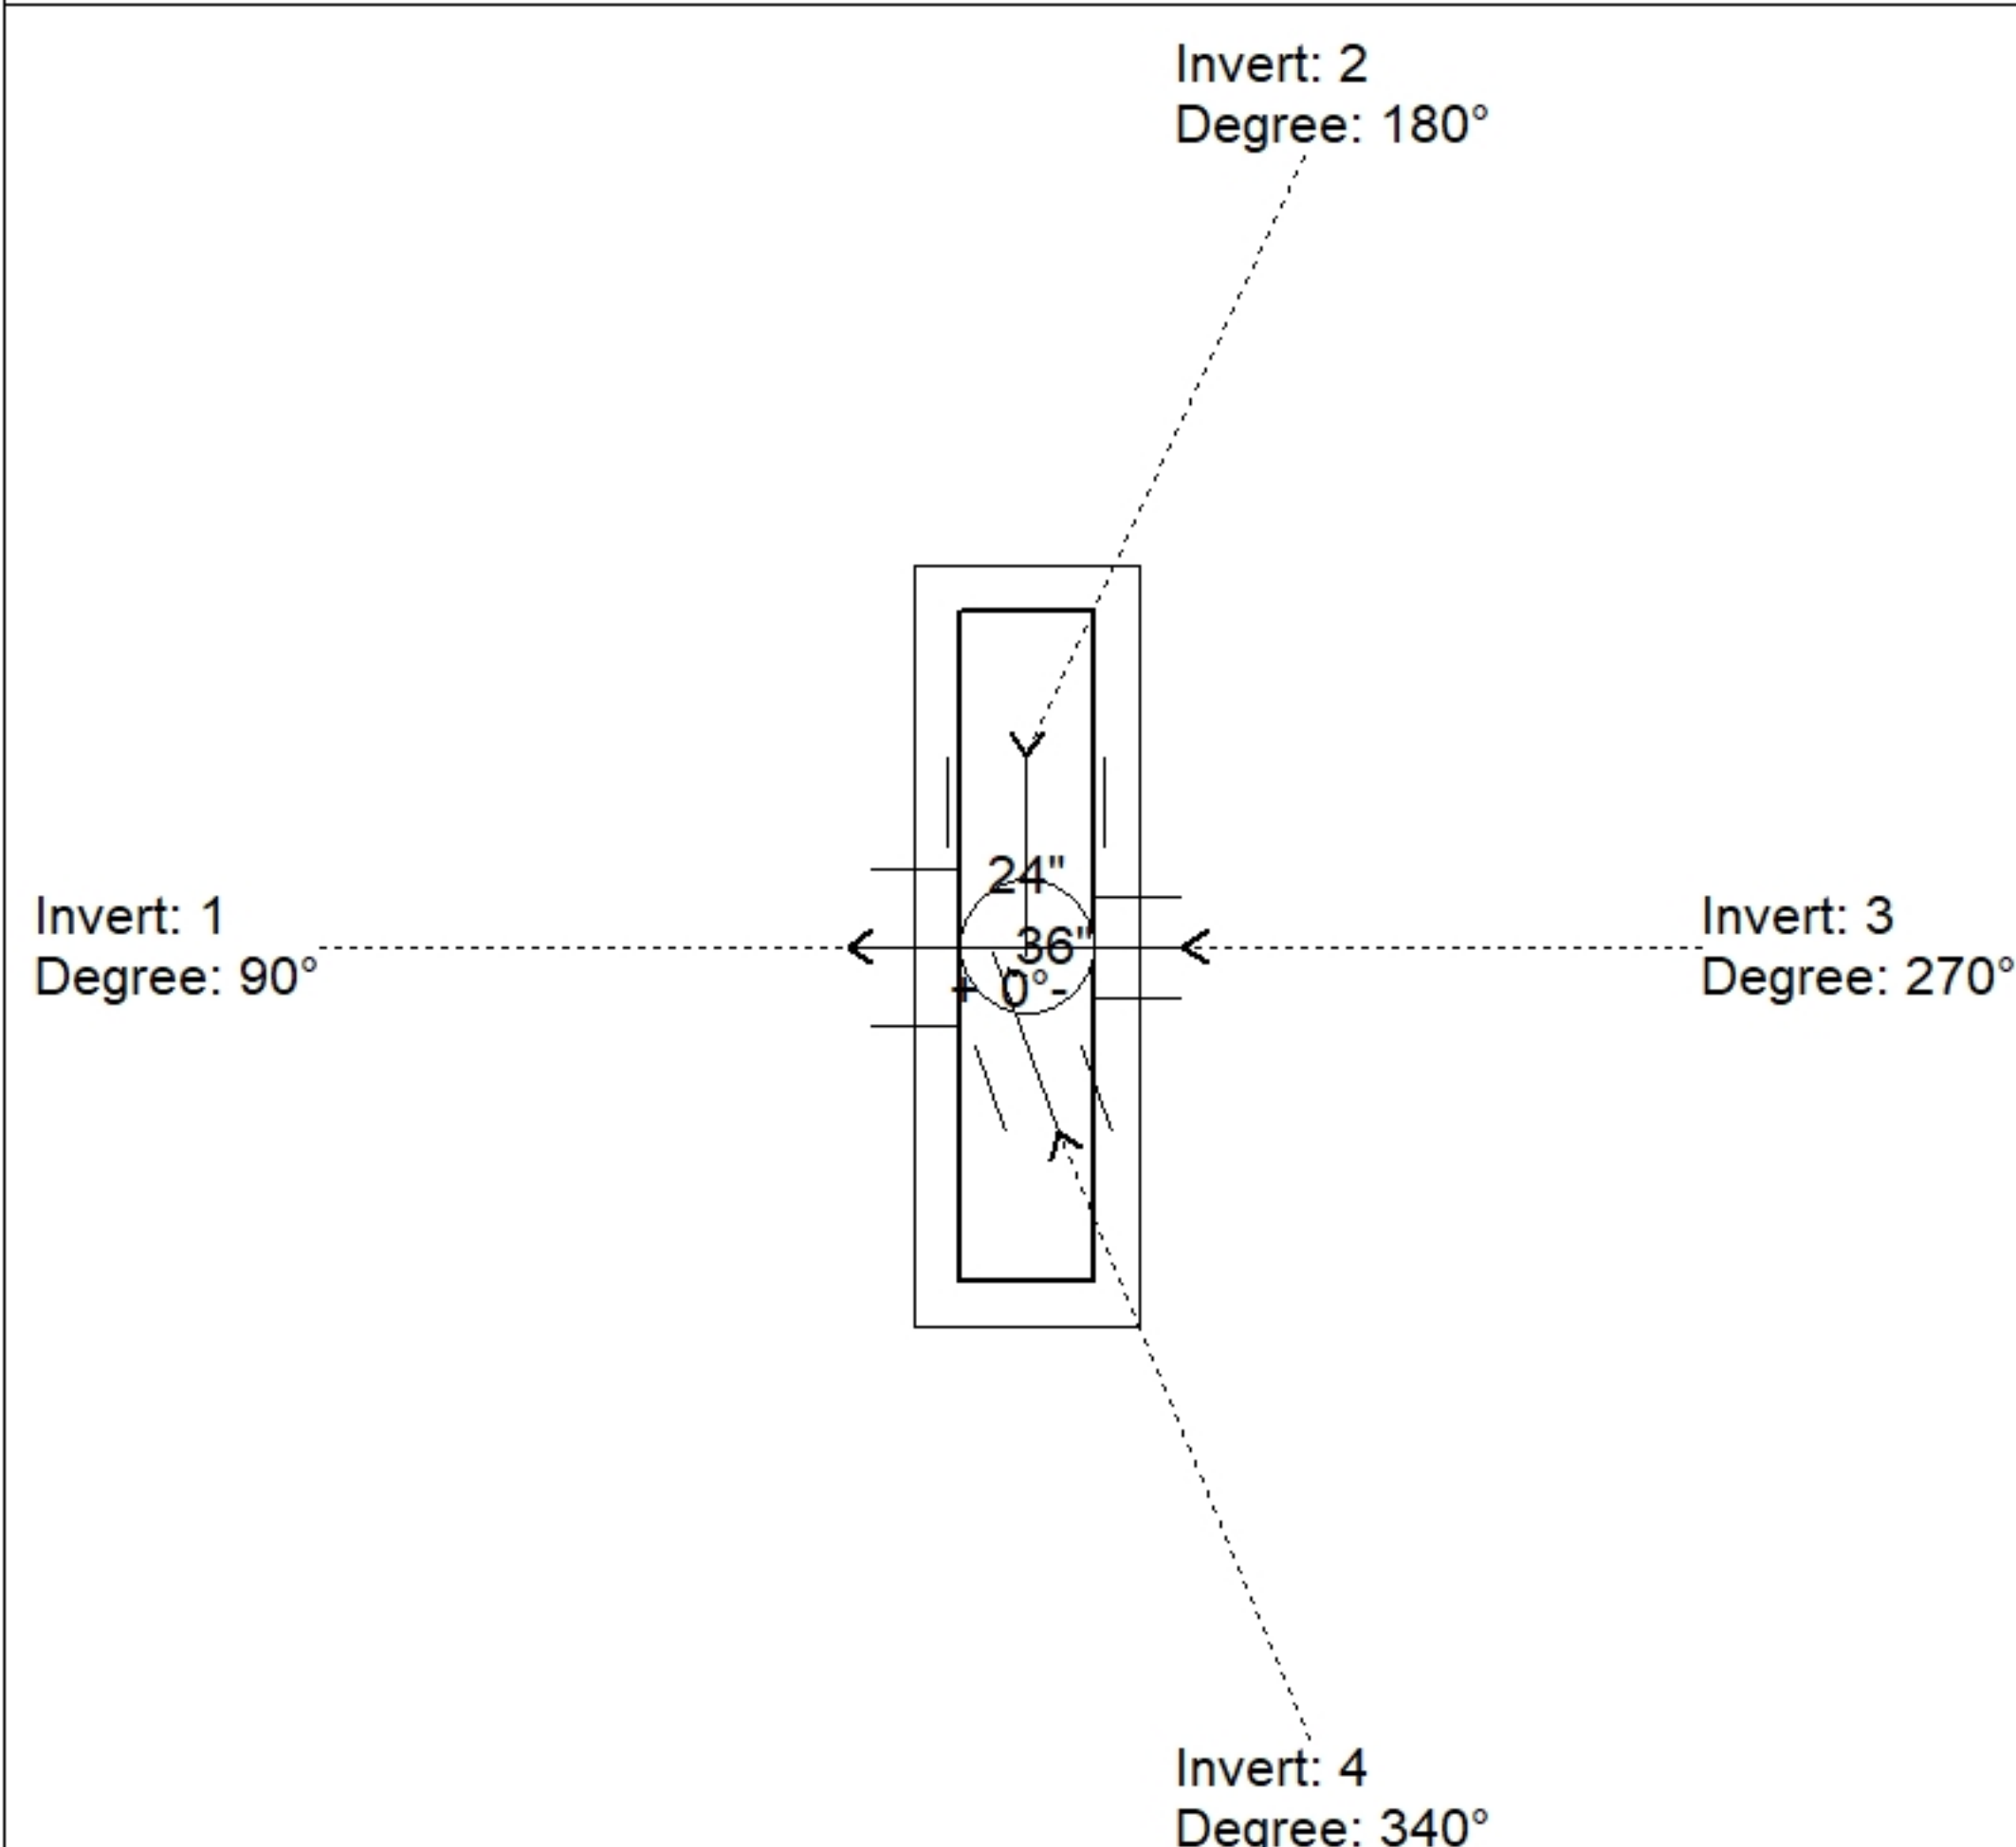

| Position | Elev    | Angle | Pipe    | Pipe OD | Hole | Connector | Up (↓) | Ref |
|----------|---------|-------|---------|---------|------|-----------|--------|-----|
| Rim      | 800.64' |       |         |         |      |           |        |     |
| Reducer  |         |       |         |         |      |           |        |     |
| Invert 1 | 794.57' | 90°   | 24" CMP | 25"     | 28"  | Hole 28   | -2"    | P1  |
| Invert 2 | 794.57' | 180°  | 24" CMP | 25"     | 28"  | Hole 28   | -2"    | P1  |
| Invert 3 | 794.57' | 270°  | 15" CMP | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 4 | 794.57' | 340°  | 15" CMP | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 5 |         |       |         |         |      |           |        |     |
| Invert 6 |         |       |         |         |      |           |        |     |
| Invert 7 |         |       |         |         |      |           |        |     |
| Invert 8 |         |       |         |         |      |           |        |     |

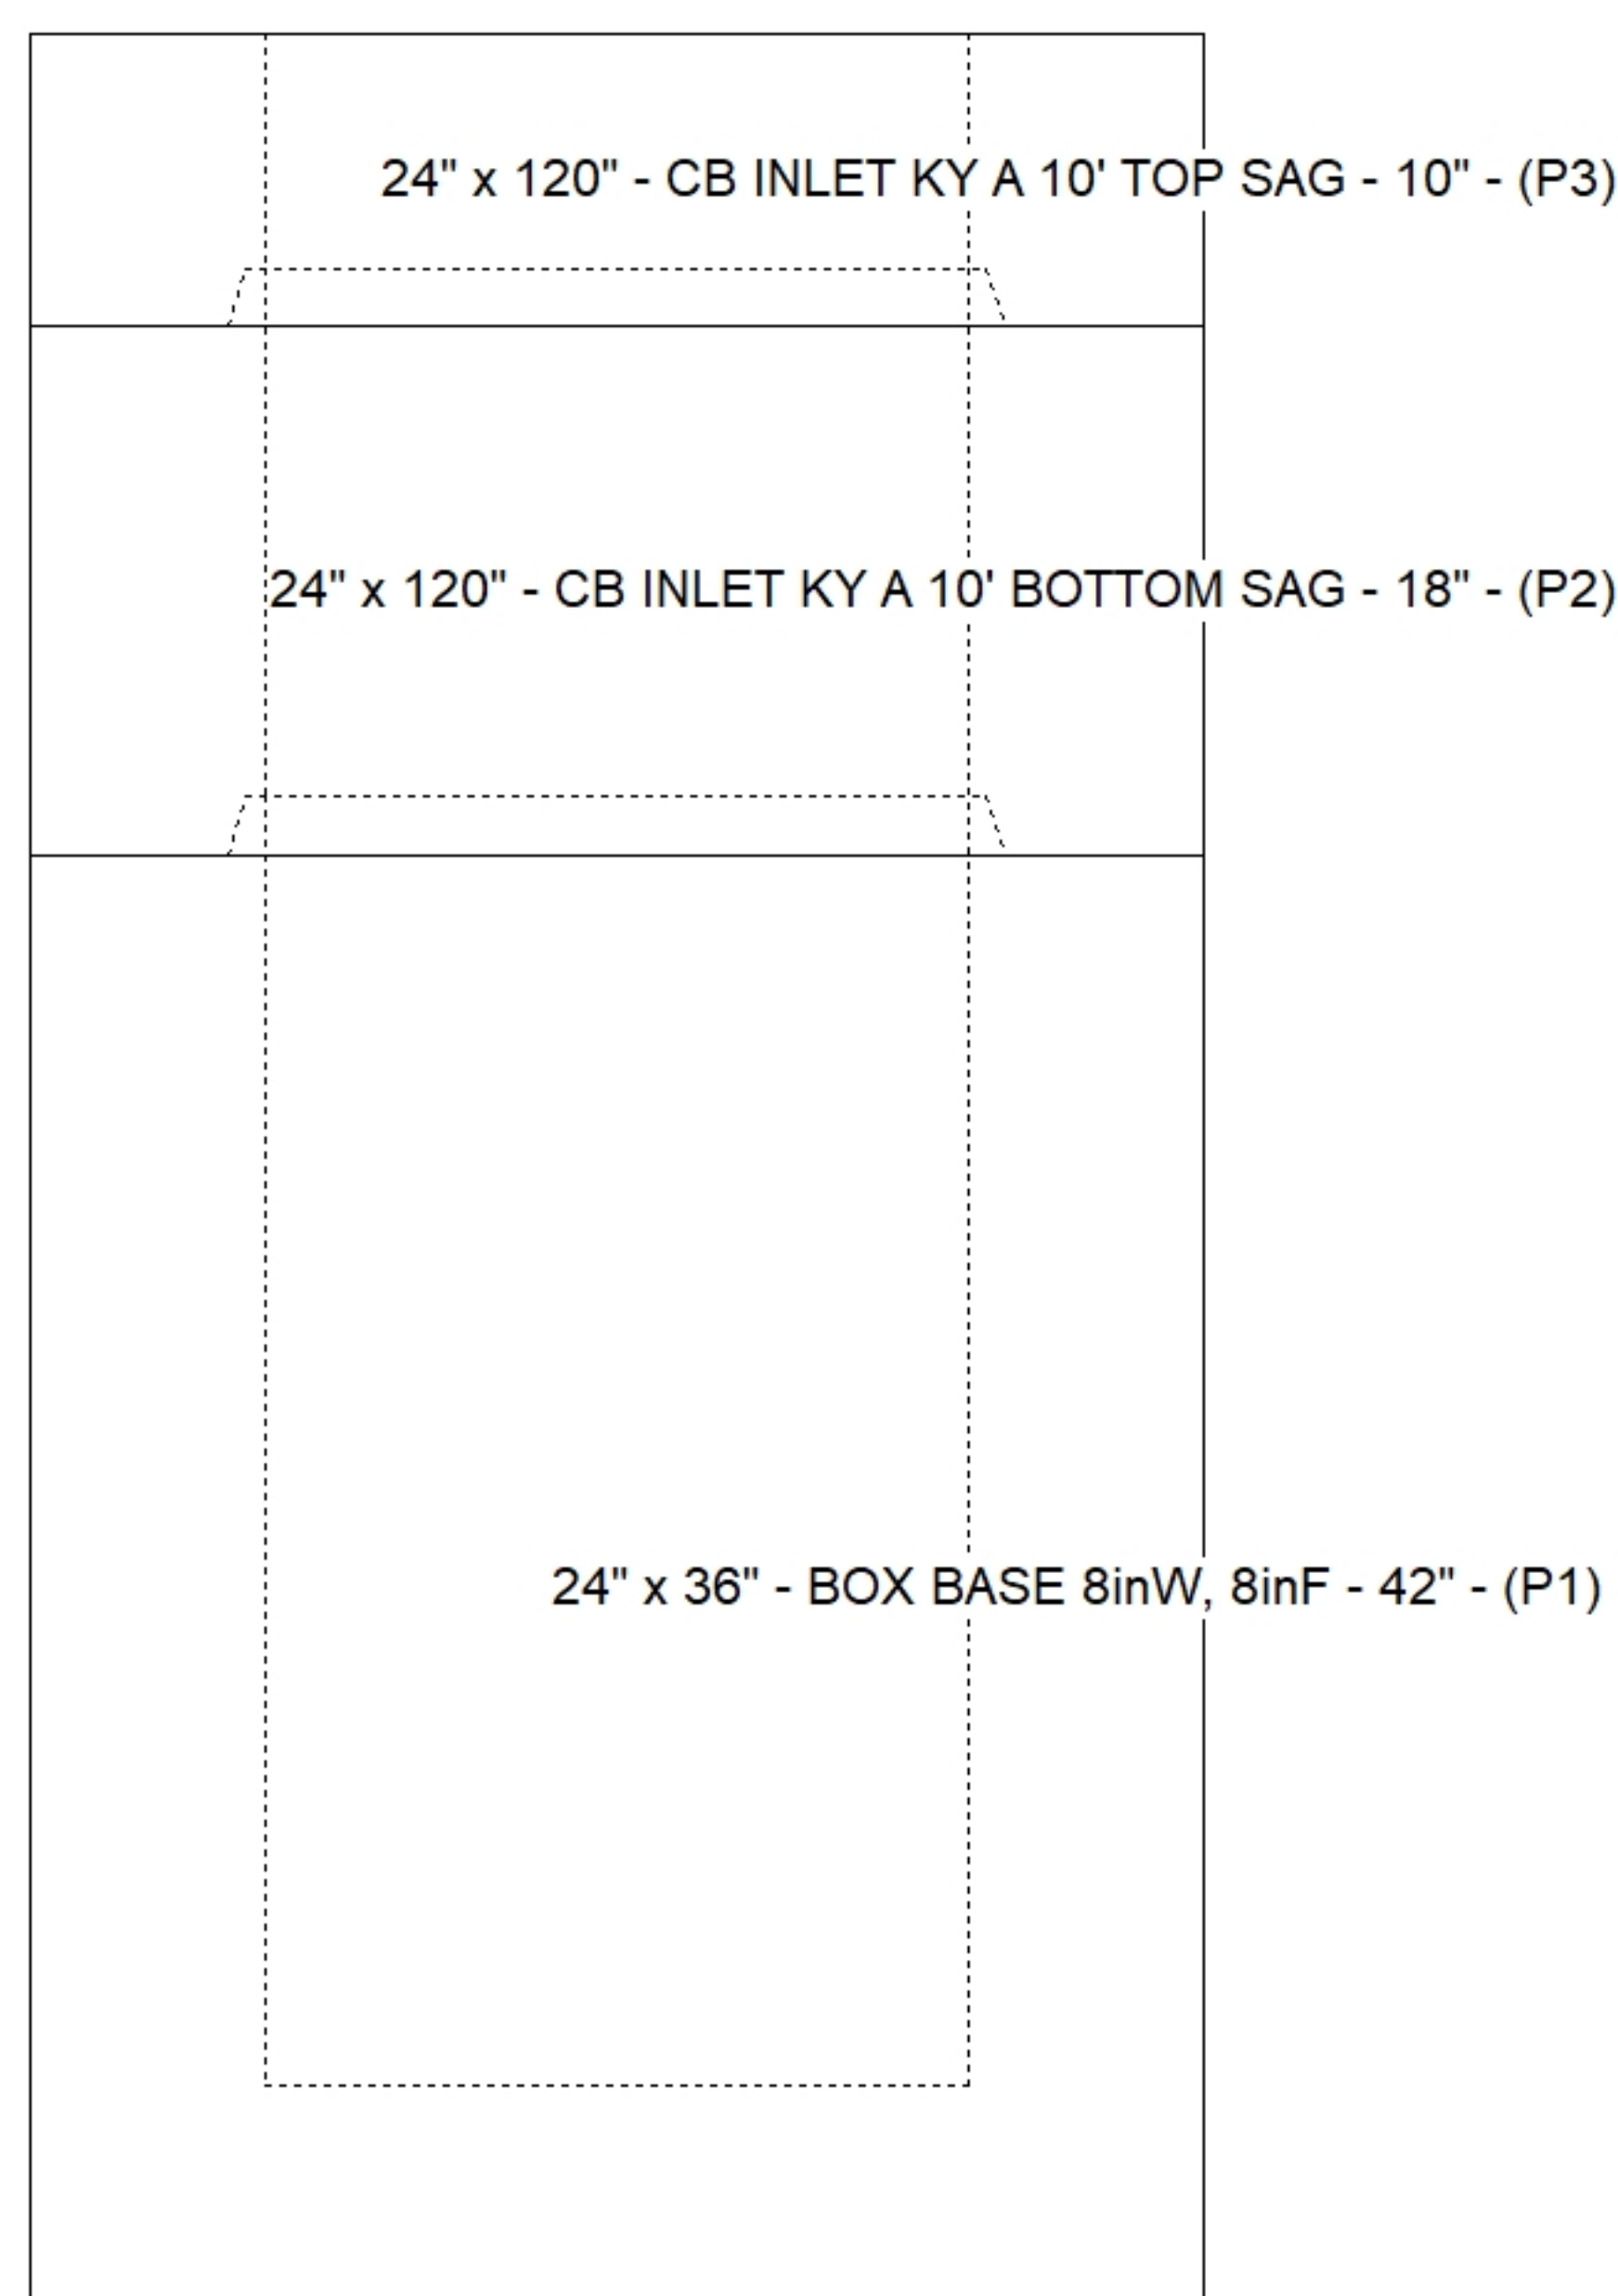

### Default - Interior Dimensions

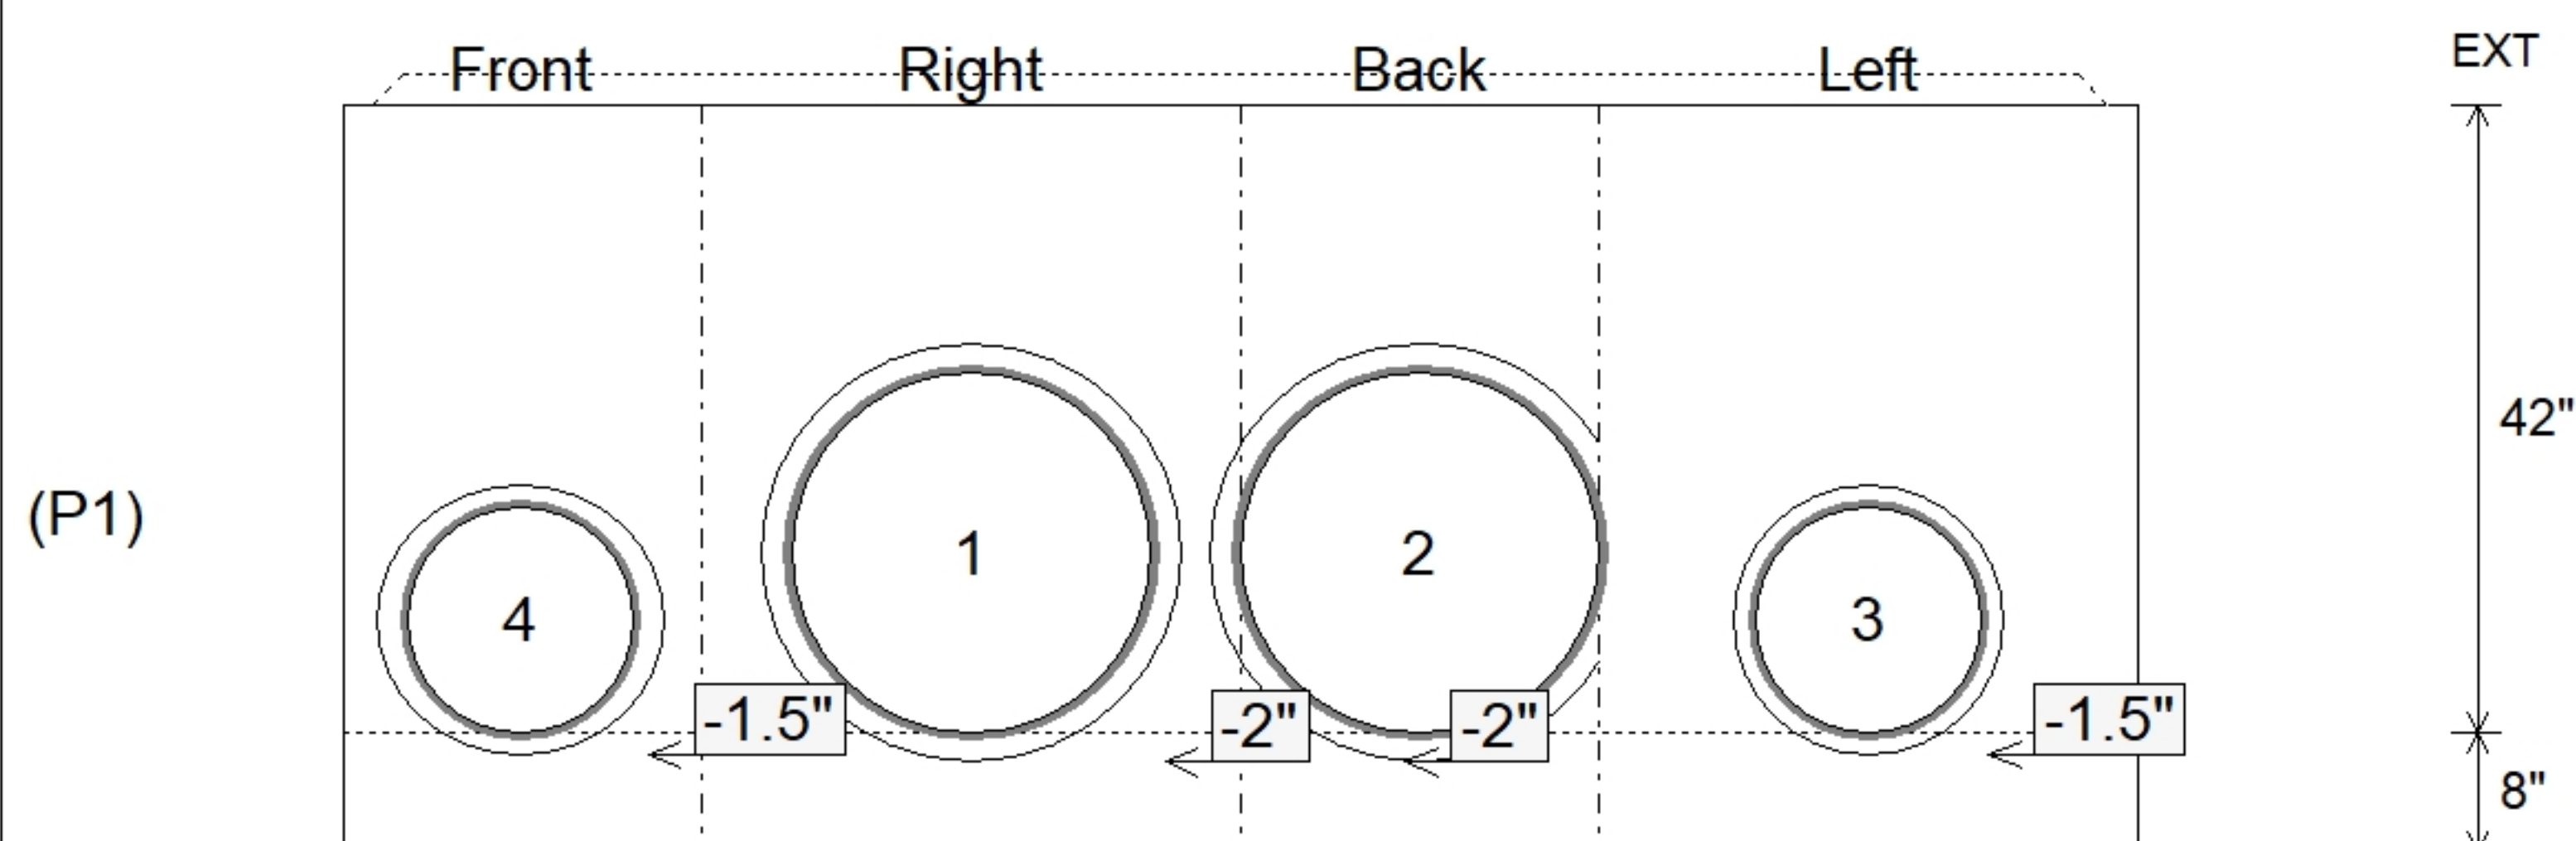

Submittal Drawing  
7/29/2026 12:08:40 PM

SUBMITTAL  
APPROVED BY:
