

Job Name: 26-1635 - KYTC Oldham Co (261505)

Job Location: Peewee Valley, KY

Contractor: Cleary Construction, Inc.

Plant: 100

7/27/2026 11:36:05 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: 50110-83 CBIA

P1 BX2436-08BA36

BOX BASE 8inW, 8inF T/n

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"

P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"

P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 36"

1) CASTING - HOE KY-206 F/C (KY CBI A)

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 18

3398 lb

5270 lb

4899 lb

206 lb

0 lb

0 lb

Structure Total: 13773 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PI AT 28 DAYS.

3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 798.97'

Rim to Invert: 5.52'


Slack: 2.24"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	793.45'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

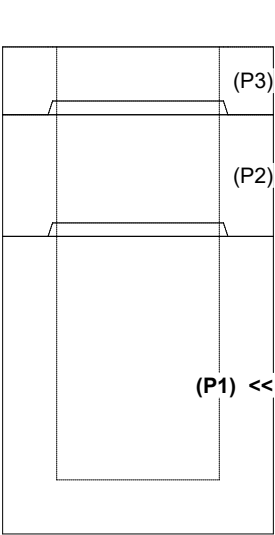

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

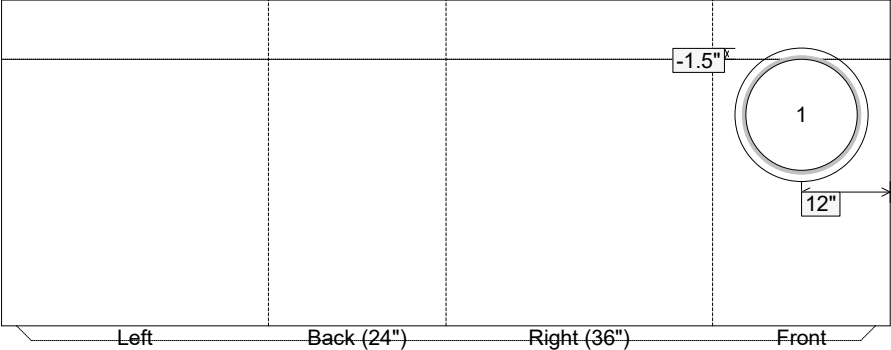

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 36"

Height (Ext): 44"

Weight (Net): 4899 lb

Volume (Net): 1.25cu.yd
