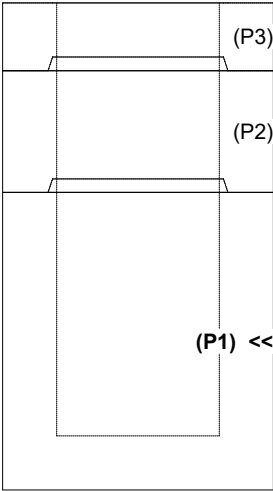


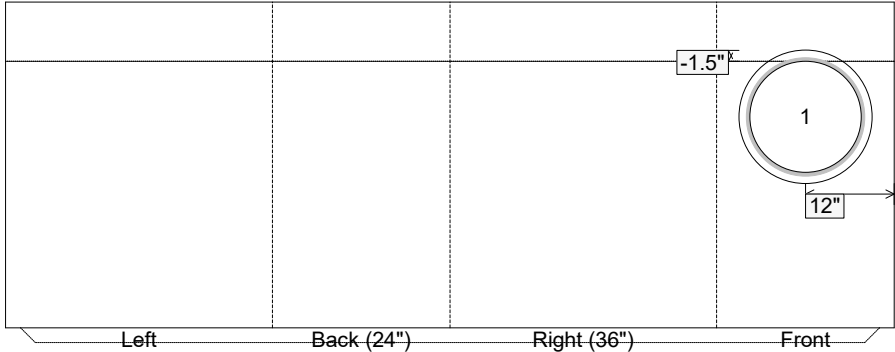


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:36:07 AM		Tech: Jared - F PC: T. Ryan			
Structure ID: 50650-86 CBIA										
P1 BX2436-08BA36 BOX BASE 8inW, 8inF T/n										
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 36" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18"					3398 lb 5270 lb 4899 lb 206 lb 0 lb 0 lb ----- Structure Total: 13773 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 806.92' Rim to Invert: 5.52' Slack: 2.24" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	801.4'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)										
										
INSIDE WALL DIMENSIONS										
										
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 4899 lb Volume (Net): 1.25cu.yd	
