



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:36:08 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 50725-87 CBIA											
P1		BX2436-08BA36		BOX BASE 8inW, 8inF T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 36" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 3) Hole - 18"					3400 lb 5270 lb 4557 lb 206 lb 0 lb 0 lb ----- Structure Total: 13433 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 804.43' Rim to Invert: 5.52' Slack: 2.24" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	798.91'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2	798.91'	90°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 3	798.91'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

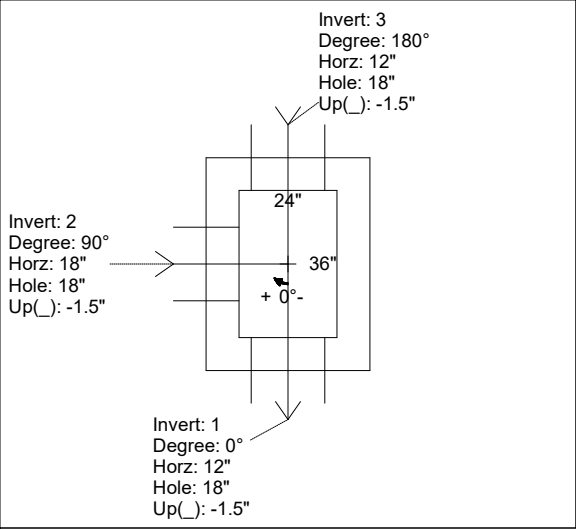

UPSIDE-DOWN VIEW (int. dimensions)

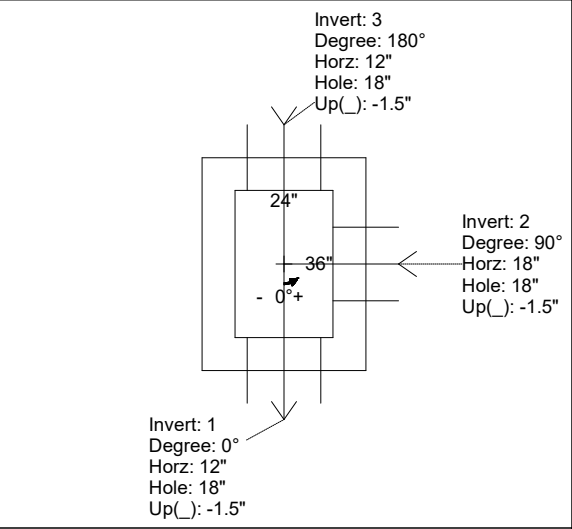

INSIDE WALL DIMENSIONS

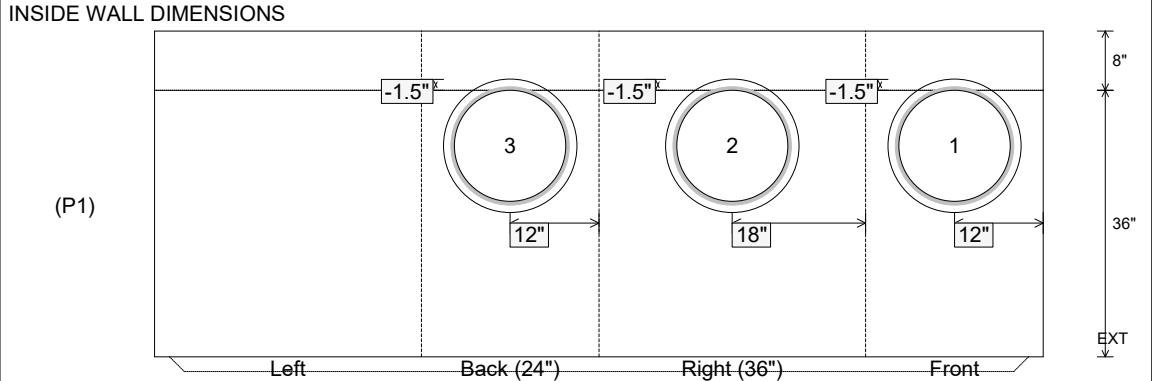

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4557 lb Volume (Net): 1.16cu.yd
----------------------------------	---------------------------------	--	--	--
