

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.71'


Floor Height: 8"

Slack: 3.52"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

0 lb

Structure Total:	12918 lb
------------------	----------

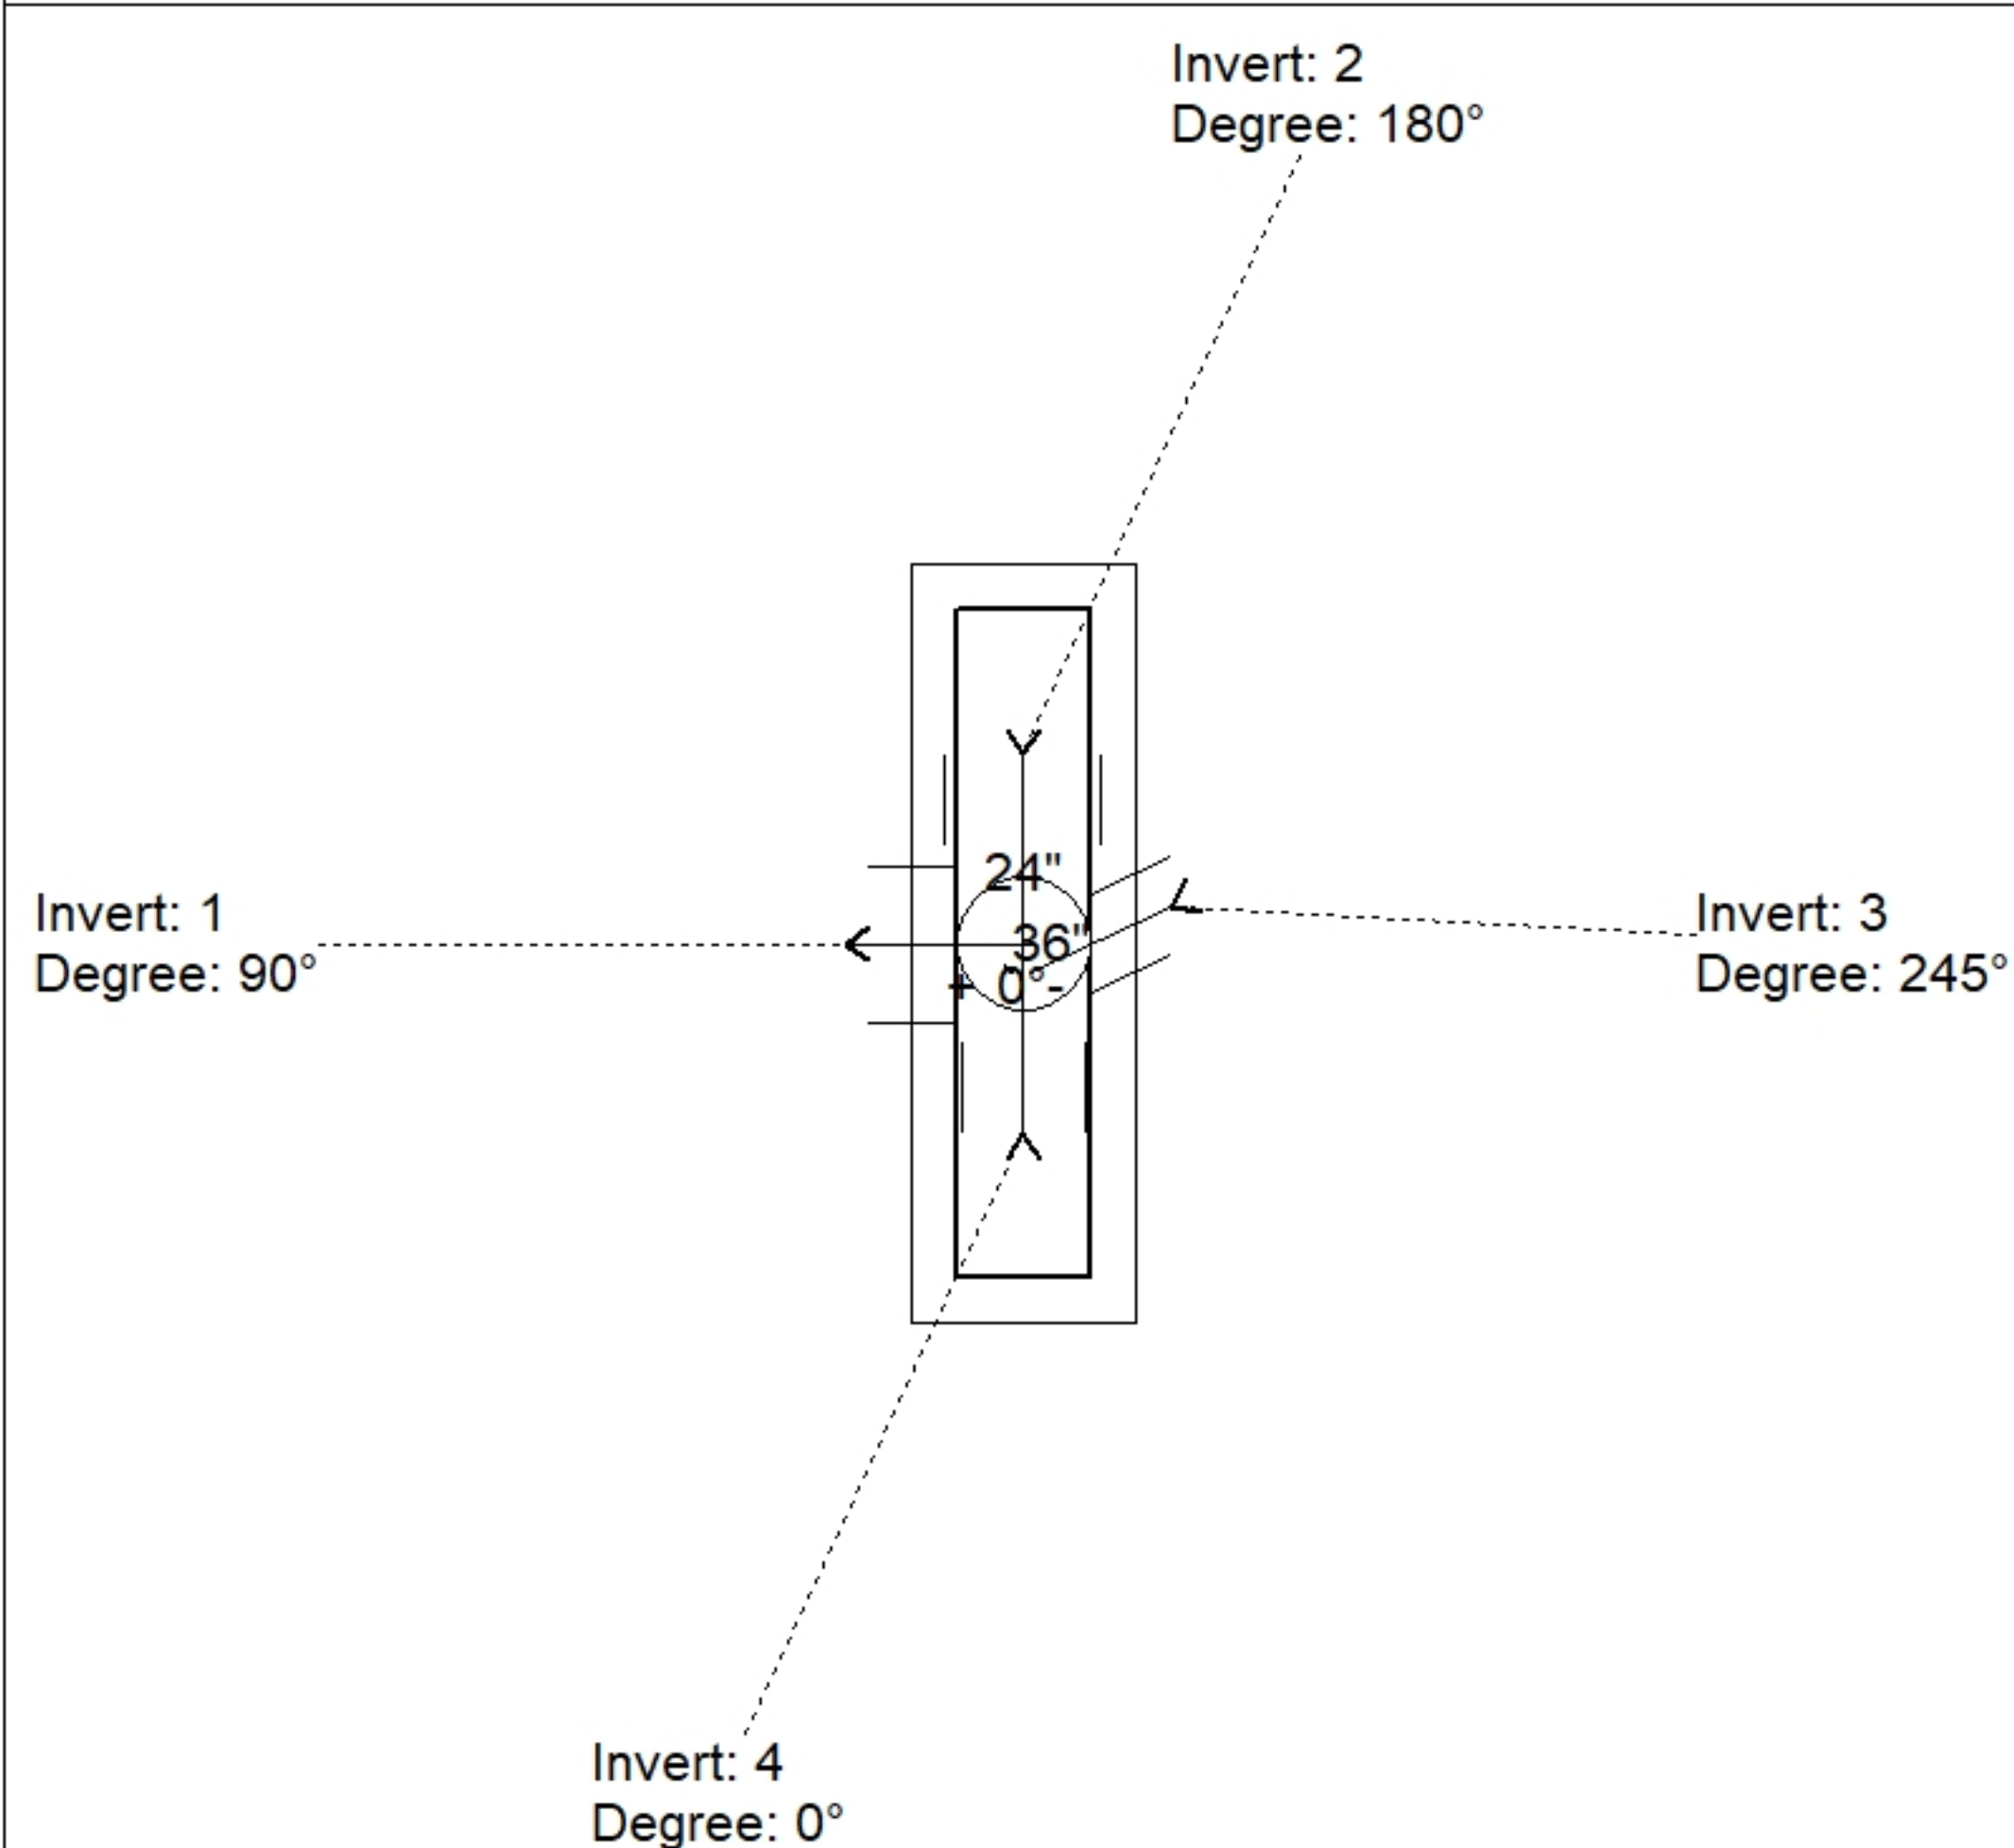


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	794.74'							
Reducer								
Invert 1	789.03'	90°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	789.03'	180°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 3	789.03'	245°	12" CMP	13"	16"	Hole 16	-2"	P1
Invert 4	789.03'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP SAG - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM SAG - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 37" - (P1)

Default - Interior Dimensions

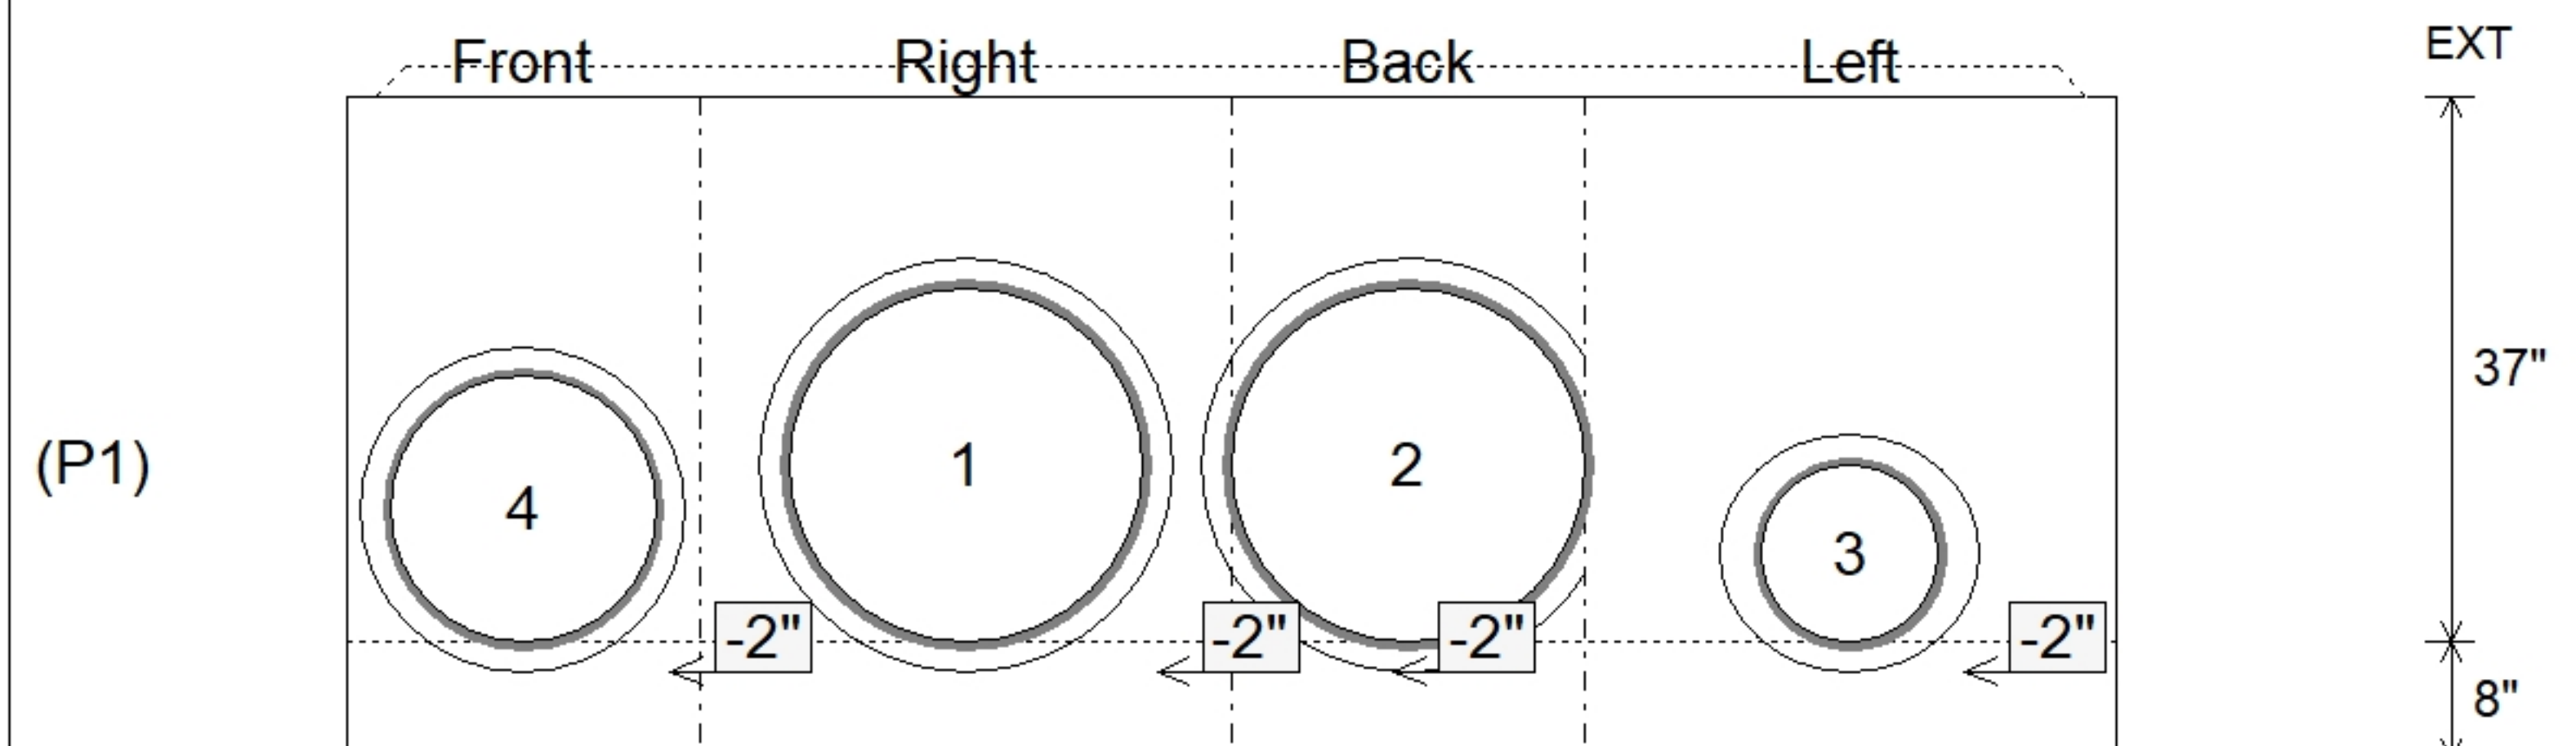

Submittal Drawing
7/29/2026 12:08:46 PM

SUBMITTAL
APPROVED BY:
