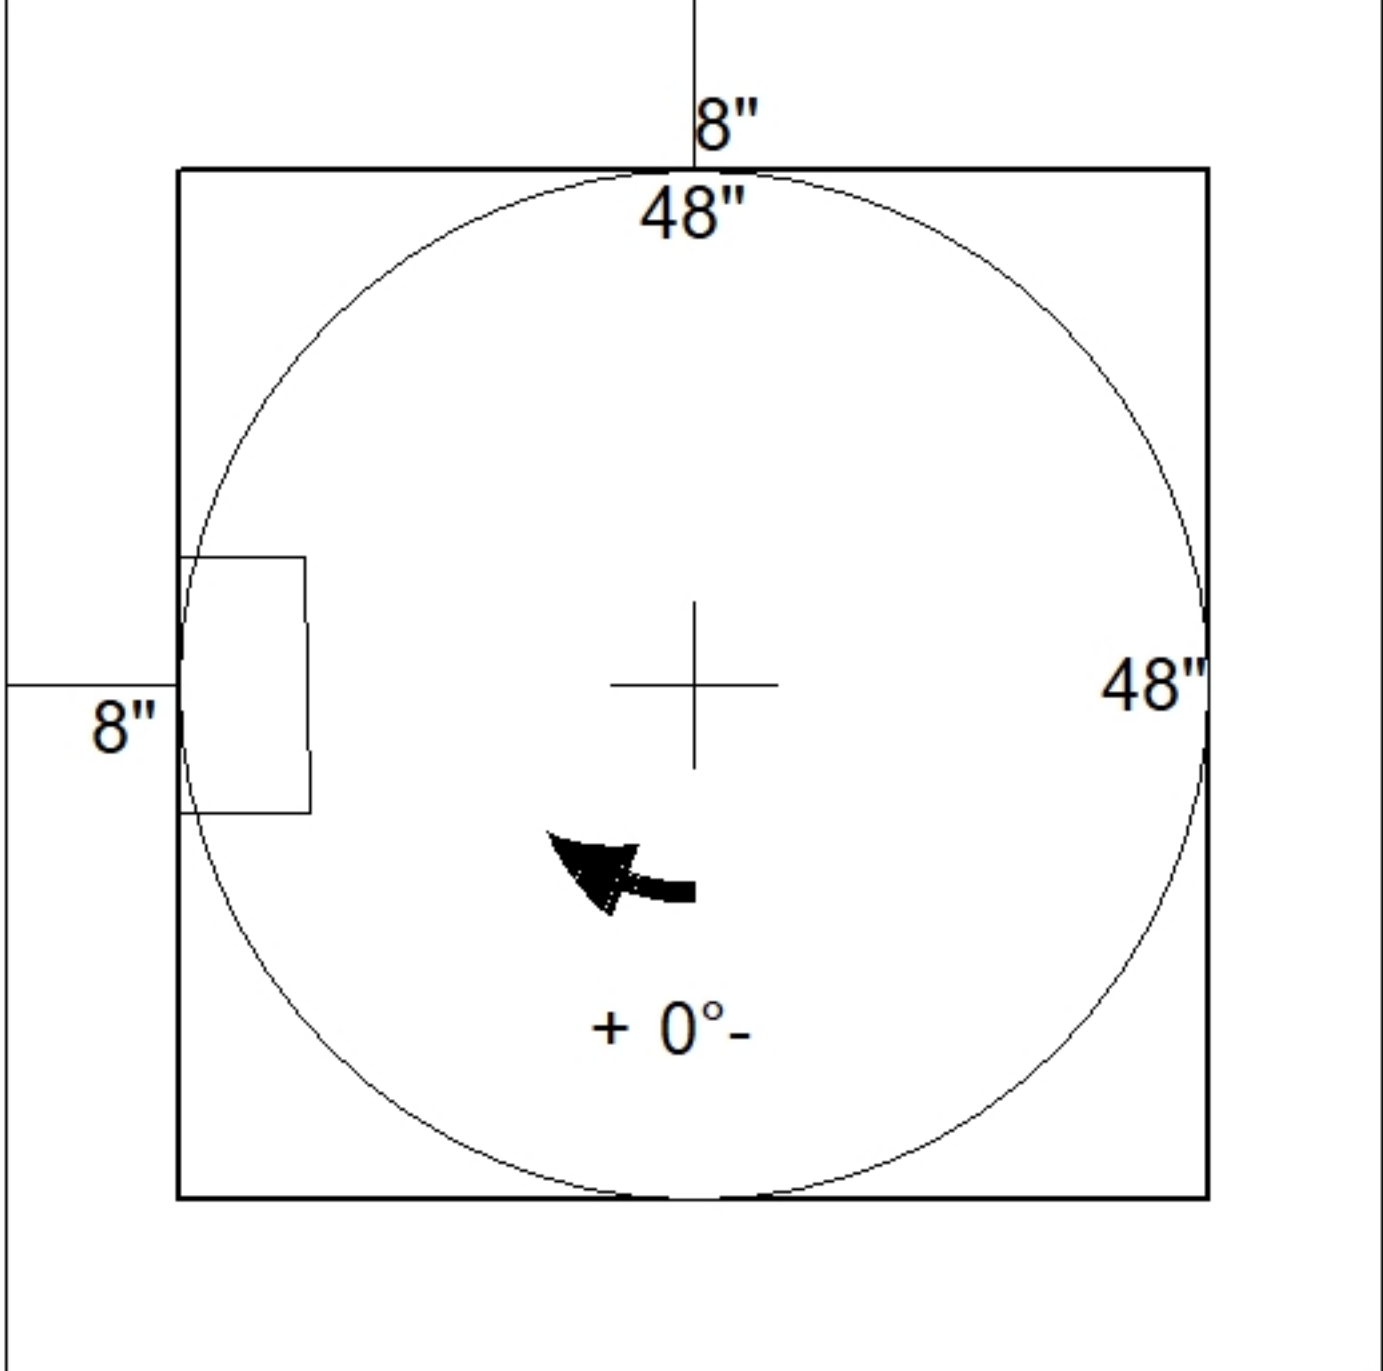
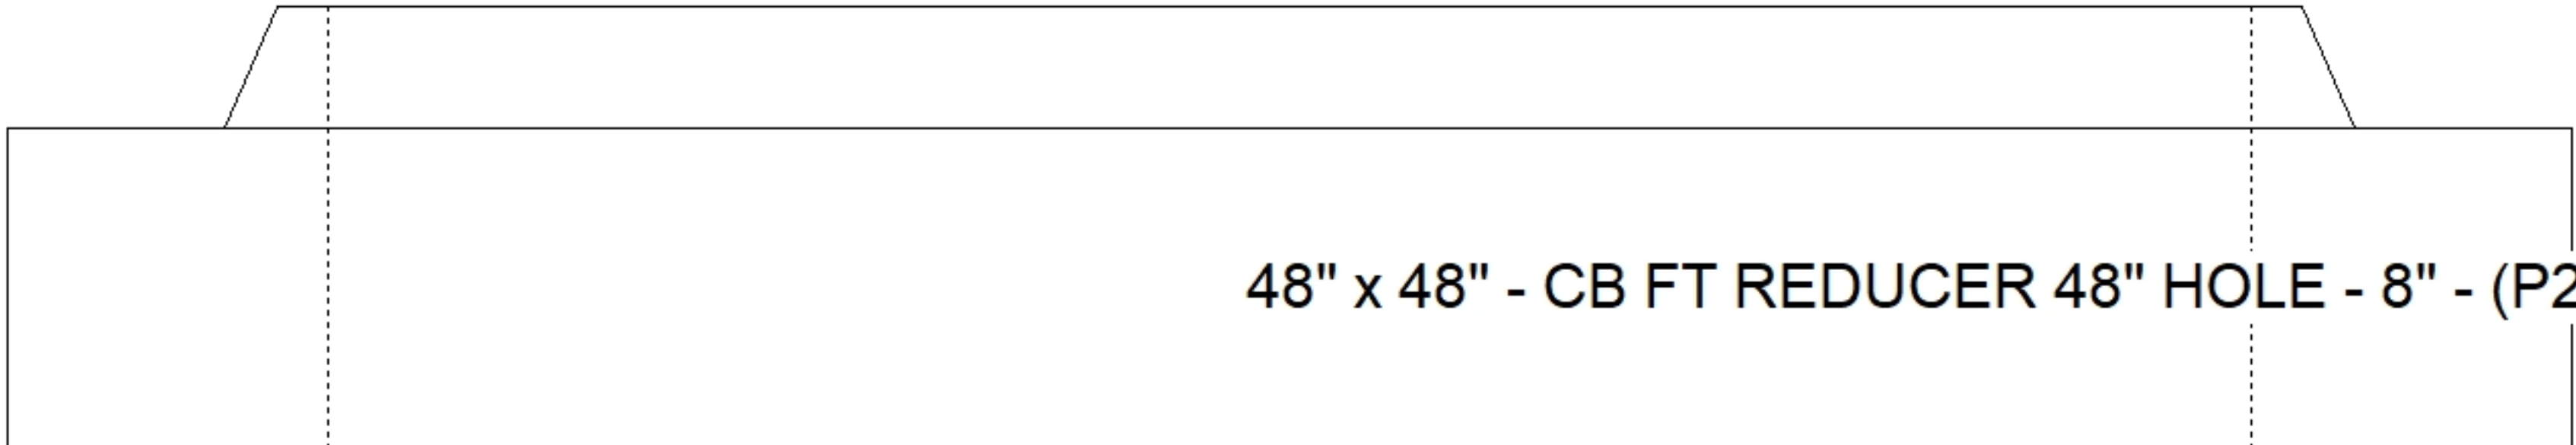


Job Name: 26-1635 - KYTC Oldham Co (261505) - P4		Plant: 100	Tech: Jared - F	
Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.		8/17/2026 2:00:48 PM	PC: T. Ryan	
Structure ID: 35770-148 MHC				
P2 BX048048-08TS48		CB FT REDUCER 48" HOLE		
P4) 24" - CASTING HEIGHT - 8" P3) 48" - ECC CONE w/ 24" HOLE - 24" P2) 48" x 48" - CB FT REDUCER 48" HOLE - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF - 38" 1) SECONDARY POUR - EXT FLANGE 1) 48" x 48" - Conseal CS-102 1.00" 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 34 1) Hole - 22 6) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 1535 lb 10684 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 13769 lb	Structure Notes: . ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-510 F/C (KY TY.2)). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W.	
				
 48" x 48" - CB FT REDUCER 48" HOLE - 8" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 1535 lb Volume (Net): 0.39cu.yd
