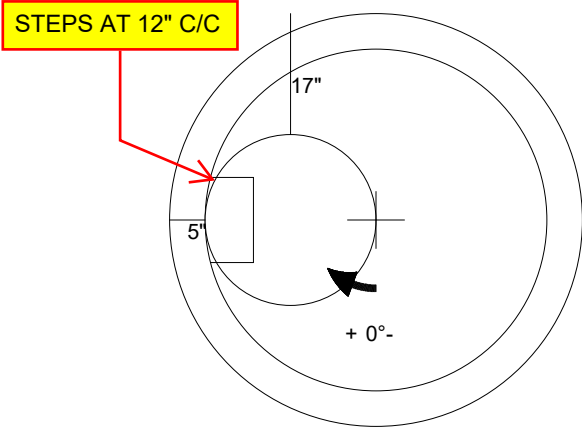



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.		Plant: 100 8/14/2026 1:21:12 PM	Tech: Jared - F PC: T. Ryan		
Structure ID: 35770-148 MHC					
P3 MH048CN24		ECC CONE w/ 24" HOLE F/G			
P4) 24" - CASTING HEIGHT - 8" P3) 48" - ECC CONE w/ 24" HOLE F/G - 24" P2) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 38" 1) 48" x 48" - Conseal CS-102 1.00" 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 34 1) Hole - 22 6) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 1535 lb 10684 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 13769 lb		Structure Notes: . ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-510 F/C (KY TY.2)). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W.	
					
					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
