

Contractor: Cleary Construction, Inc.

Plant: 100



Slack: 0.92"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT)
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


- P4) 15" x 27" - P.I.P. - BY OTHERS - 8"
- P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
- P2) 24" x 30" - BOX RISER 8inW - 30"
- P1) 24" x 30" - BOX BASE 8inW, 8inF - 48"
- 2) 24" x 30" - Conseal CS-102 1.00"
- 1) 15" x 27" - Conseal CS-102 1.00"
- 1) Hole - 28
- 1) Hole - 18
- 1) Hole - 22
- 2) Hole - 4

0 lb
963 lb
2803 lb
4907 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 8673 lb

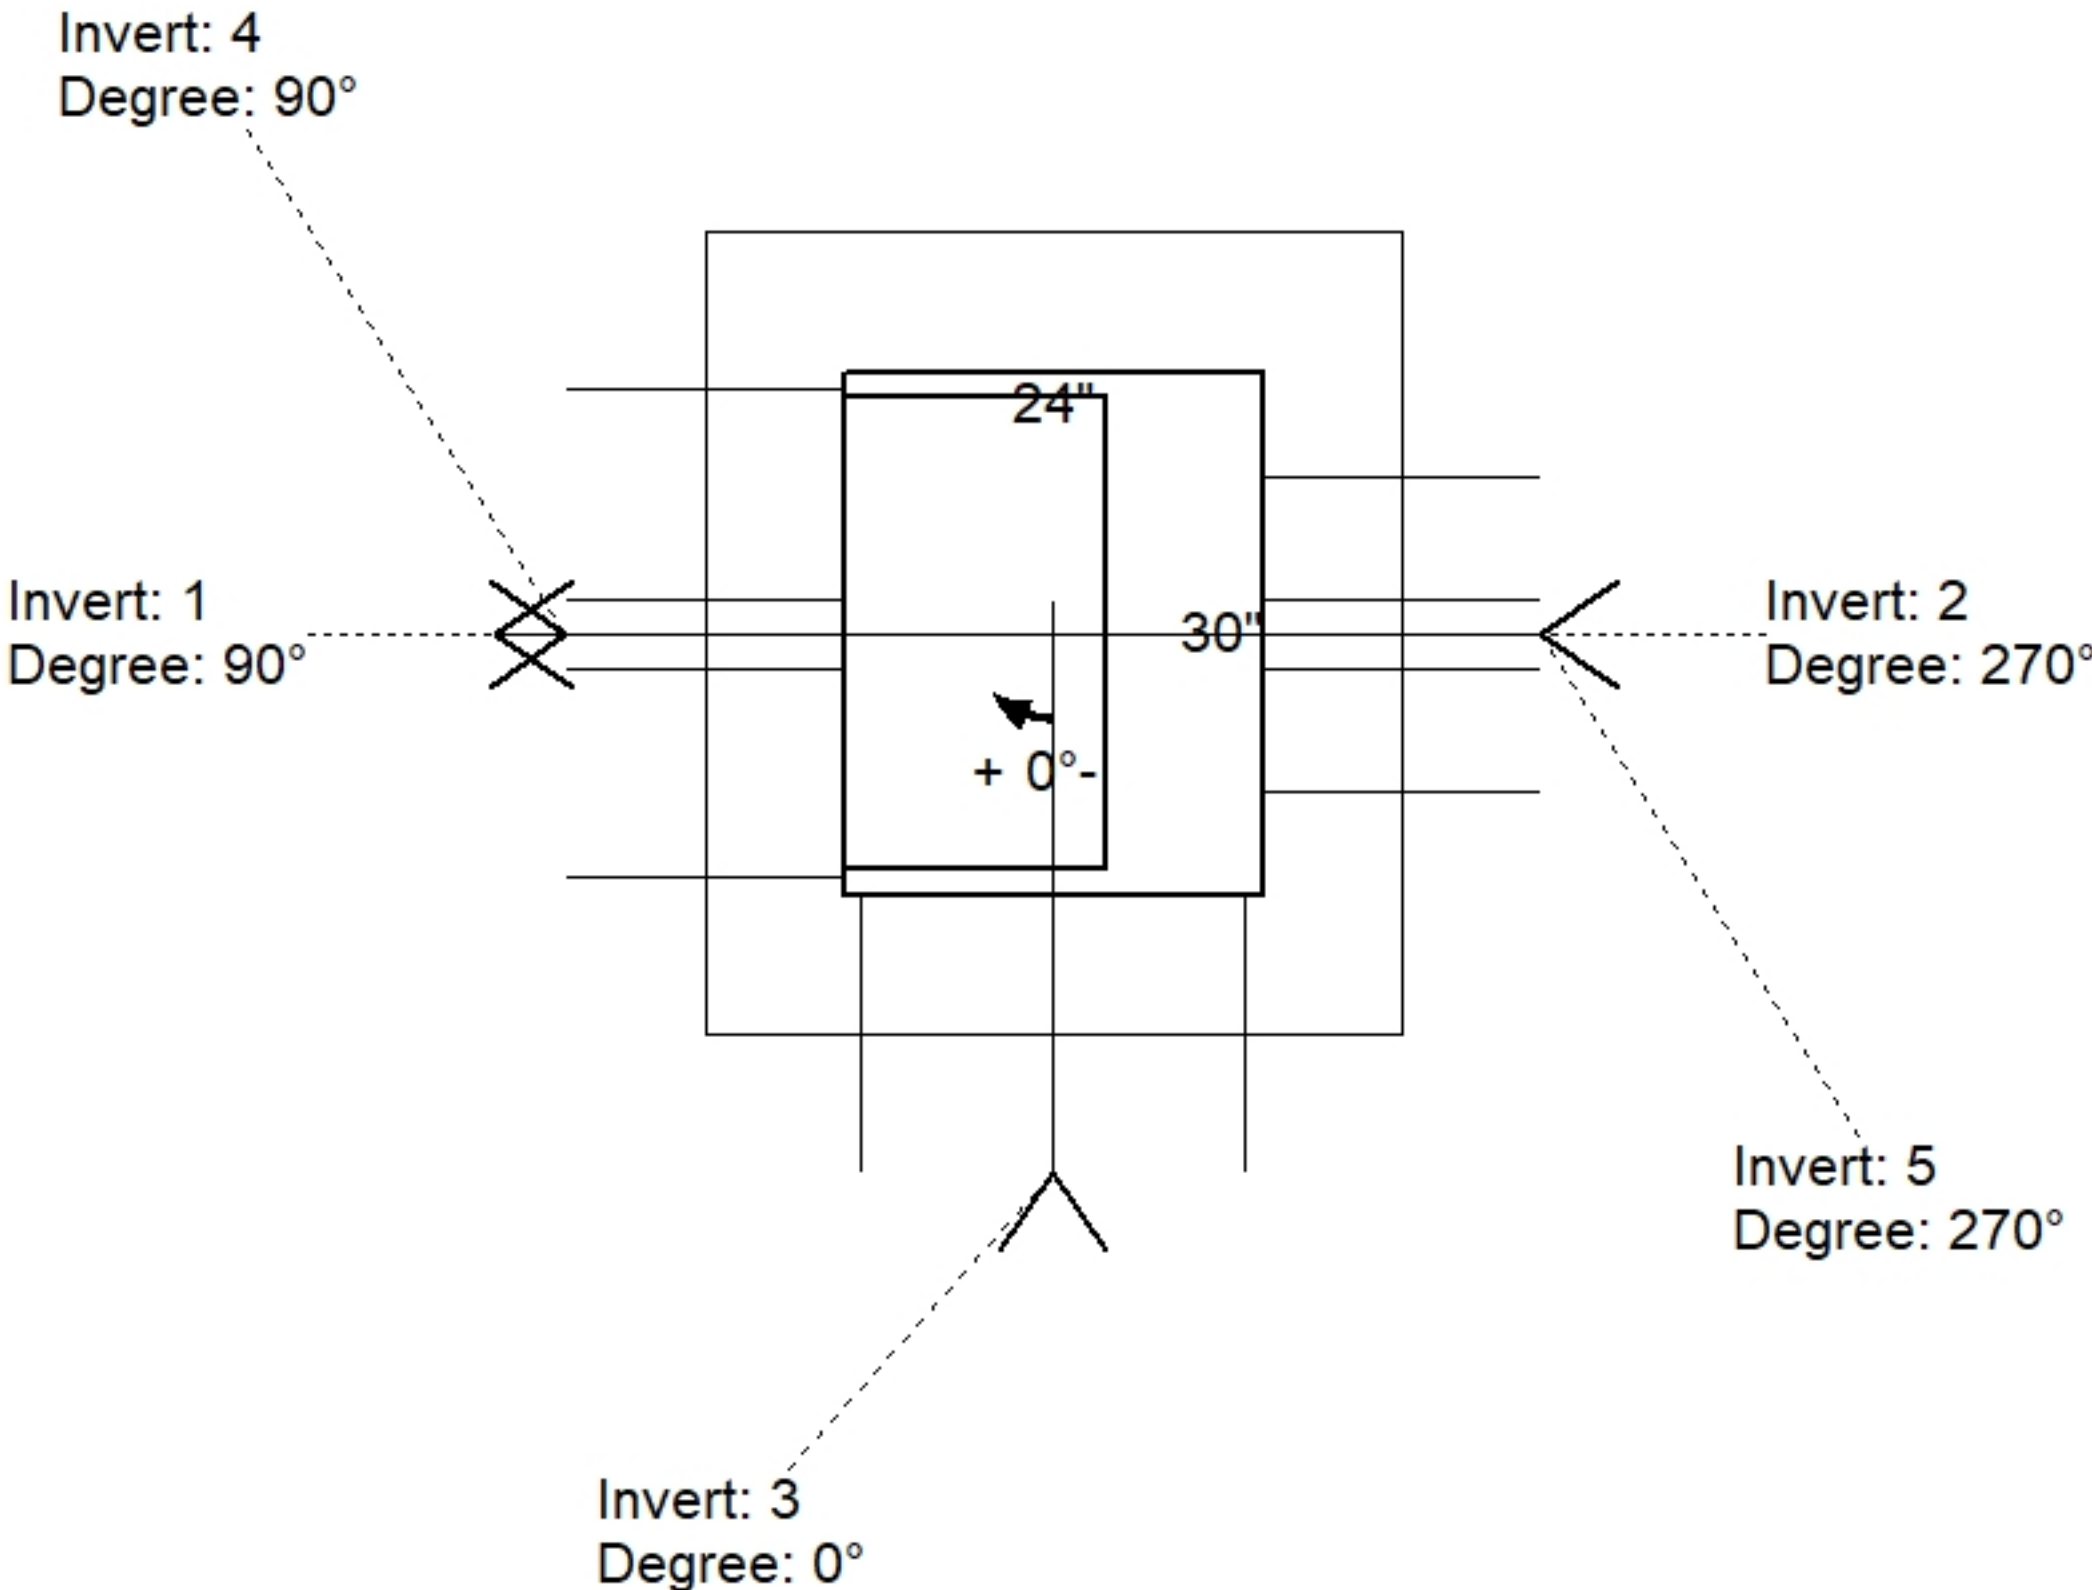

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	820.55'							
Reducer								
Invert 1	812.64'	90°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	814.52'	270°	15" CMP	16"	18"	Hole 18	21.06"	P1
Invert 3	812.64'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 4	818.473'	90°	4" WEEP HOLE	4"	4"	Hole 4	19.996"	P2
Invert 5	818.473'	270°	4" WEEP HOLE	4"	4"	Hole 4	19.996"	P2
Invert 6								
Invert 7								
Invert 8								

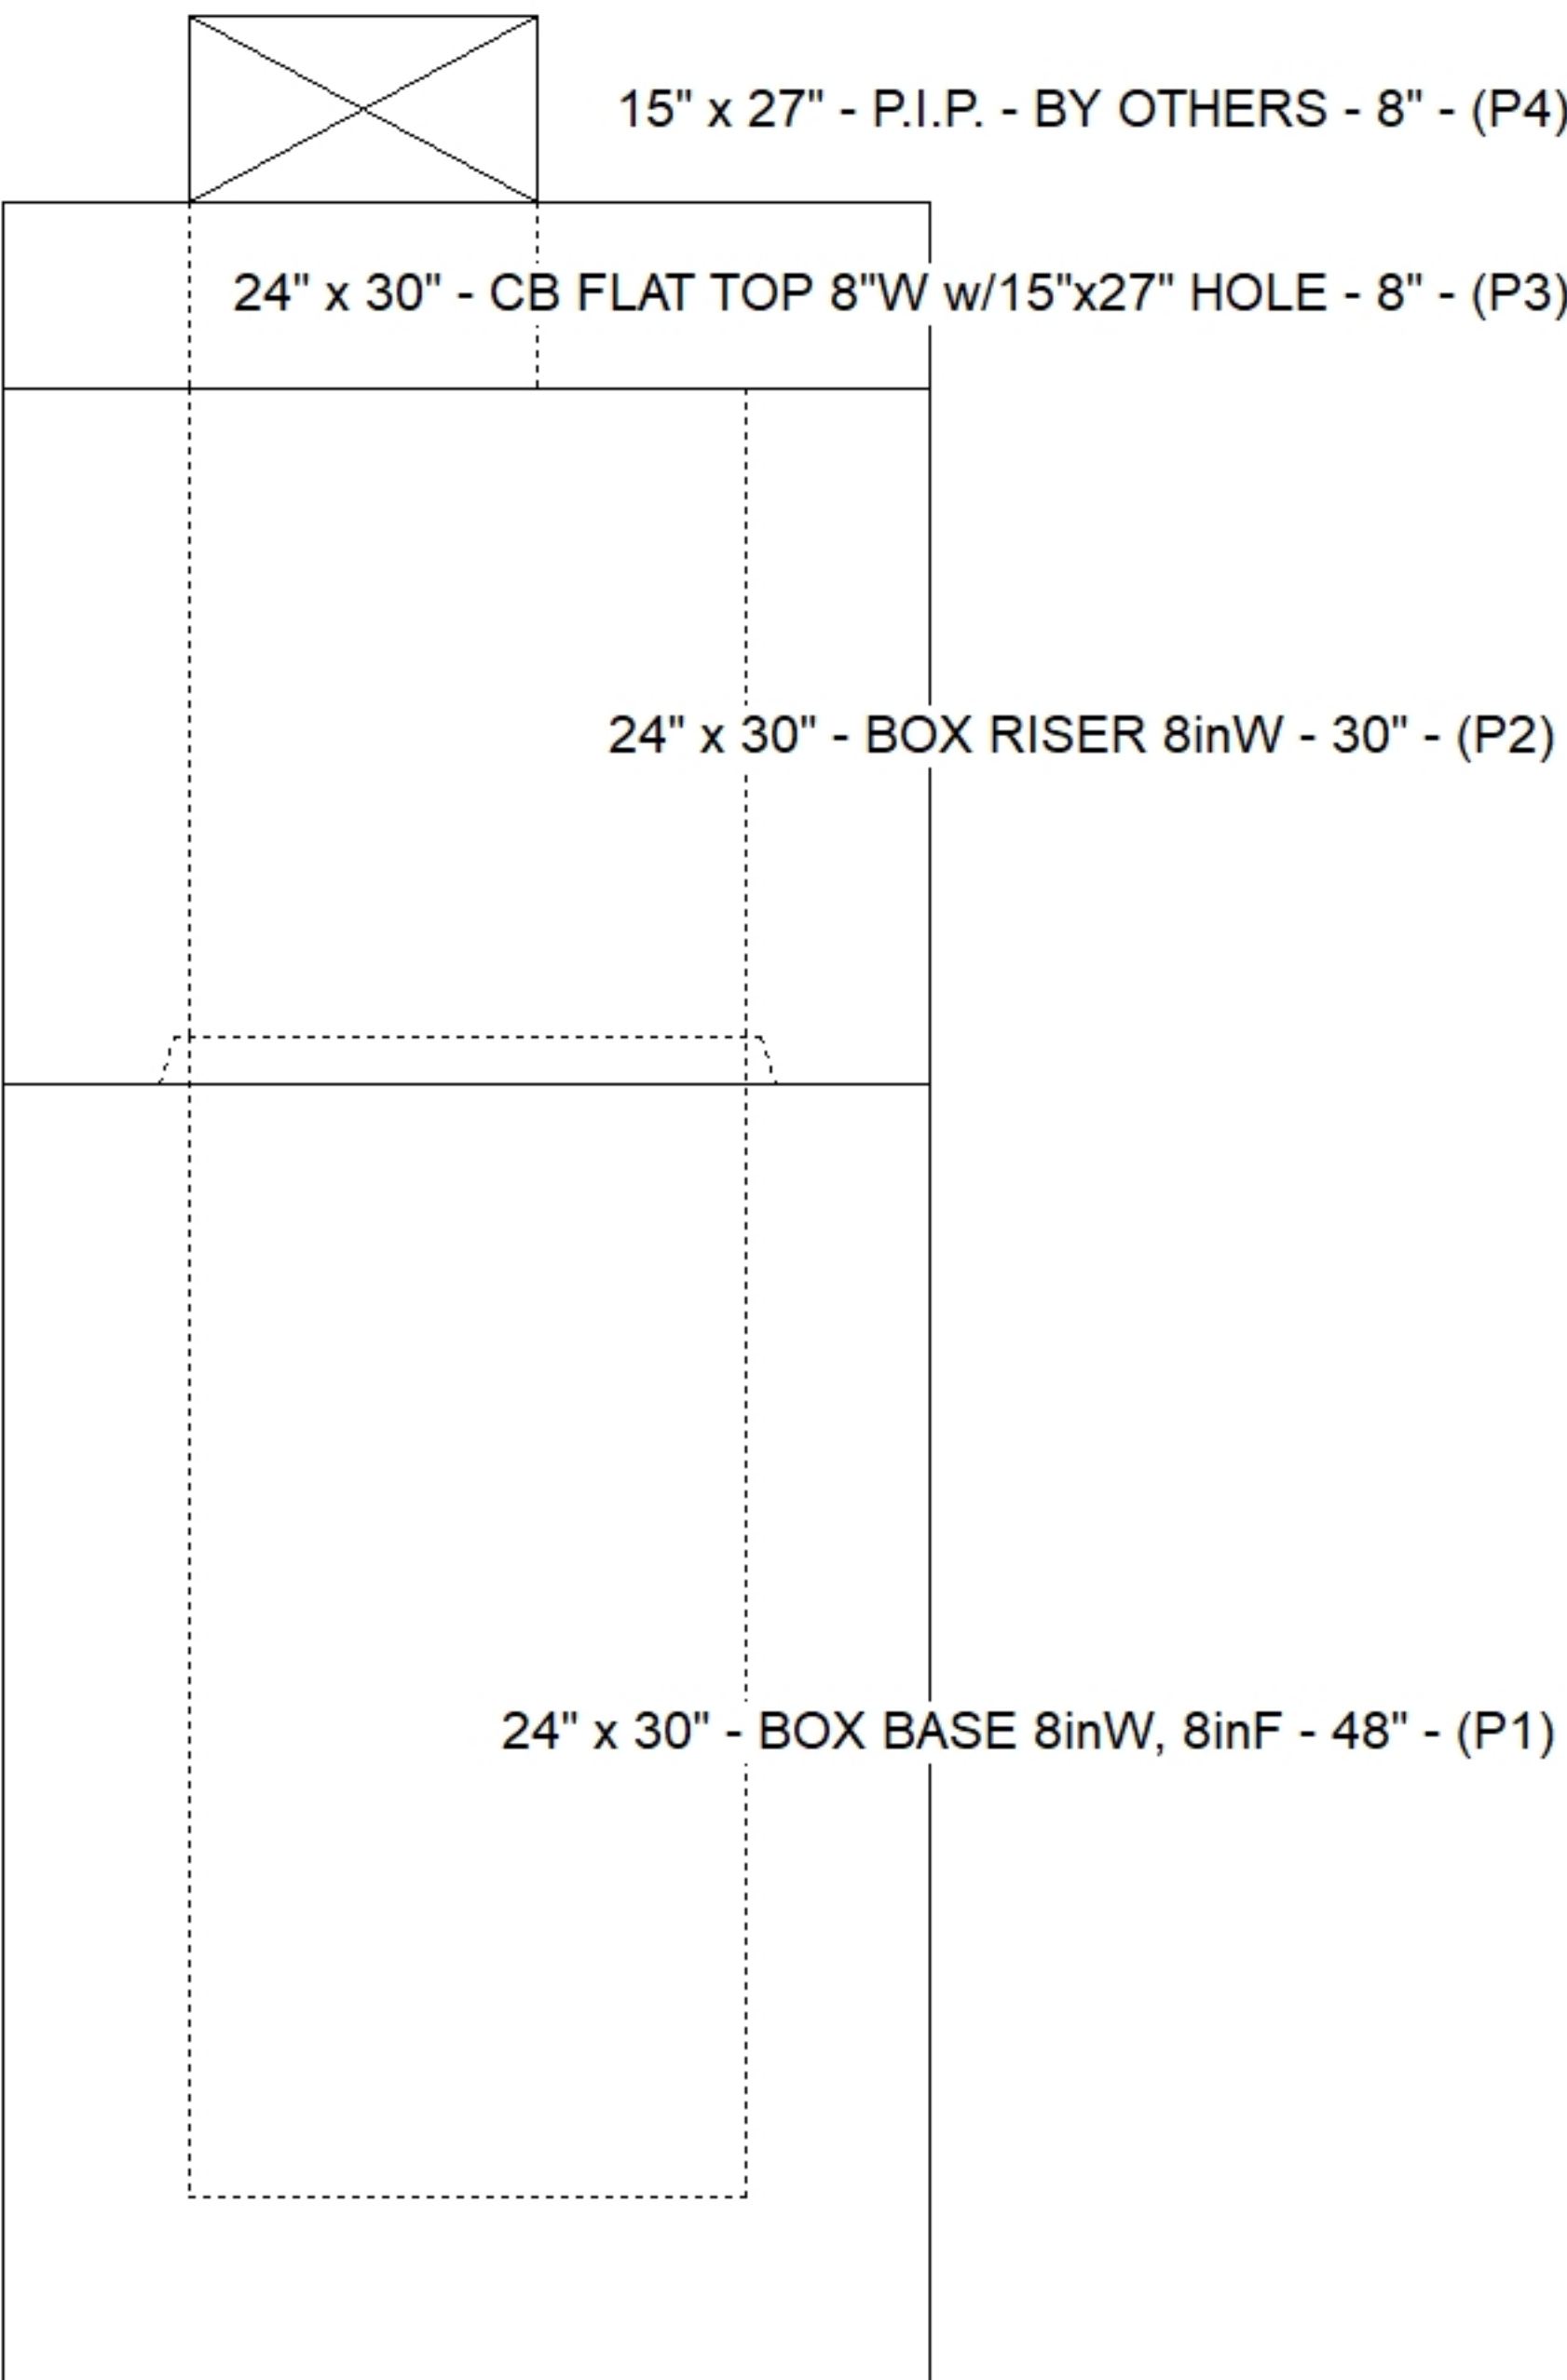

Default - Interior Dimensions

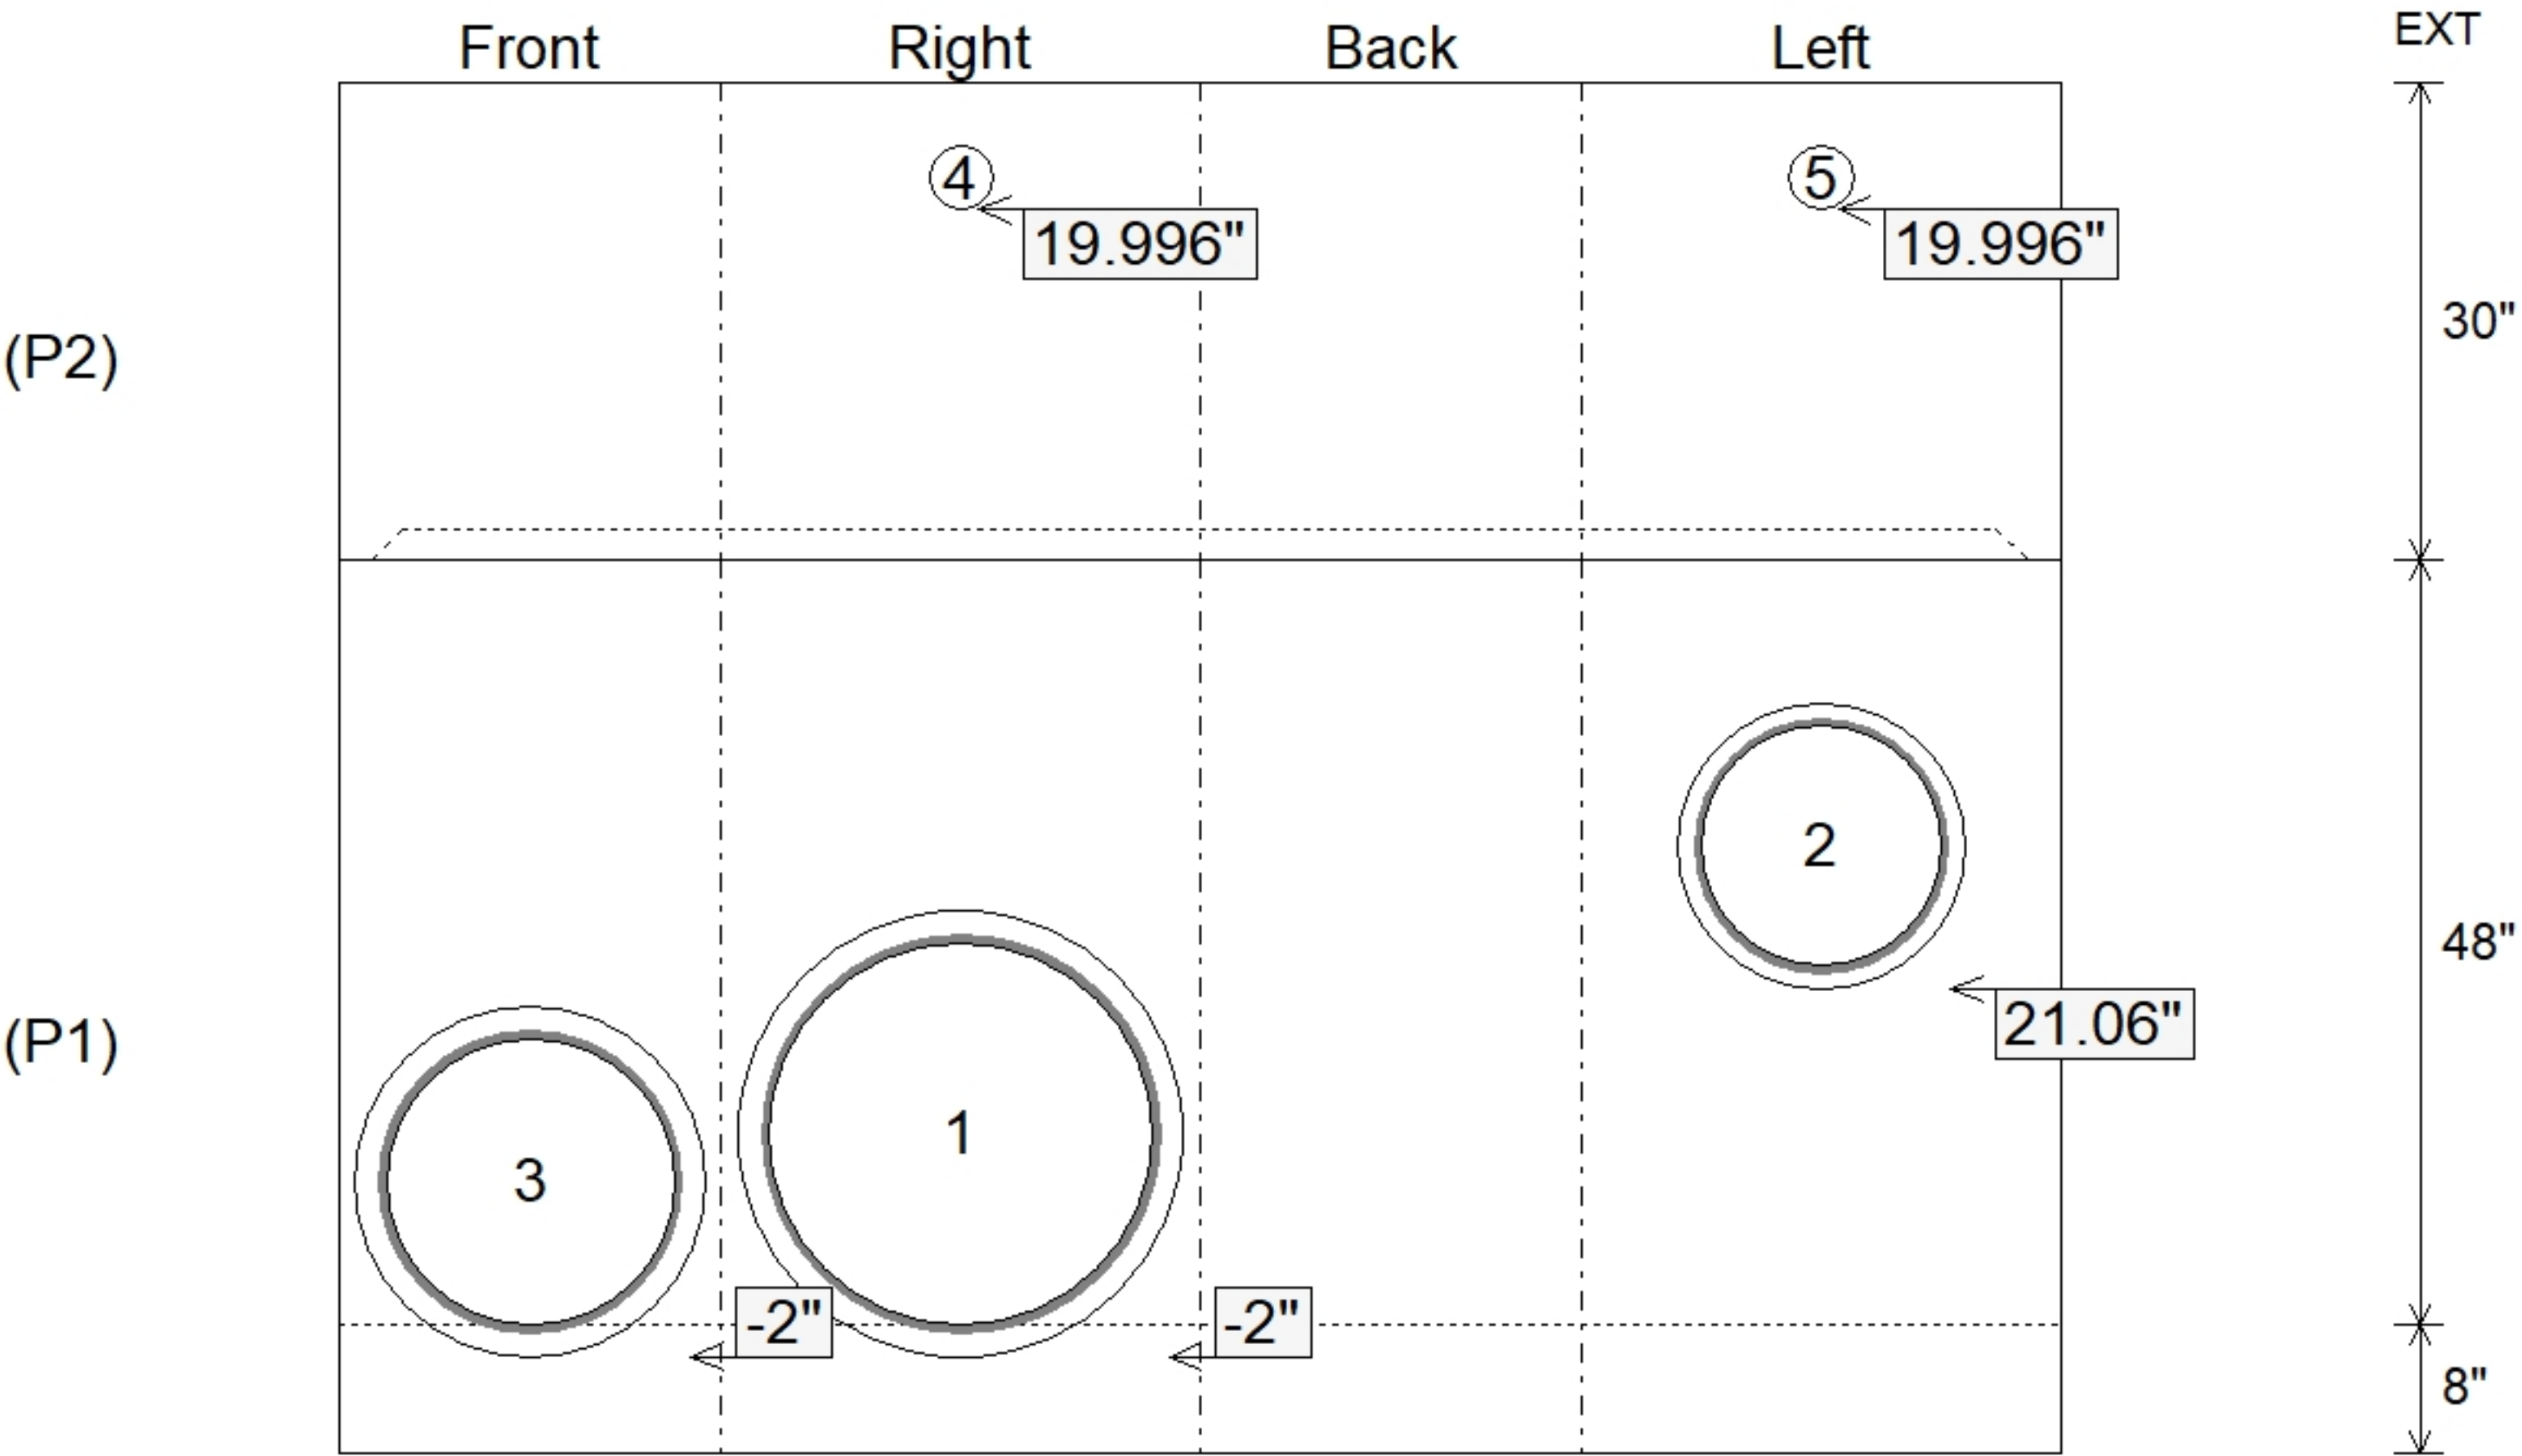

Submittal Drawing
8/17/2026 2:01:33 PM

SUBMITTAL
APPROVED BY:
