

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 3.5'

Floor Height: 8"

Slack: 0"

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3))

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P2) 36" x 36" - P.I.P. - BY OTHERS - 8'

P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 34"

1) 36" x 36" - Conseal CS-102 1.00'

1) Hole - 18


0 lb

5661 lb

0 lb

0 lb



Structure Total: 5661 lb

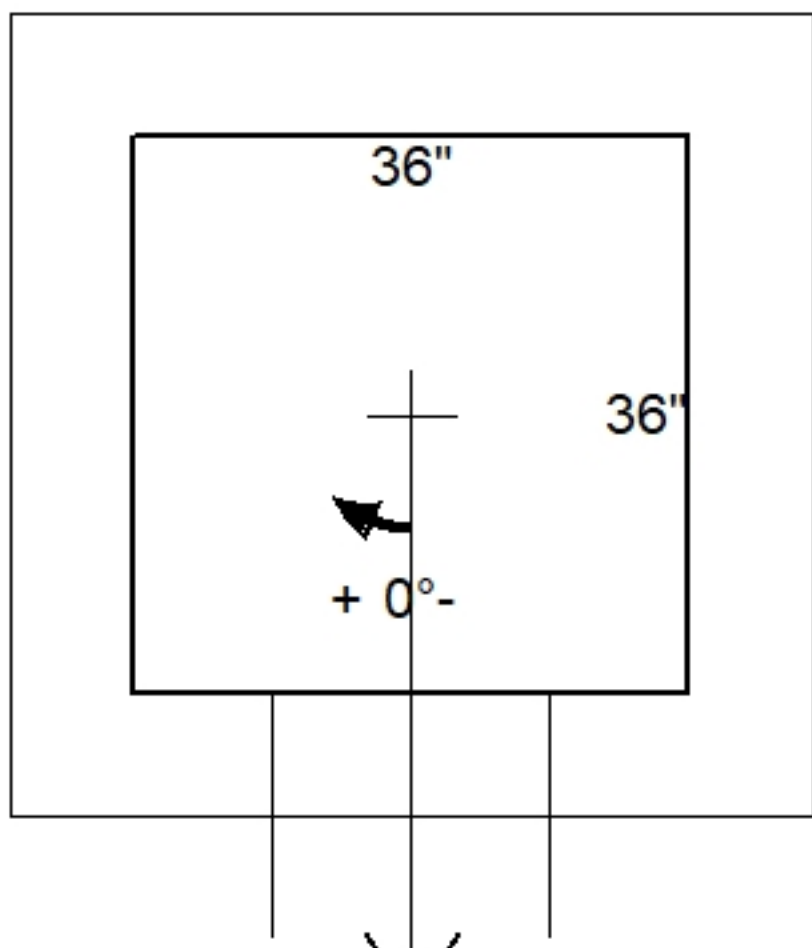

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	797.26'							
Reducer								
Invert 1	793.76'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

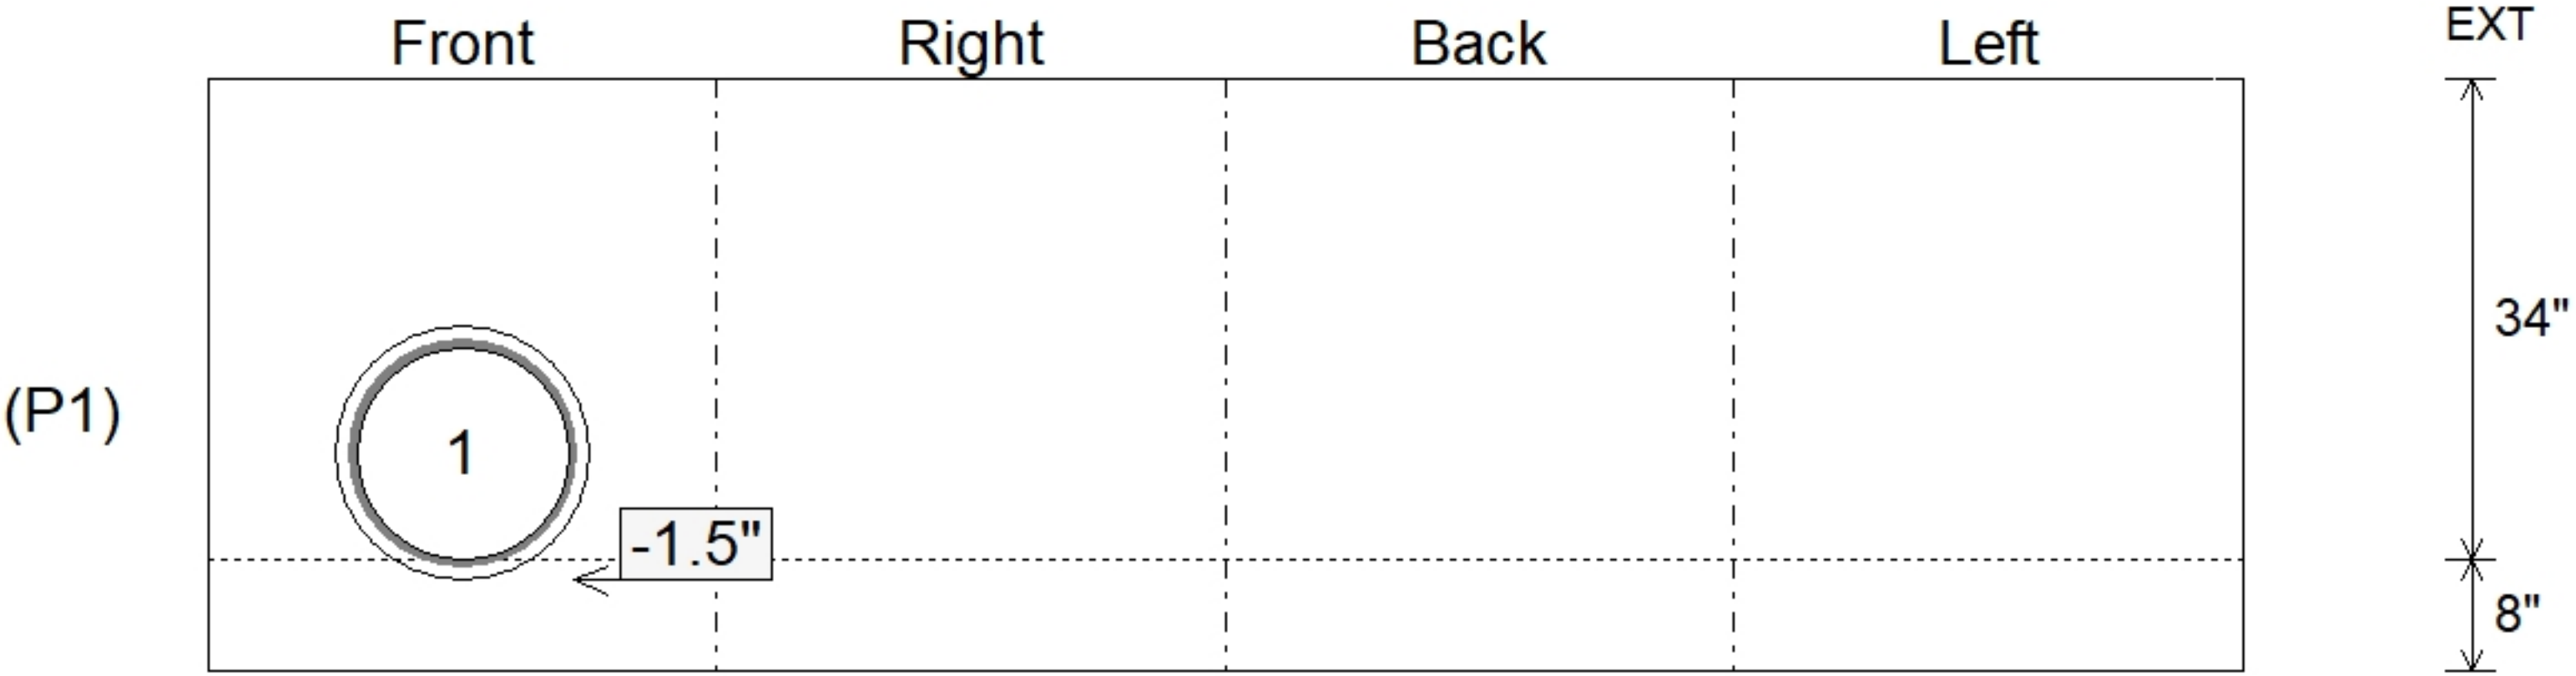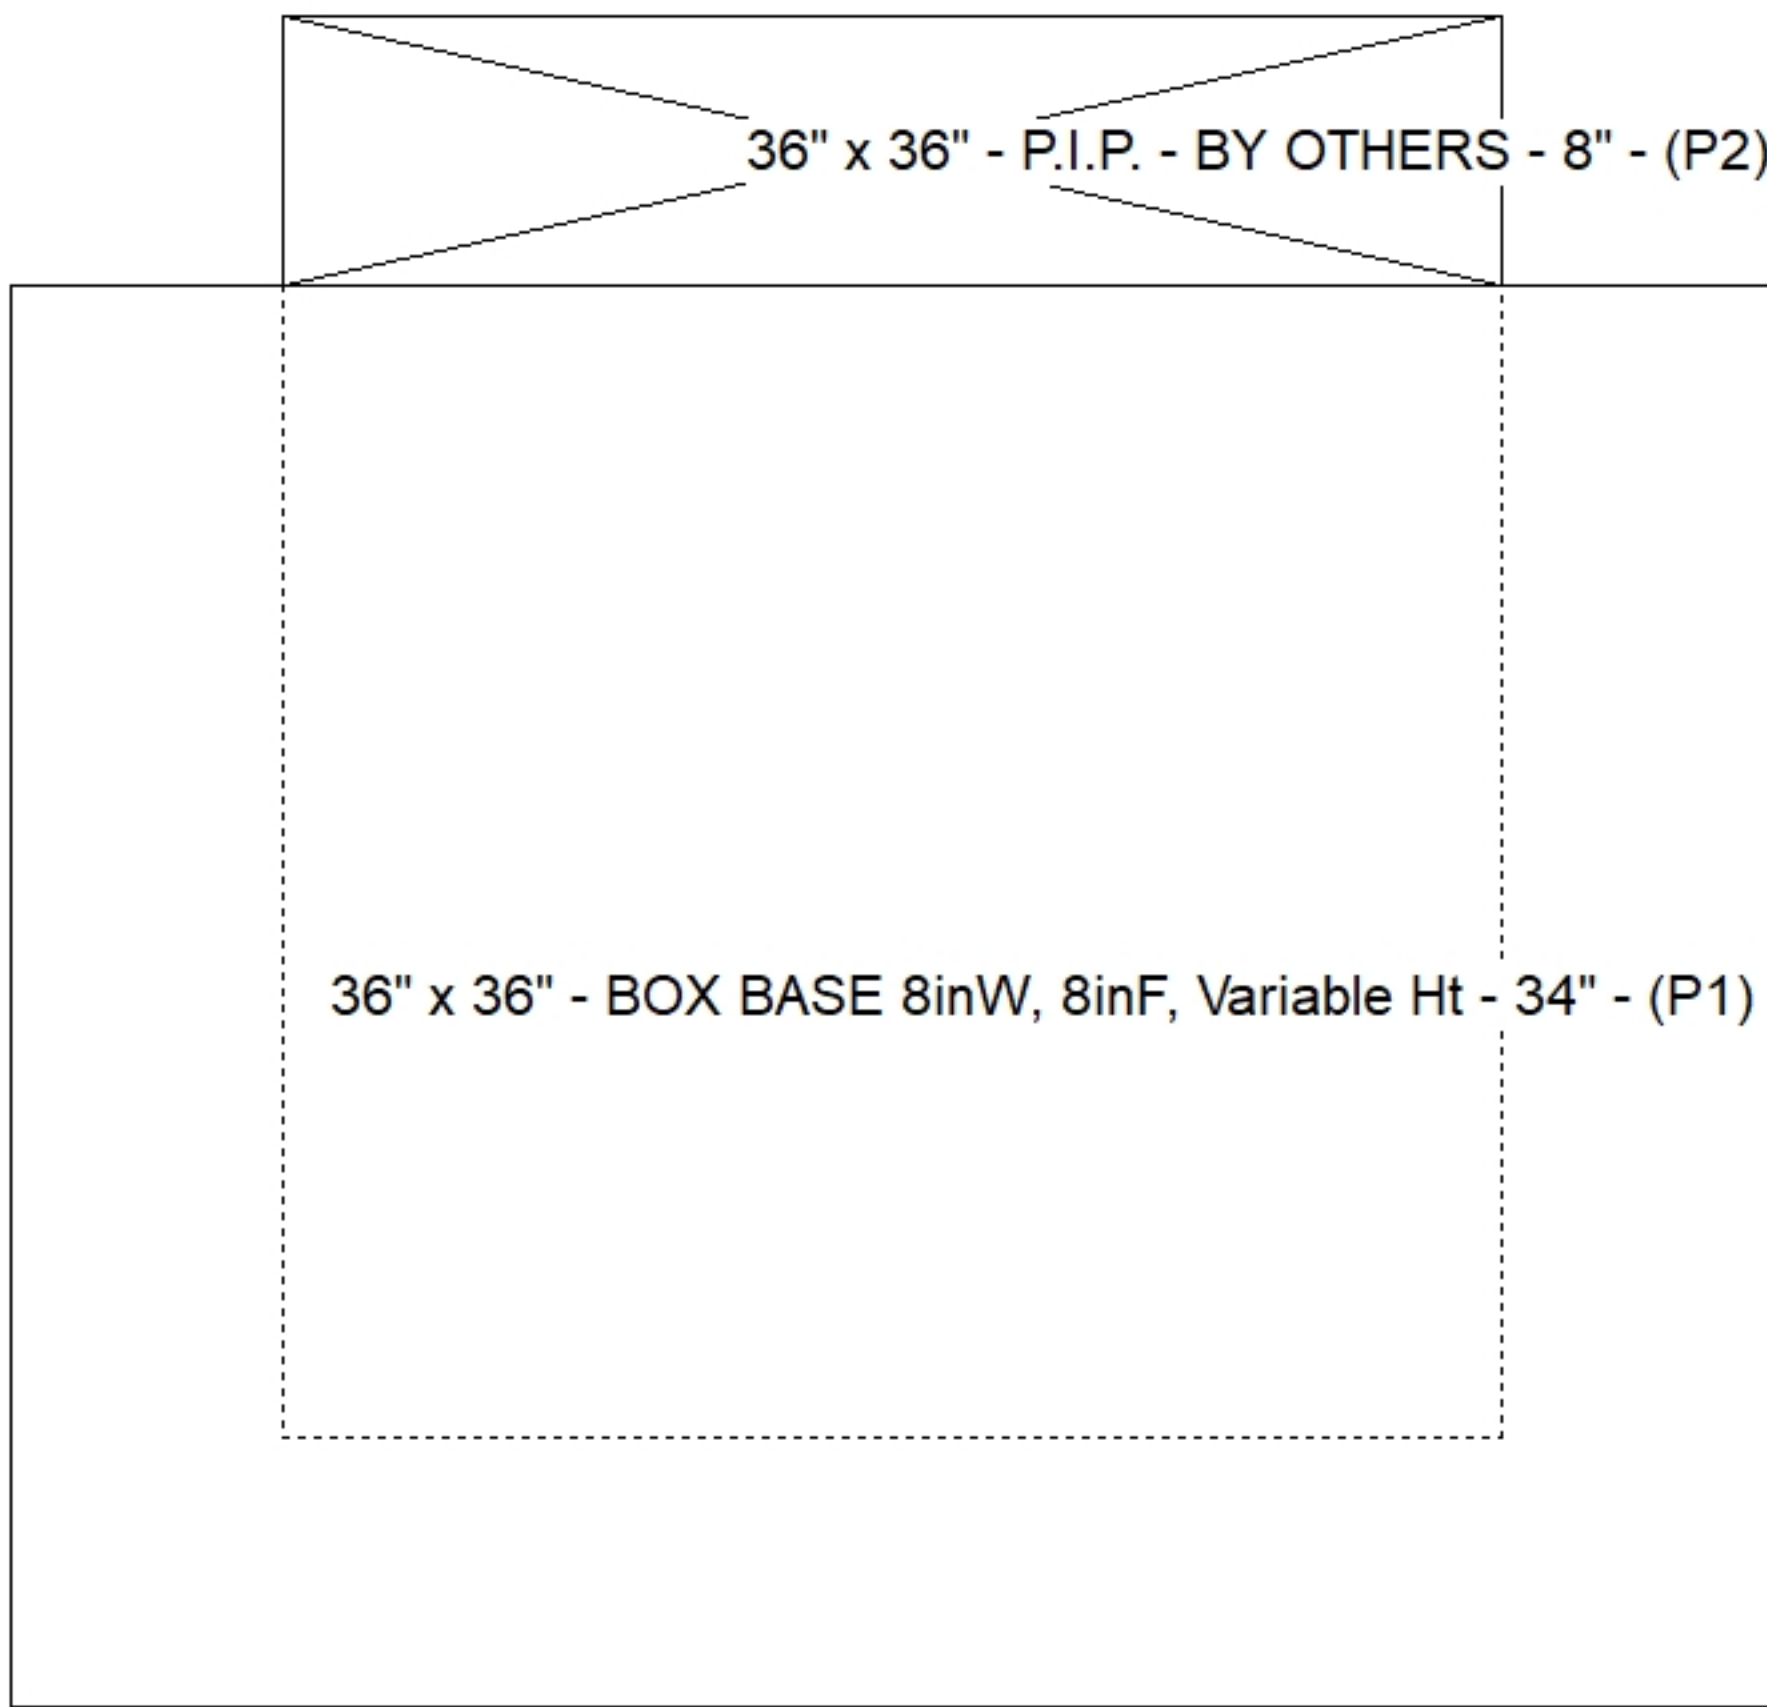

Submittal Drawing
8/17/2026 2:01:26 PM

SUBMITTAL
APPROVED BY:
