



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 8/12/2026 11:09:09 AM		Tech: Jared - F PC: T. Ryan			
Structure ID: 50650-121 DBI3										
P1 BX3636-08BAVF					BOX BASE 8inW, 8inF, Variable Ht F/n					
P2) 36" x 36" - P.I.P. - BY OTHERS - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 33" 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 5543 lb 0 lb 0 lb ----- 5543 lb Structure Total:		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 805.22' Rim to Invert: 3.45' Slack: 0.4" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	801.77'	0°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

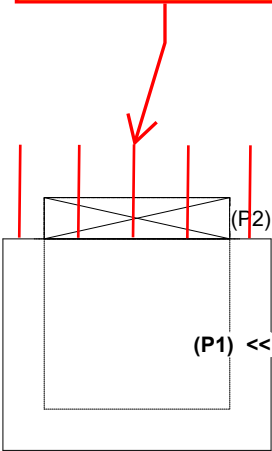


RIGHT-SIDE UP VIEW (int. dimensions)

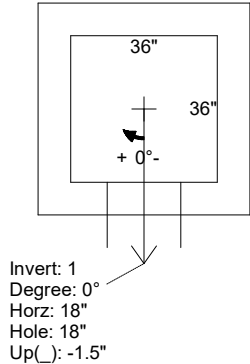

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

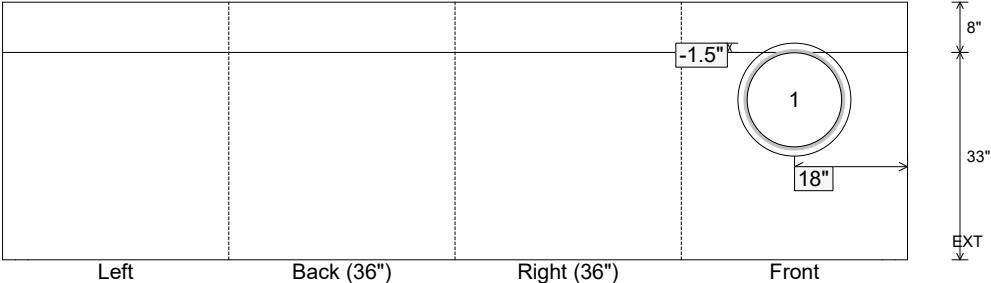

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 5543 lb Volume (Net): 1.42cu.yd
----------------------------------	-------------------------------	--	--	--
