

Contractor: Triton Construction, Inc.

Plant: Beaver Dam



Type: SAN.MH w/ConBlock-CDA Red
Size: 48"


Rim to Invert: 8.43'

Floor Height: 8"


Slack: 0.16"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total:	10955 lb
------------------	----------

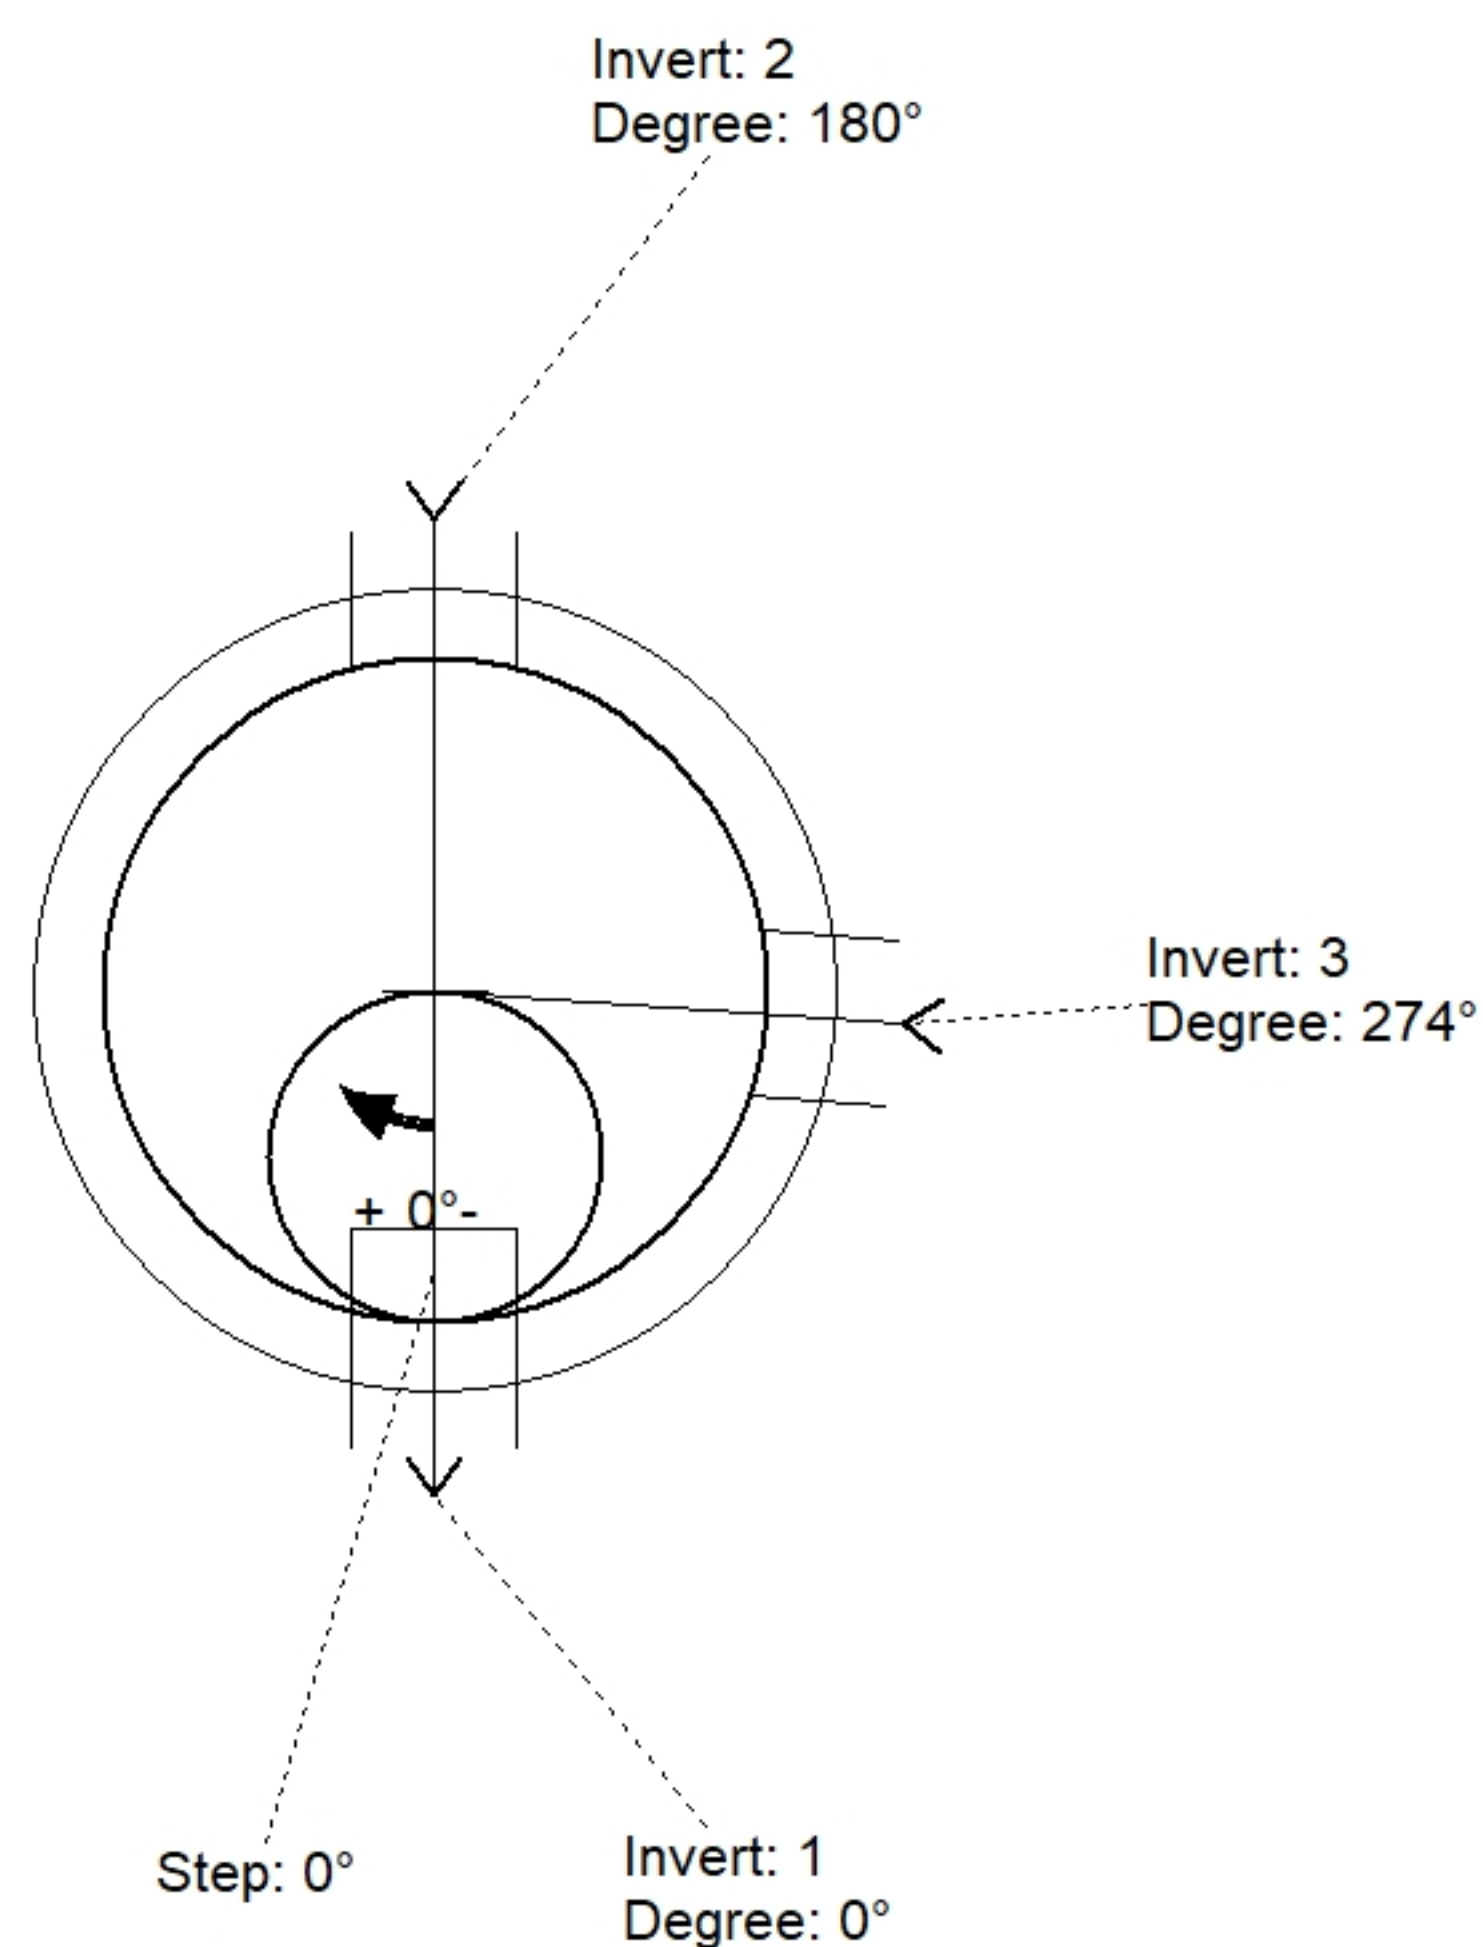

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	744.08'							
Reducer								
Invert 1	735.65'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	735.75'	180°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3	735.75'	274°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

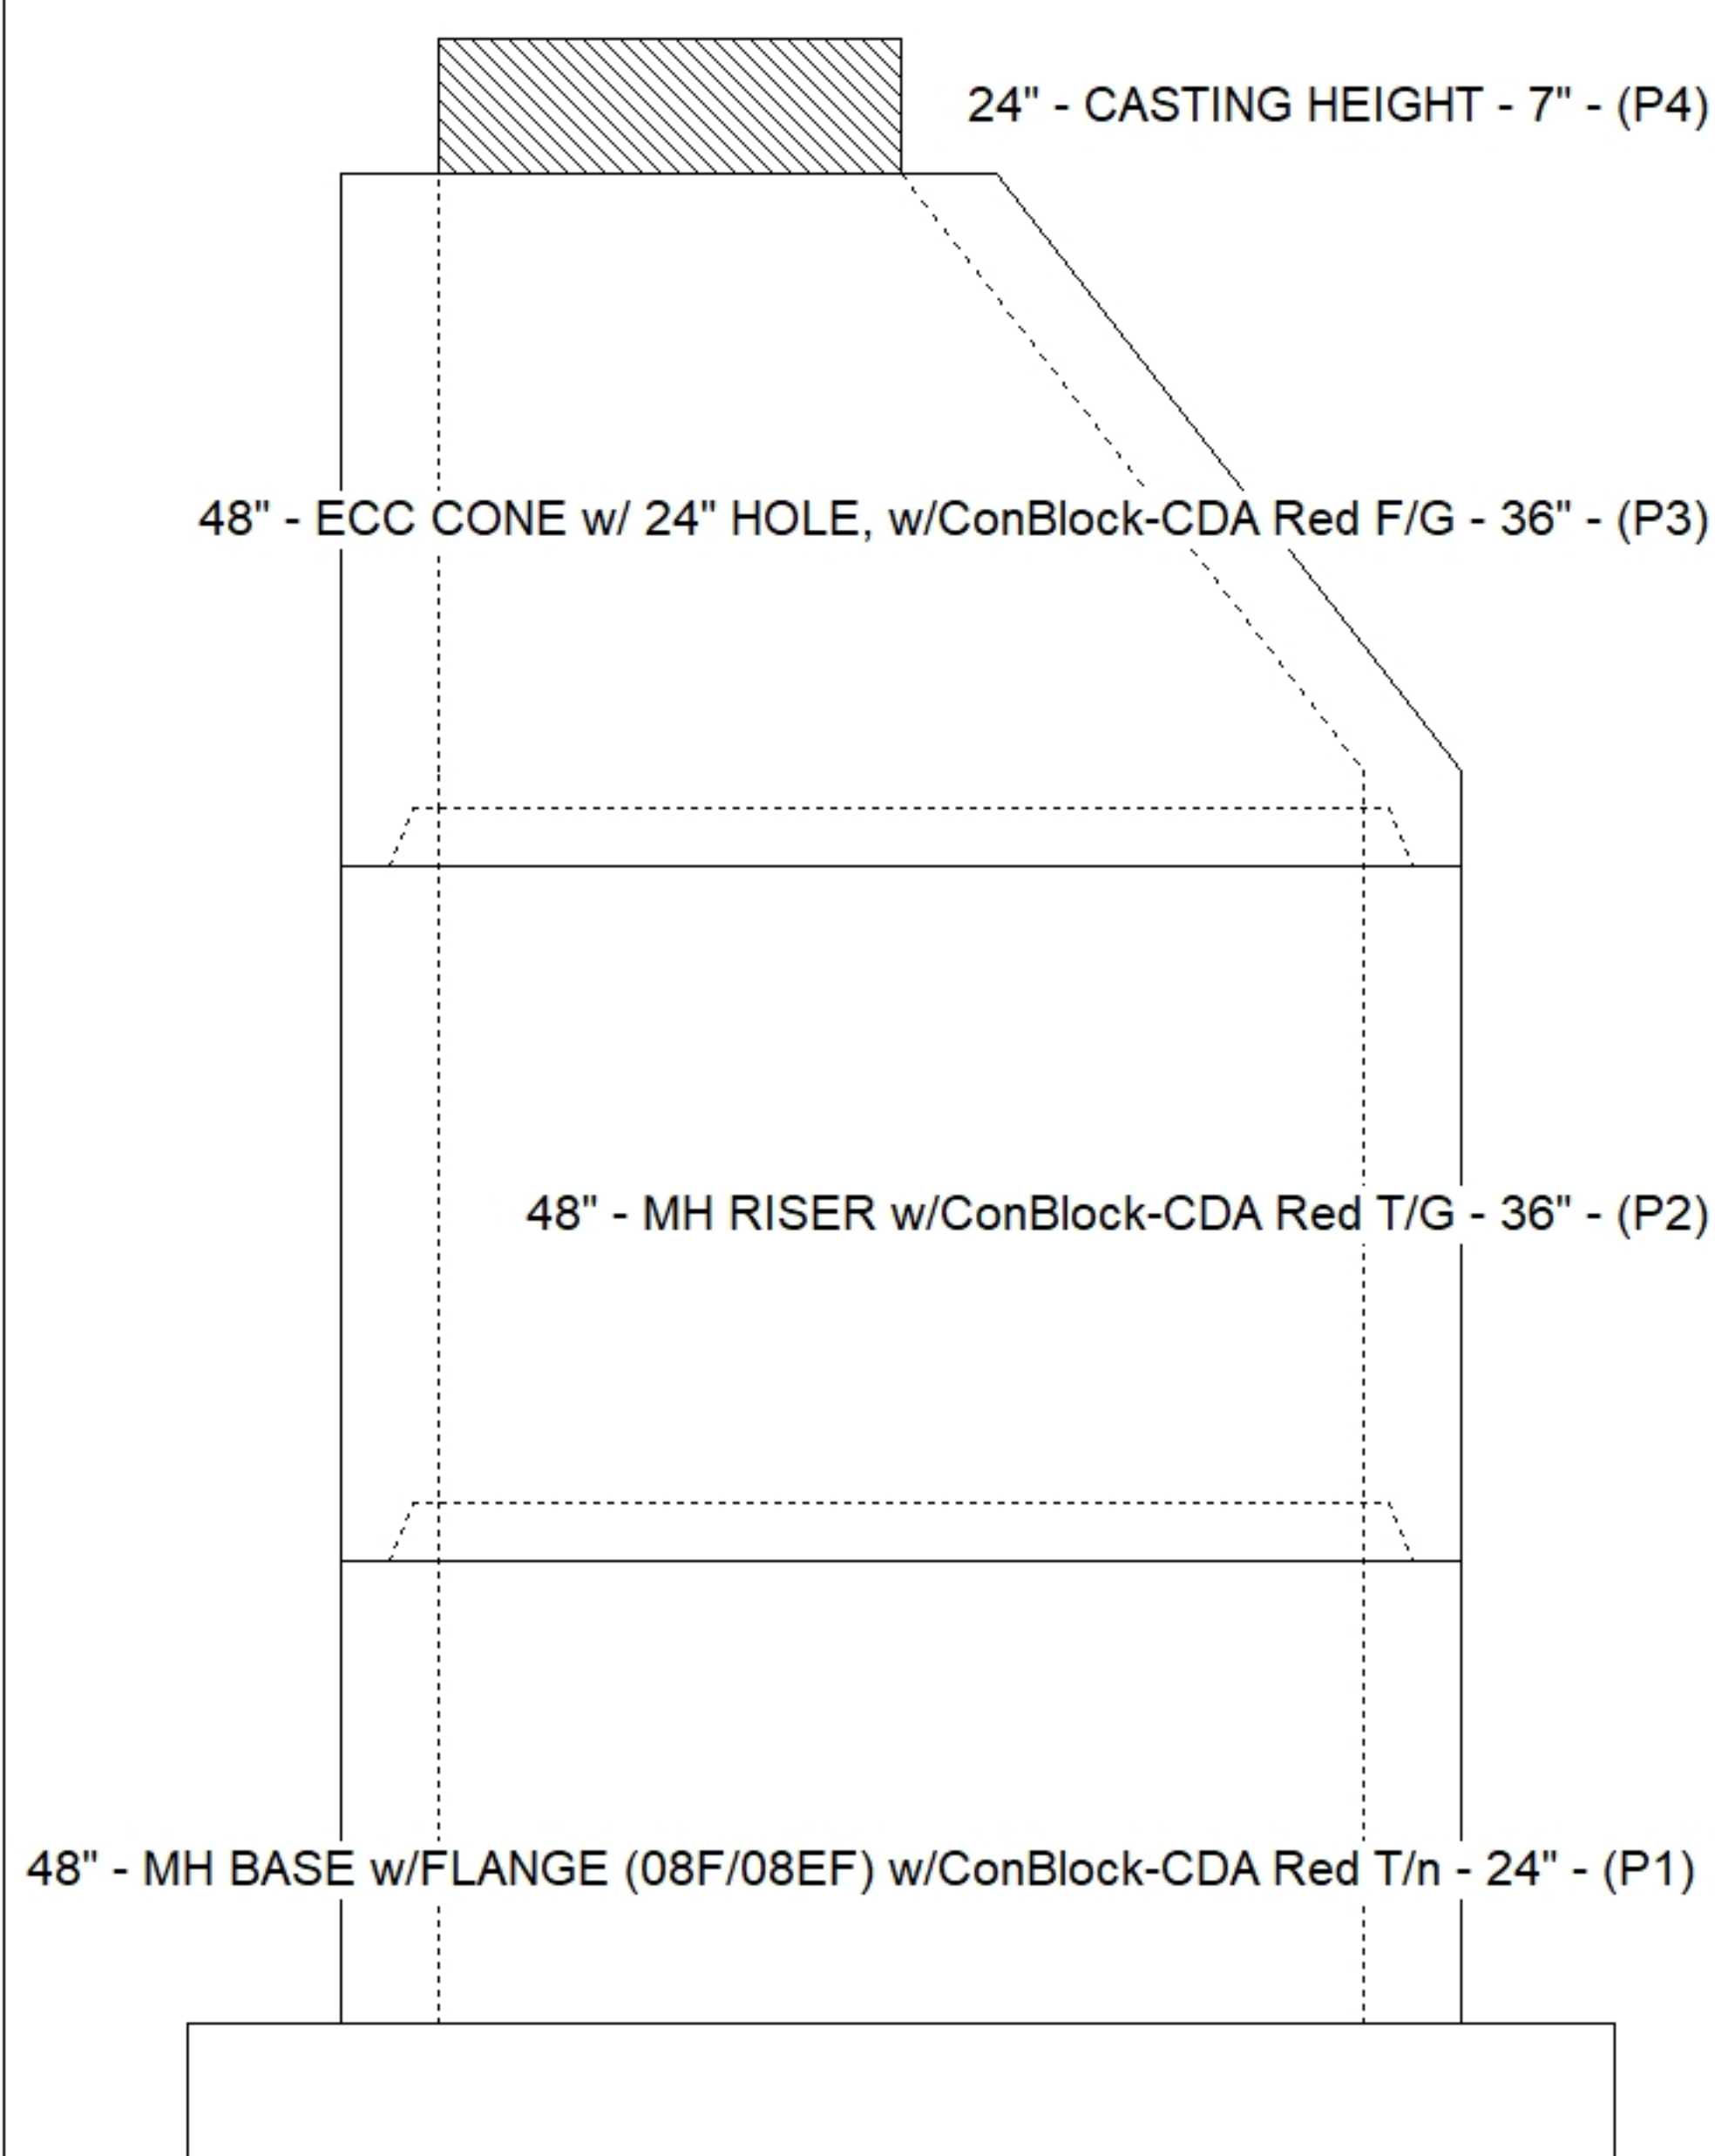

SUBMITTAL
APPROVED BY:
