

Job Name: 26-1644 - BGMU Miox Feed Lines
Job Location: Bowling Green, KY
Contractor: Scott & Ritter, Inc.

PC: C. Goff
 TECH: Jared - F
 Plant: 100



Structure ID: **JB #4**
 Spec: Custom Slabs
 Type: Cust. Top Slab
 Size: 72" x 72"

Rim: 1'
 Invert: 1'
 Rim to Invert: 0'

Sump: 0"
 Floor (Top): 0'
 Floor Height: 0"


Floor (Bot): 0'
 Overall Height: 1'
 Slack: 0"

Structure Notes:
 1. PER ASTM C913 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS & NO INVERT CHANNEL.
 4. CASTING BY ICAST (PAMREX 36" F/C)



REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..

STRUCTURE SUMMARY:

P2) 36" - CASTING (cast in) - 0"	0 lb
P1) 72" x 72" - 72IN X 72IN OD FLAT TOP SPEC. (w/ CASTING CAST IN) - 12"	4197 lb
1) CASTING - PAMREX 36" F/C	393 lb
1) 36" - Conseal CS-102 1.00"	0 lb
Structure Total:	4590 lb

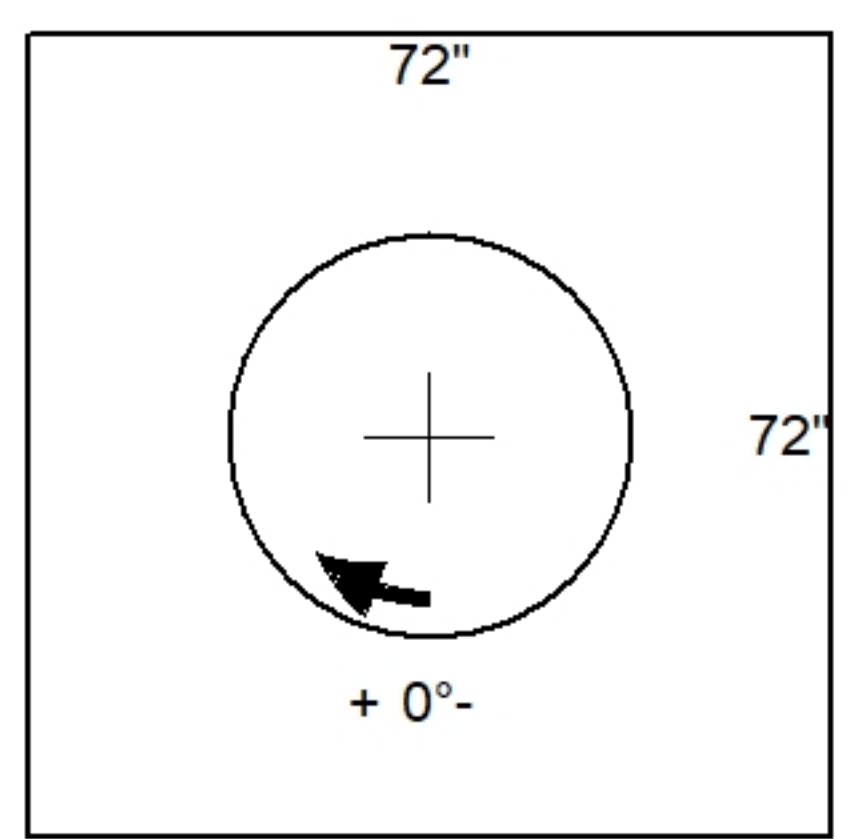

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

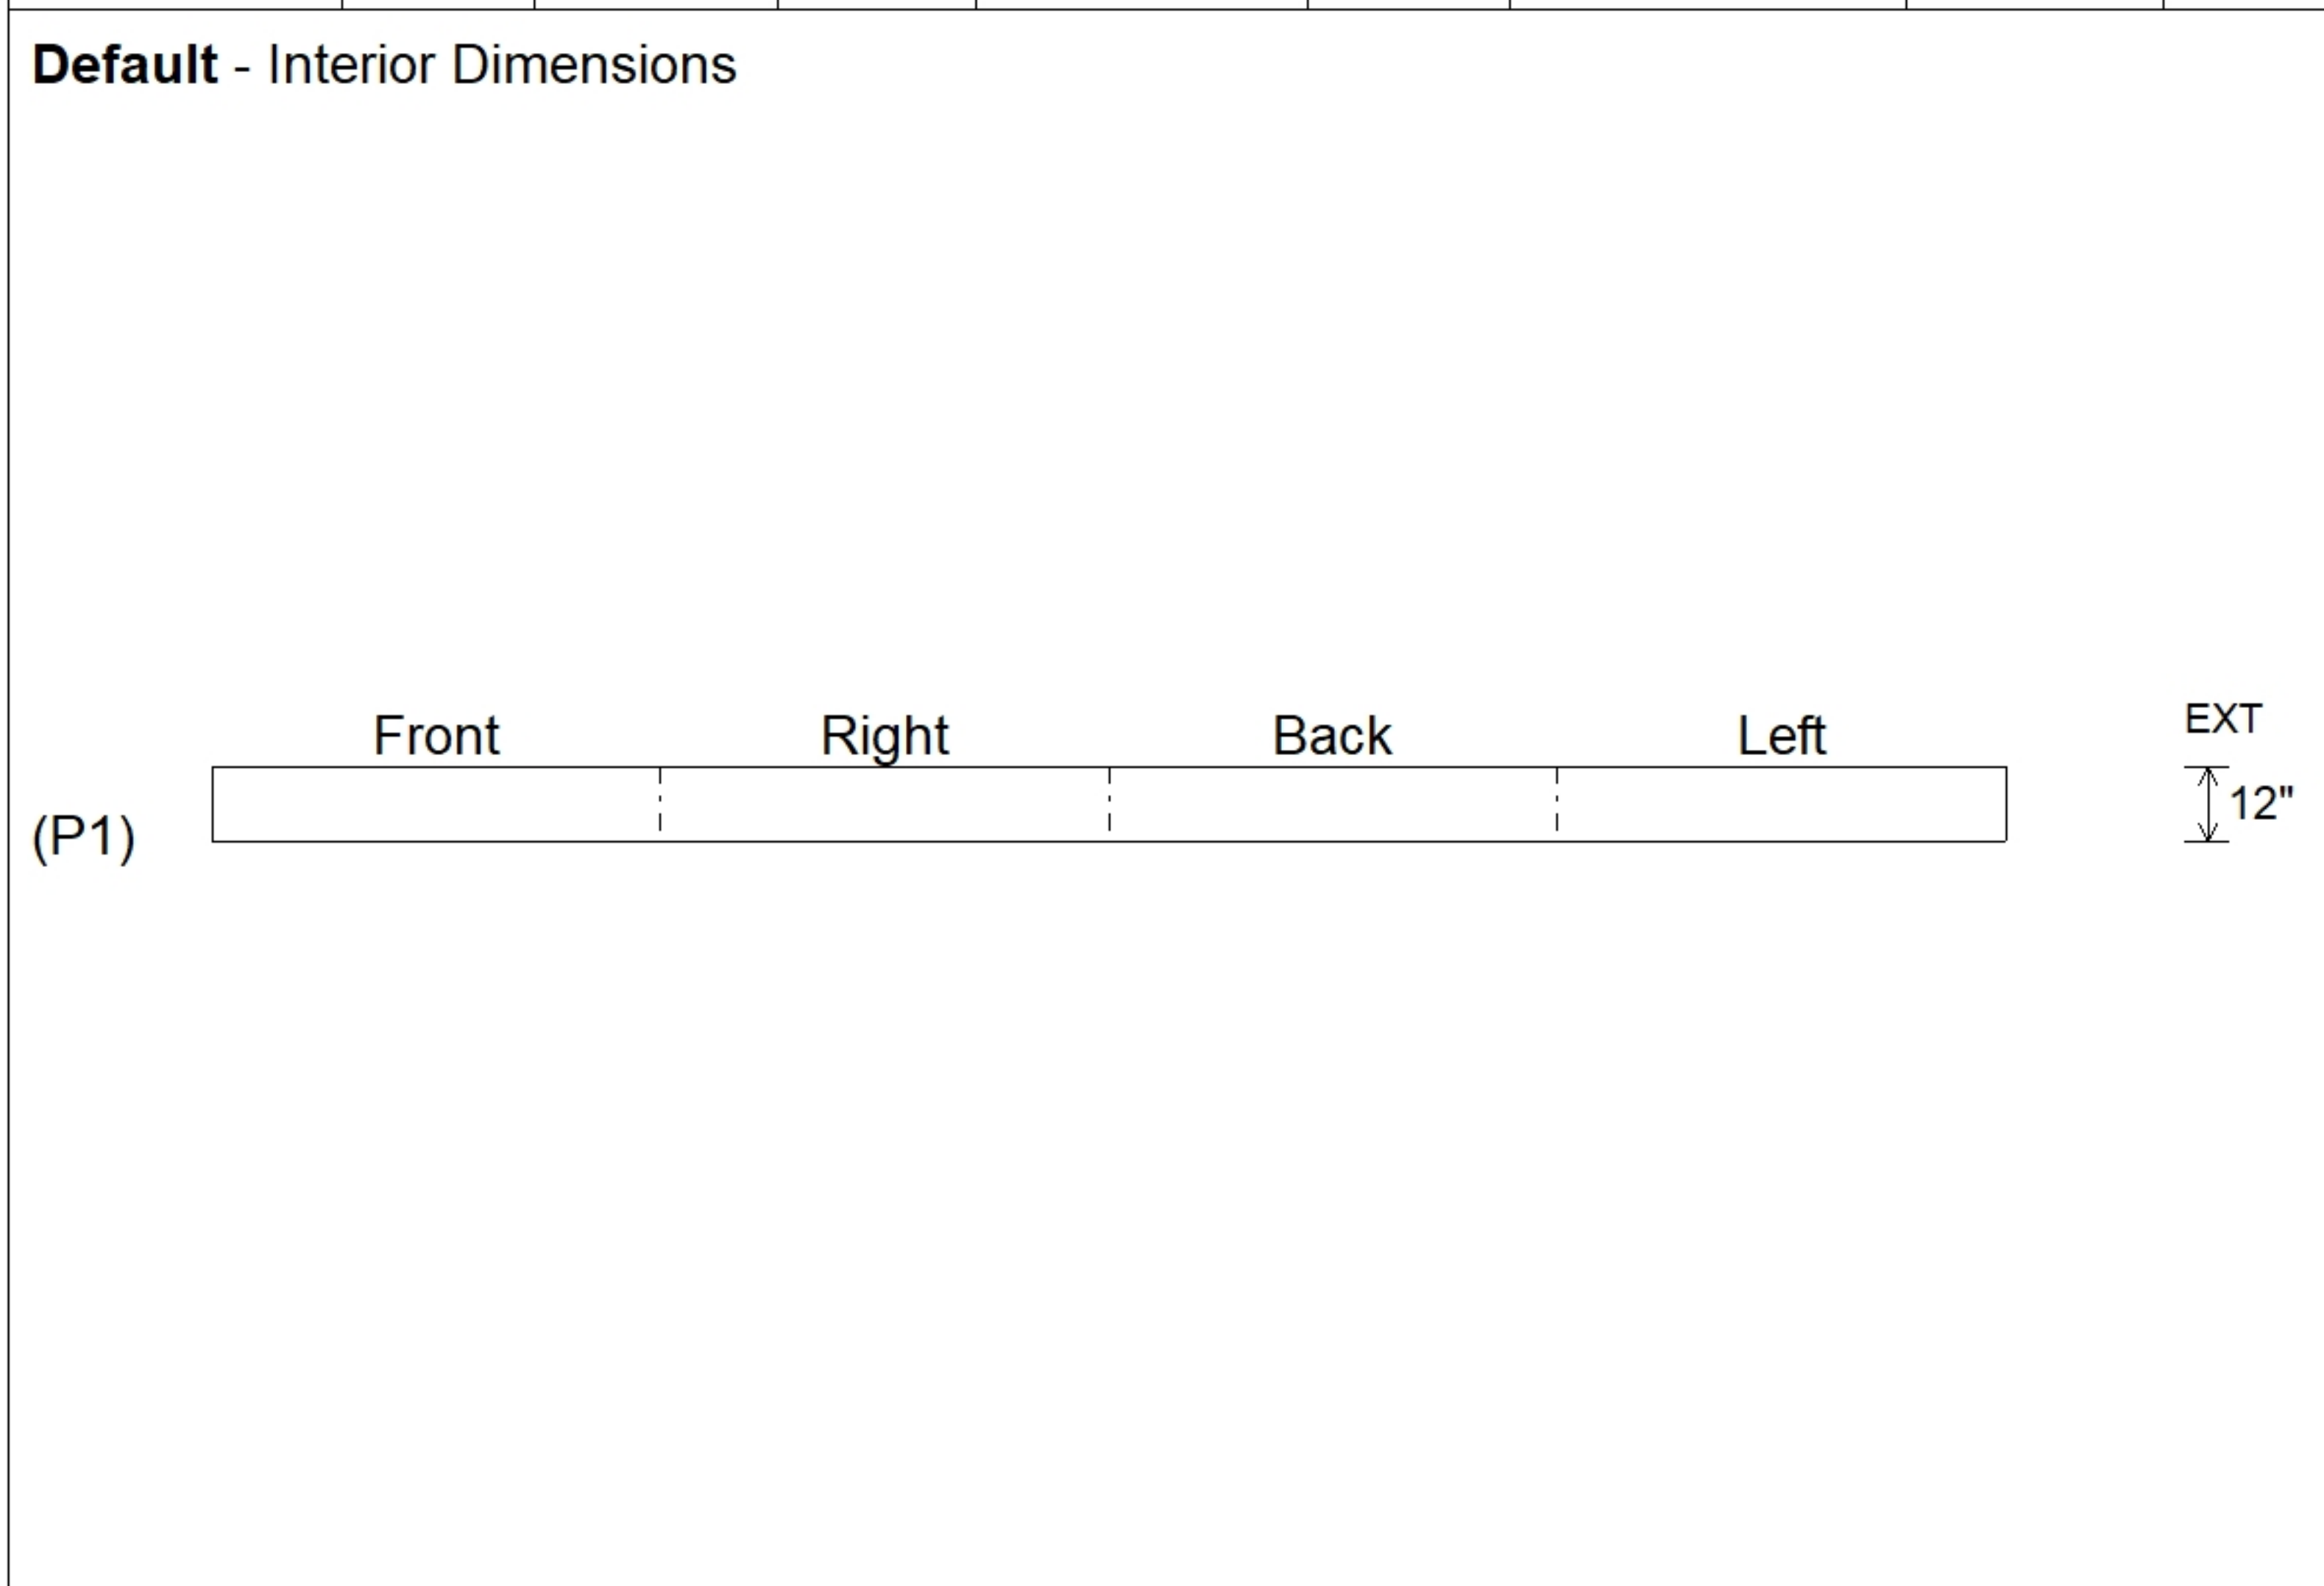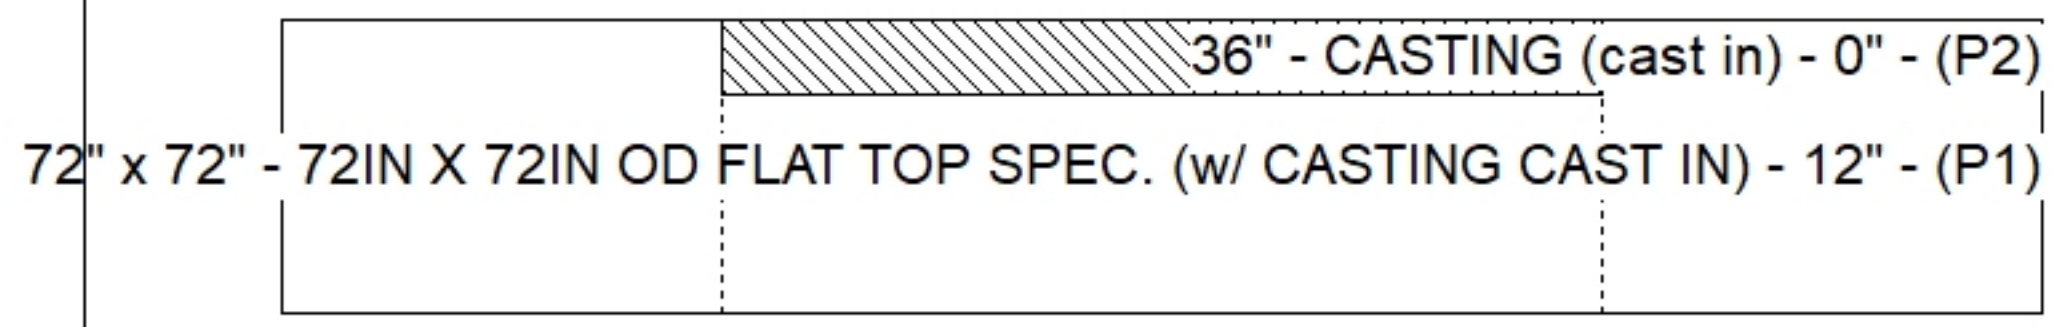

Submittal Drawing
 3/31/2026 10:59:08 AM

SUBMITTAL
 APPROVED BY:
