

Job Name: 26-1651B Buffalo Trace
Job Location: Campbellsville, KY
Contractor: Buzick Construction

Plant: Beaver Dam
6/26/2026 2:23:09 PM

Tech: S. Felletter
PC: E. Bradley



Structure ID: CB 791.43 - TOP

P1 MH048LD07S

MH FLAT TOP w/34"x34" Hole F/F

P2) 34" x 34" - CASTING HEIGHT - 3"
P1) 48" - MH FLAT TOP w/34"x34" Hole F/F - 7"
1) CASTING - HOE 595 F/G


0 lb
873 lb
376 lb
Structure Total: 1249 lb

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE 595 F/C).


REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

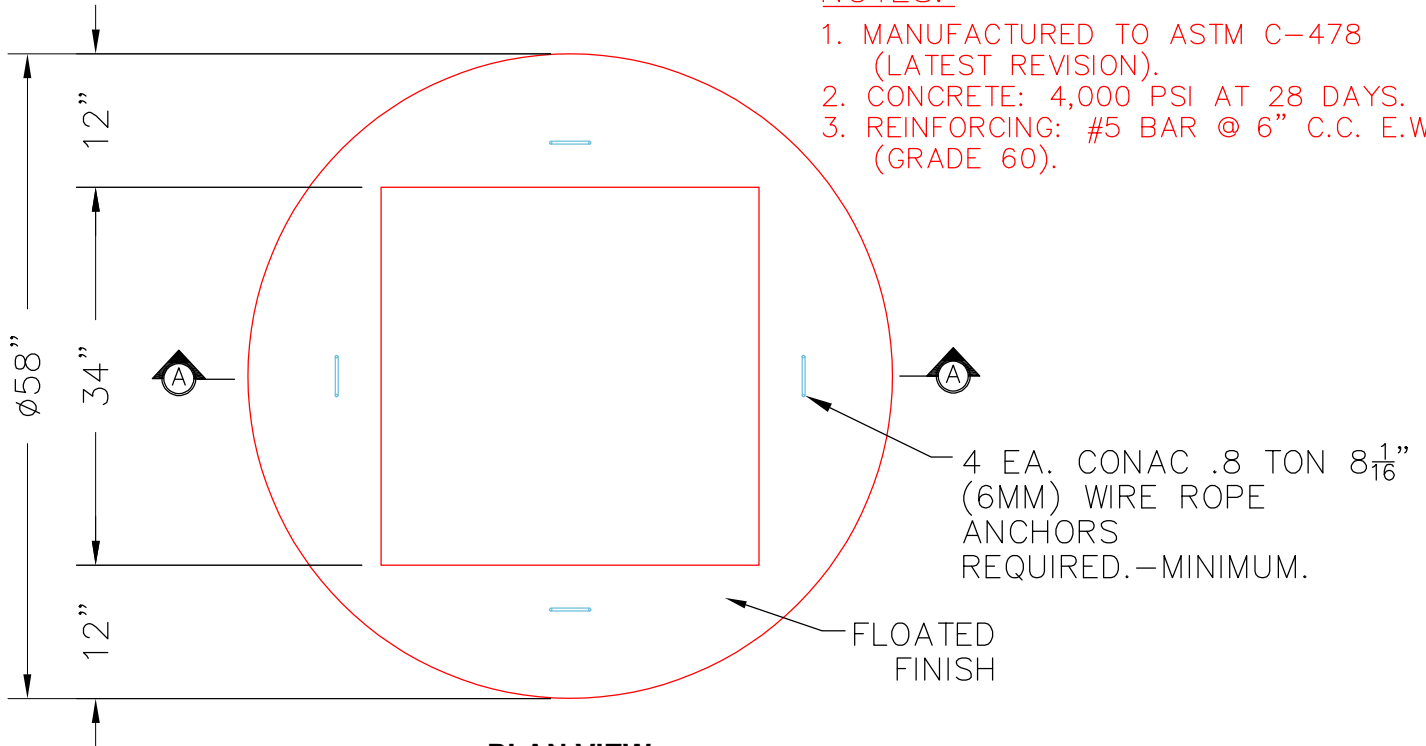

PLAN VIEW

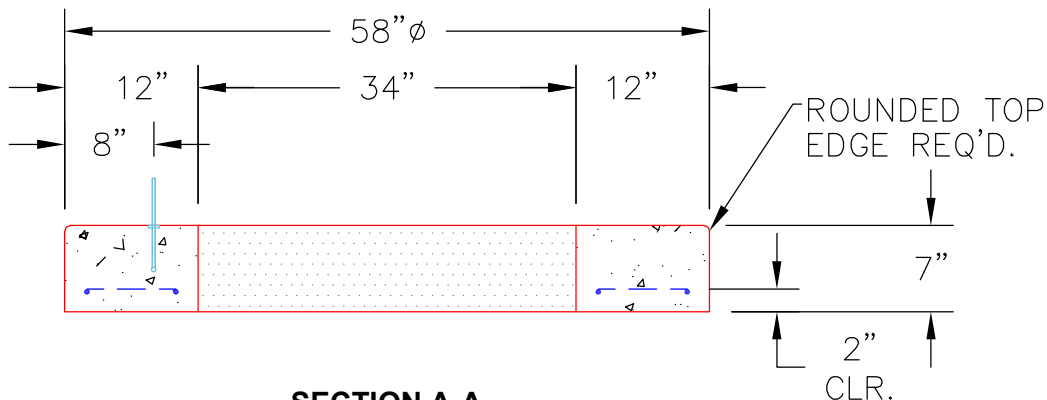

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 873 lb
Volume (Net): 0.22cu.yd
