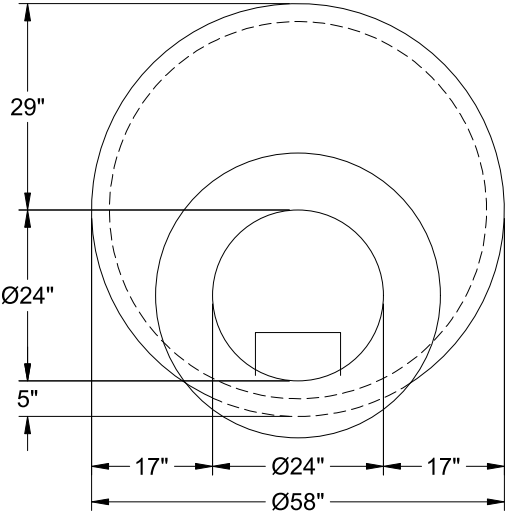



Job Name: 26-1715 - Christian Co HS Sewer Job Location: Hopkinsville, KY Contractor: West Kentucky Industrial & Plumbing		Plant: 100 6/8/2026 4:06:11 PM	Tech: Jared - A PC: T. Lewis	
Structure ID: 3 SS-MH				
P3 MH048CN30CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 18" 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1140 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 DD (DBL Bands) 1) PSX - 8QRS DD (DBL Bands) 7) MH Step ML-10-TDS-NCR - 10"		0 lb 1961 lb 2515 lb 2519 lb 0 lb 0 lb 1440 lb 0 lb 250 lb 0 lb 0 lb 8 lb 6 lb 0 lb 8699 lb	<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. CONBLOCK CDA RED ADMIXTURE REQUIRED 6. JBS 1140 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1961 lb Volume (Net): 0.5cu.yd
