

Job Name: 26-1733 - Liberty Power Station
Job Location: Liberty, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/20/2026 8:30:30 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: CB-22

P2 MH060LD08CC

MH FLAT TOP w/24" Ctr. Hole



- P3) 24" - CASTING HEIGHT - 4"
P2) 60" - MH FLAT TOP w/24" Ctr. Hole - 8"
P1) 60" - MH BASE Custom Ht - 70"
1) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 40
1) DOGHOUSE INVRTD - 18"x19"
6) MH Step ML-10-TDS-NCR - 10"

0 lb
2429 lb
8515 lb
0 lb
0 lb
0 lb
0 lb
0 lb

10944 lb

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Structure Total:

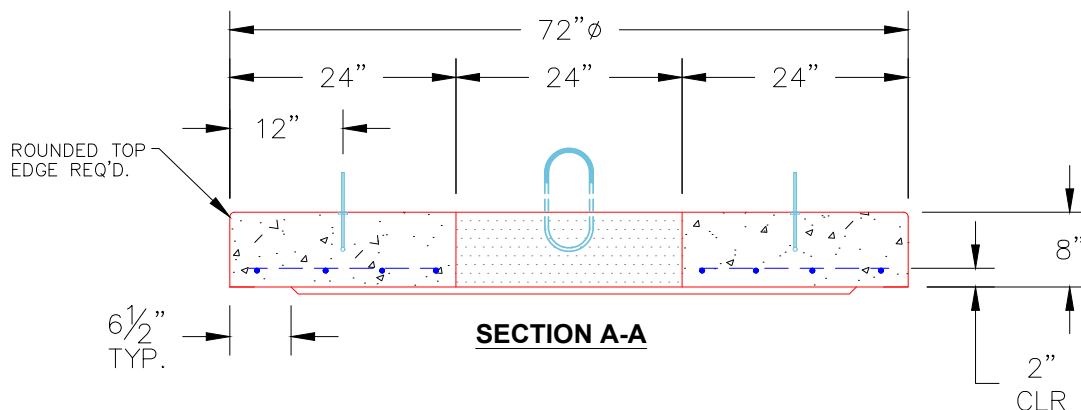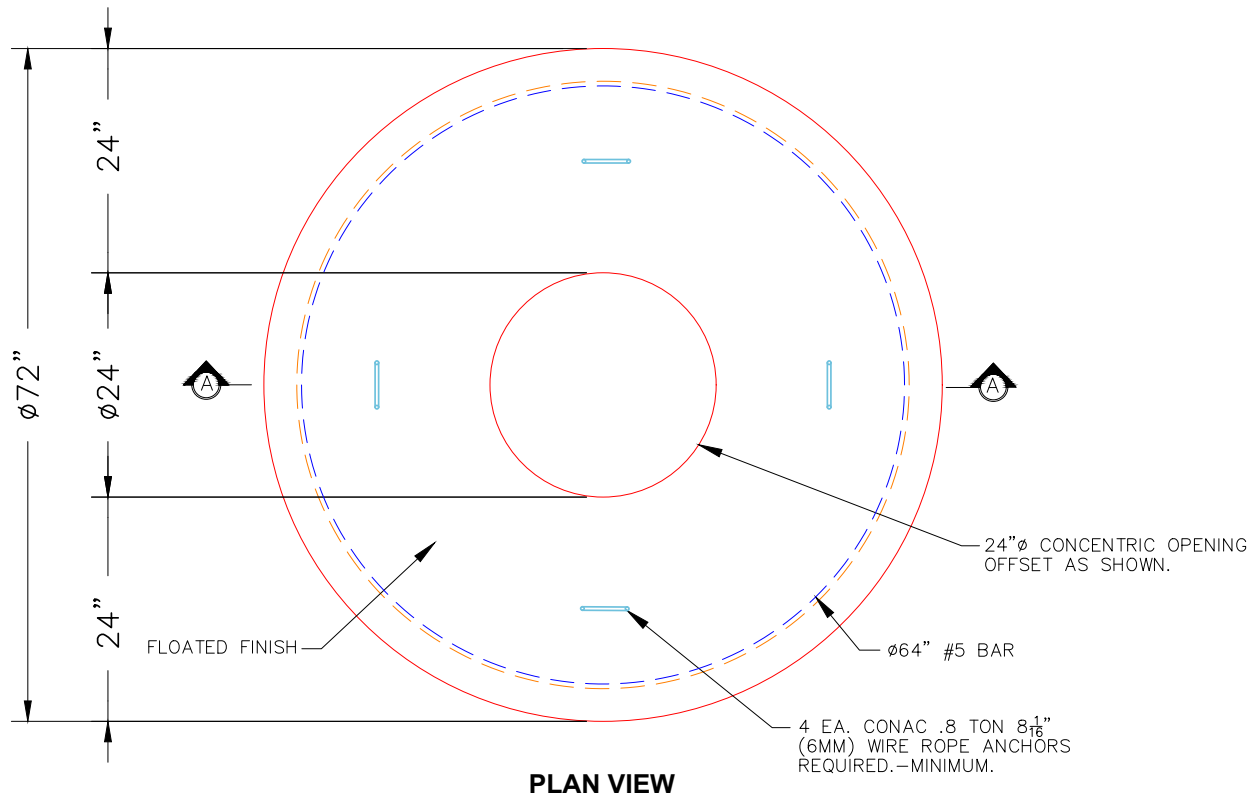

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 2429 lb
Volume (Net): 0.62cu.yd
