

Job Name: 26-1733 - Liberty Power Station
Job Location: Liberty, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/20/2026 8:30:32 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: CB-33

P2 MH048LD12CC


MH FLAT TOP w/ 24" Center Hole

- P3) 24" - CASTING HEIGHT - 4"
P2) 48" - MH FLAT TOP w/ 24" Center Hole - 12"
P1) 48" - MH BASE Custom Ht - 46"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 32
4) MH Step ML-10-TDS-NCR - 10"


Structure Total:

- 0 lb
1580 lb
3817 lb
0 lb
0 lb
0 lb
0 lb

5397 lb
- Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

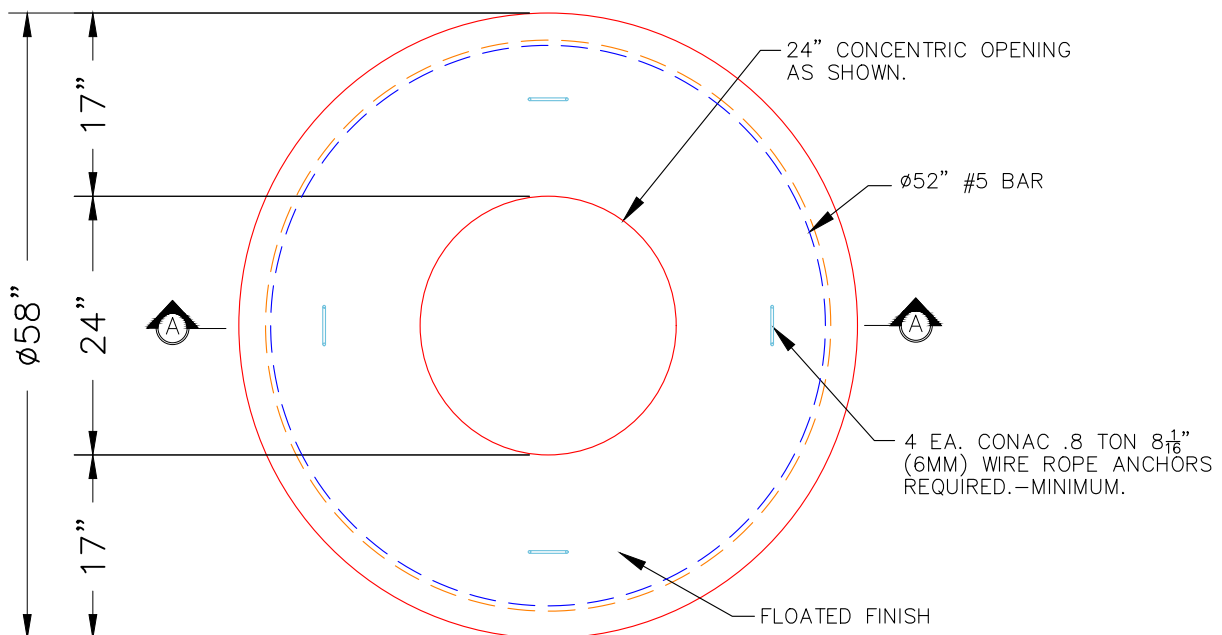

PLAN VIEW

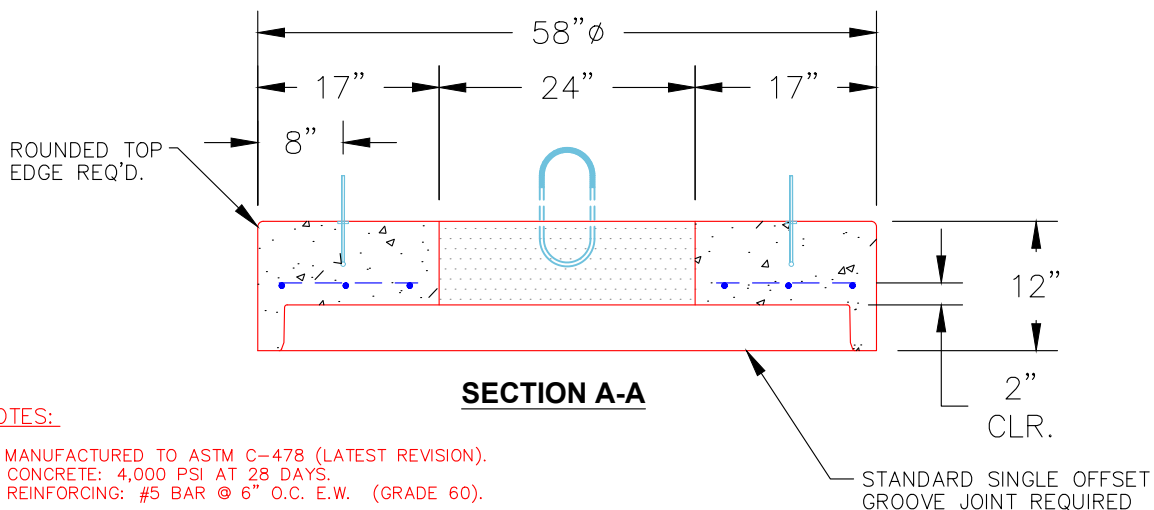

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1580 lb
Volume (Net): 0.39cu.yd
