

Contractor: Clarksville Gas and Water

TECH: Jared - F

Plant: 100



Size: 48" x 96"

Rim to Invert: 6'


Floor Height: 0"

Slack: 0"

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB(As.12) #5 BARS AT 6" C.C.E.W.
- WALLS(As.12) #5 BARS AT 8" C.C.E.W.


P4) 36" x 72" - HATCH (CAST FLUSH) - 3.5"	100 lb
P3) 48" x 96" - CB FLAT TOP 8"W w/36"x72" HATCH - 8"	3072 lb
P2) 48" x 96" - BOX RISER 8inW, Variable Ht - 64"	13058 lb
P1) 48" x 96" - P.I.P. BY OTHERS - BTM SLAB - 0"	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
2) 48" x 96" - Conseal CS-102 1.00" (Double)	0 lb
1) 36" x 72" - Conseal CS-102 1.00" (Double)	0 lb
2) DOGHOUSE - 16"x36"	0 lb

Structure Total: 16230 lb

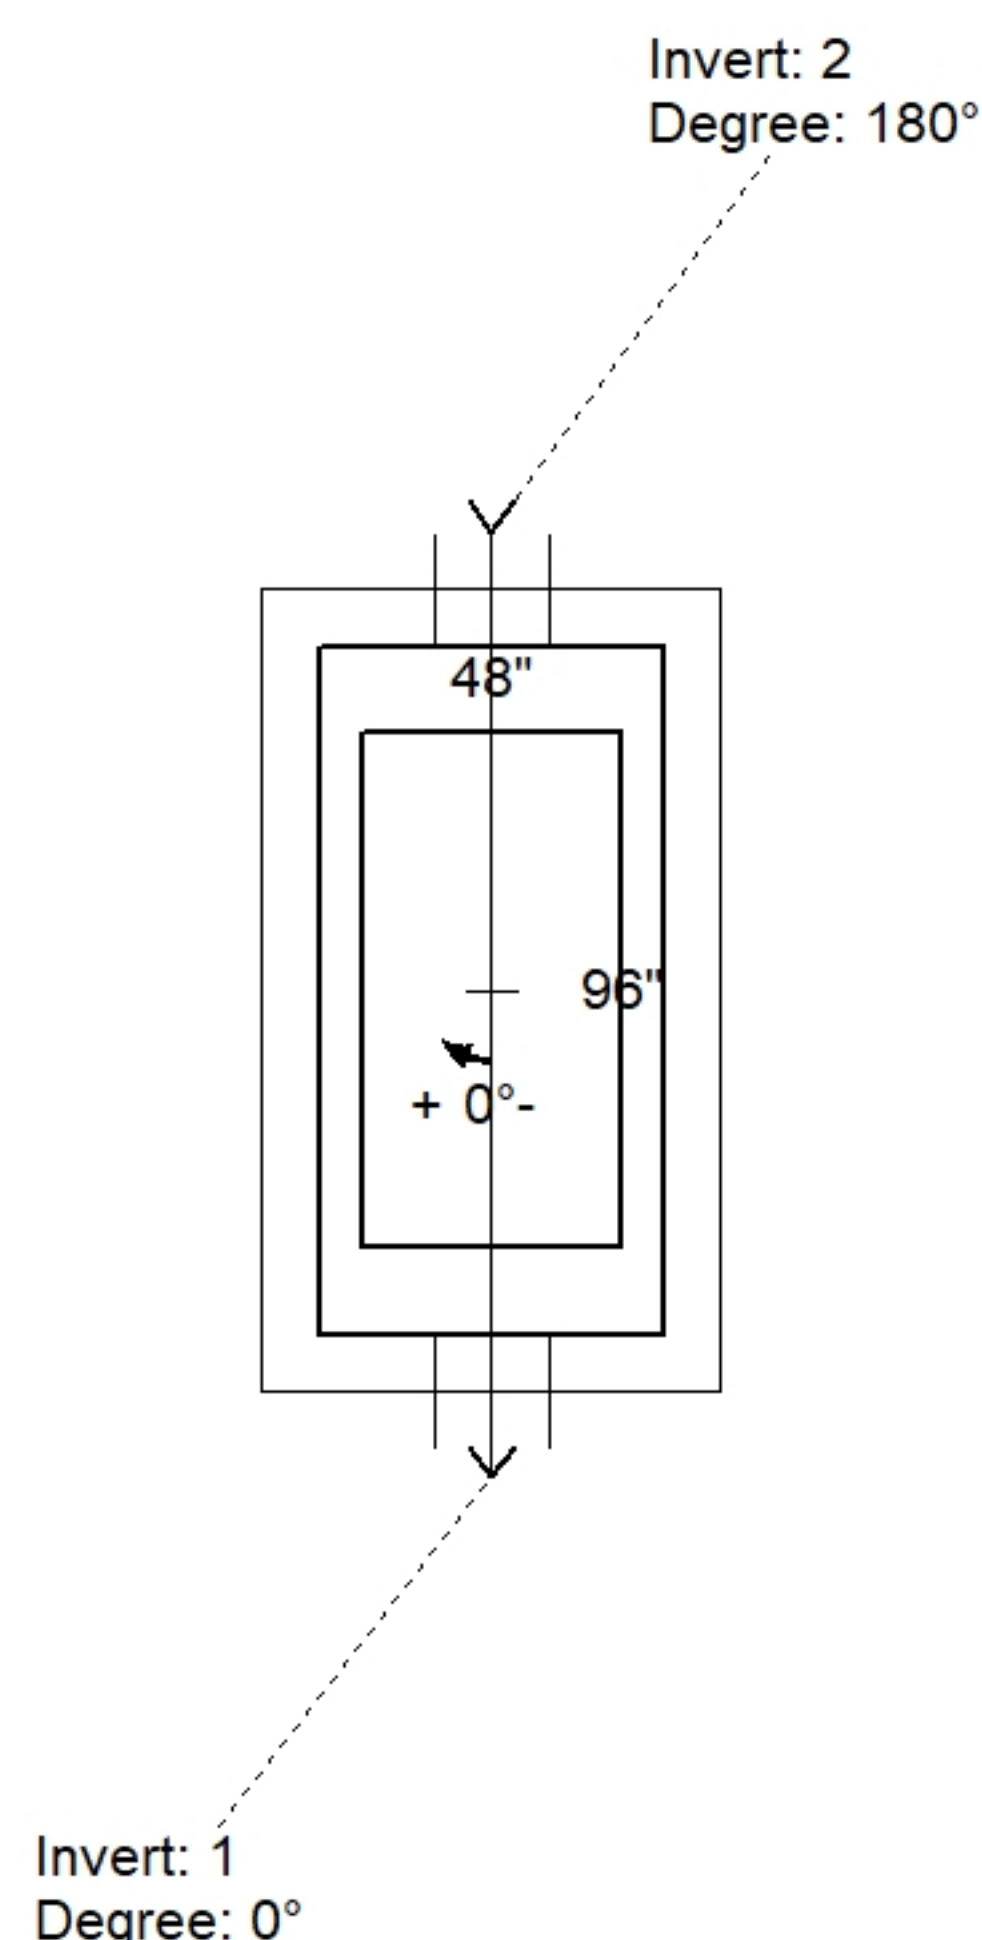


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	6'							
Reducer								
Invert 1	0'	0°	0" No Hole	0.01"	16" x 36"	DOGHOUSE 16"x36"	0"	P2
Invert 2	0'	180°	0" No Hole	0.01"	16" x 36"	DOGHOUSE 16"x36"	0"	P2
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

36" x 72" - HATCH (CAST FLUSH) - 3.5" - (P4)
48" x 96" - CB FLAT TOP 8" W w/36" x 72" HATCH - 8" - (P3)

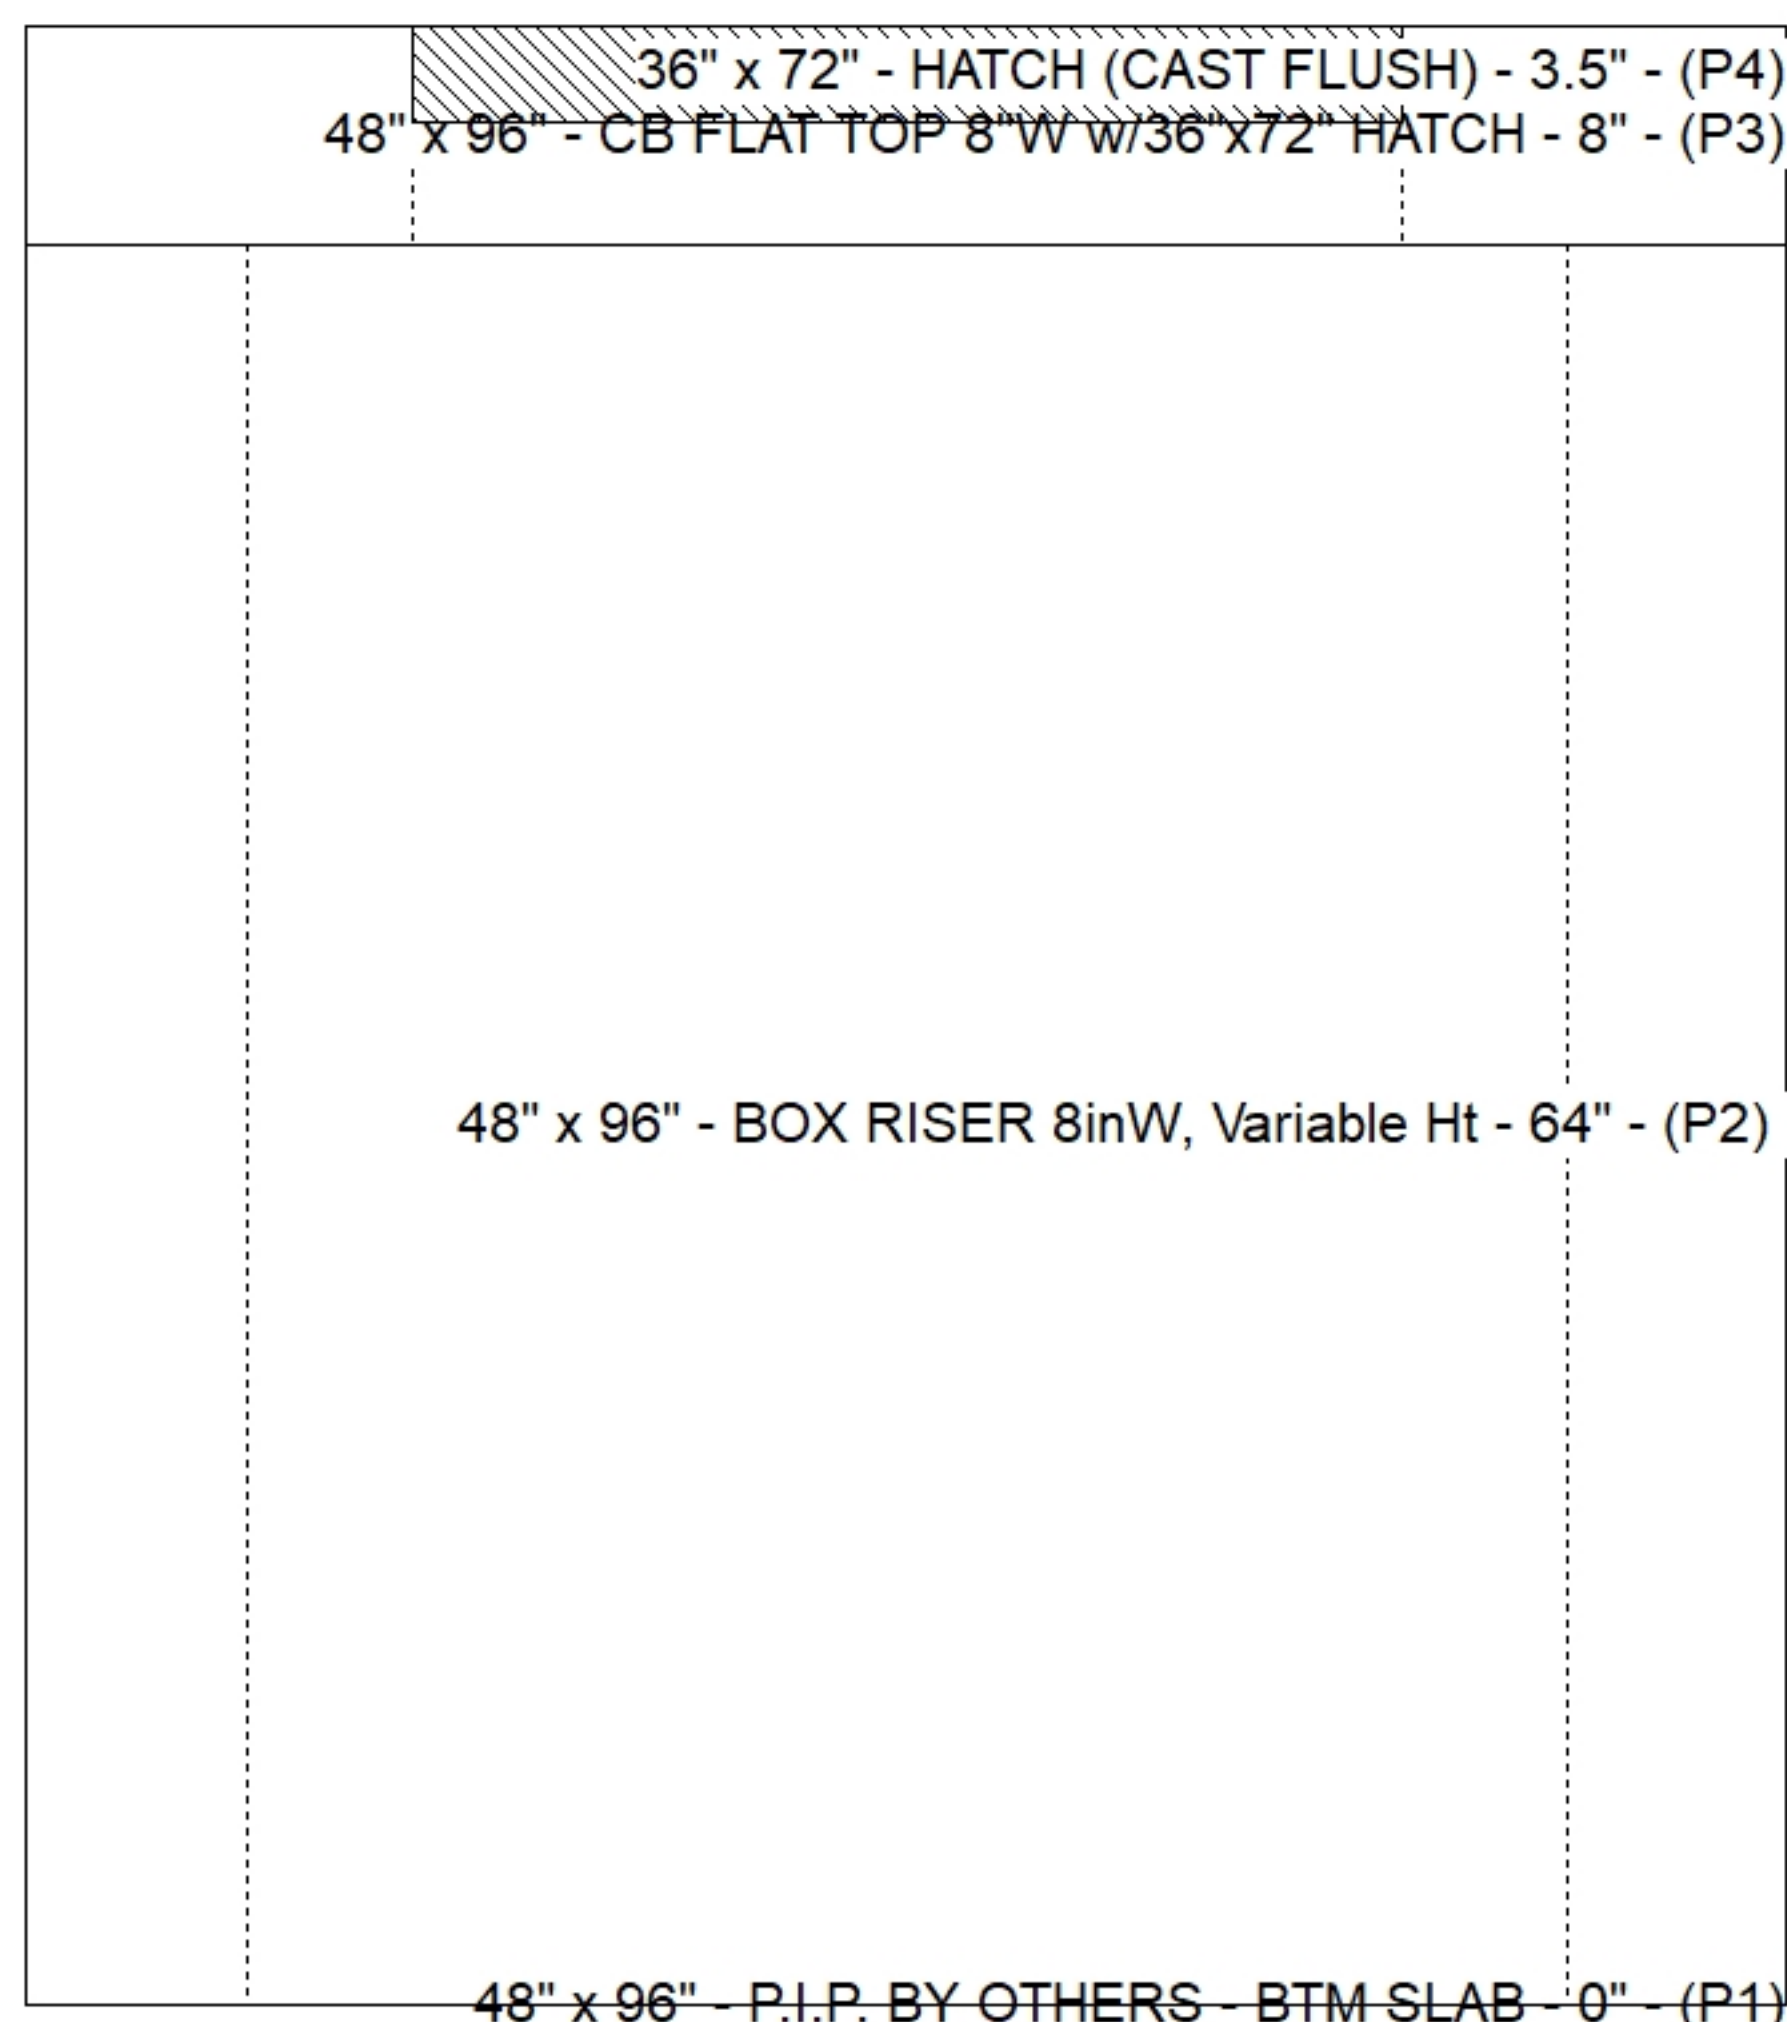

Default - Interior Dimensions

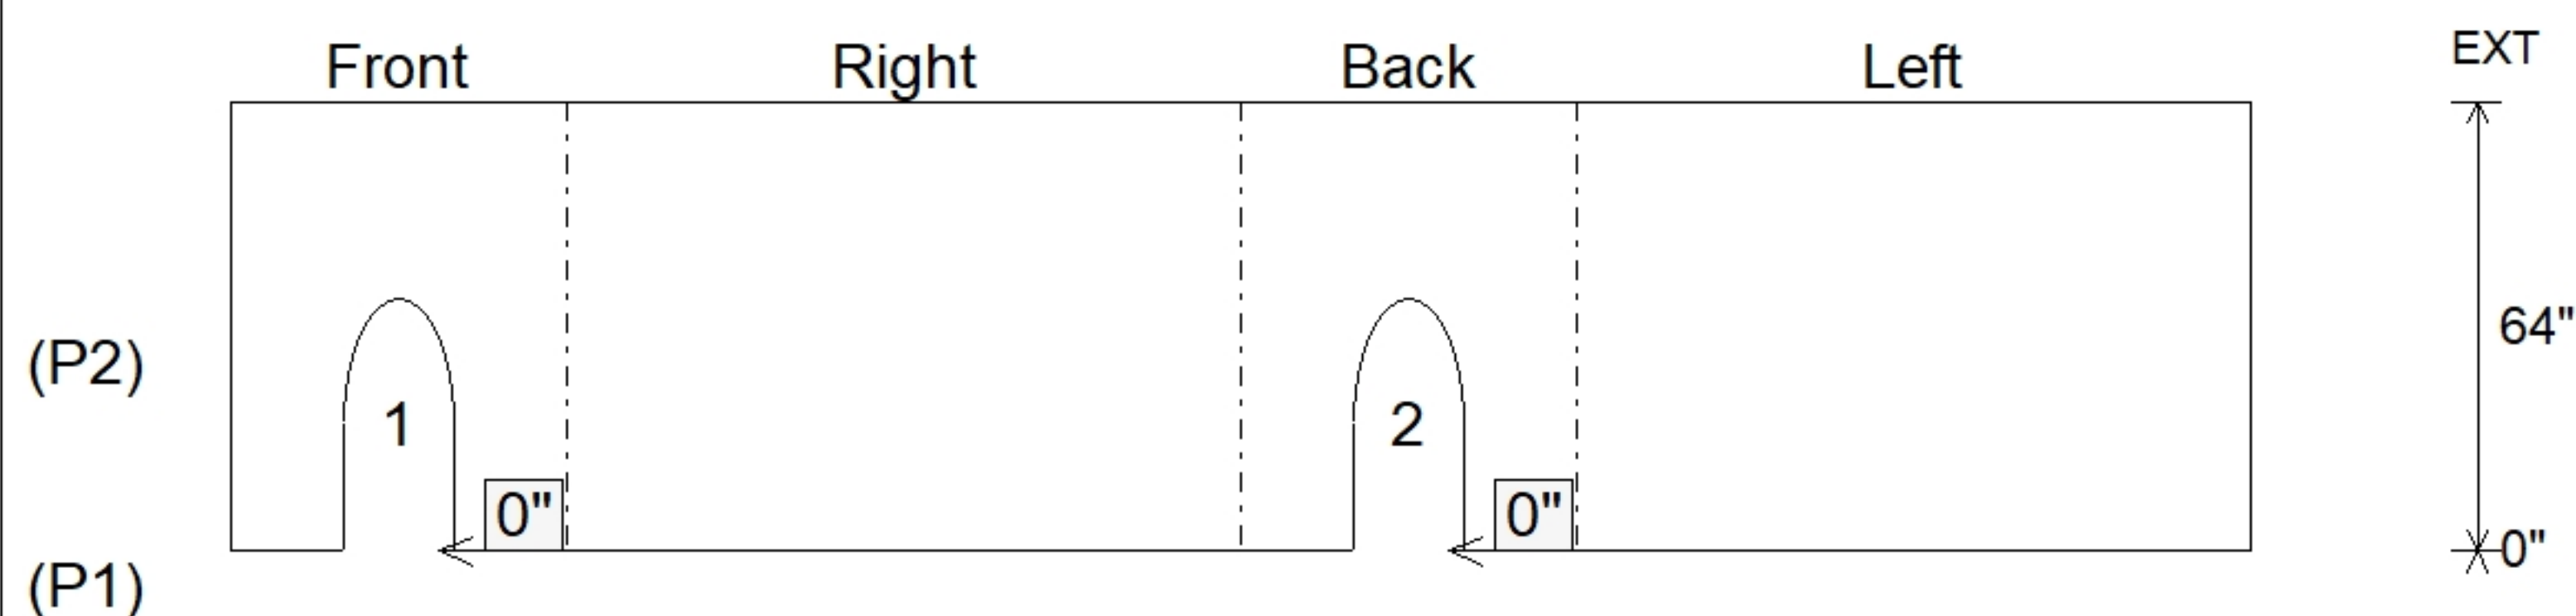

Submittal Drawing
8/13/2026 10:26:03 AM

SUBMITTAL
APPROVED BY:
