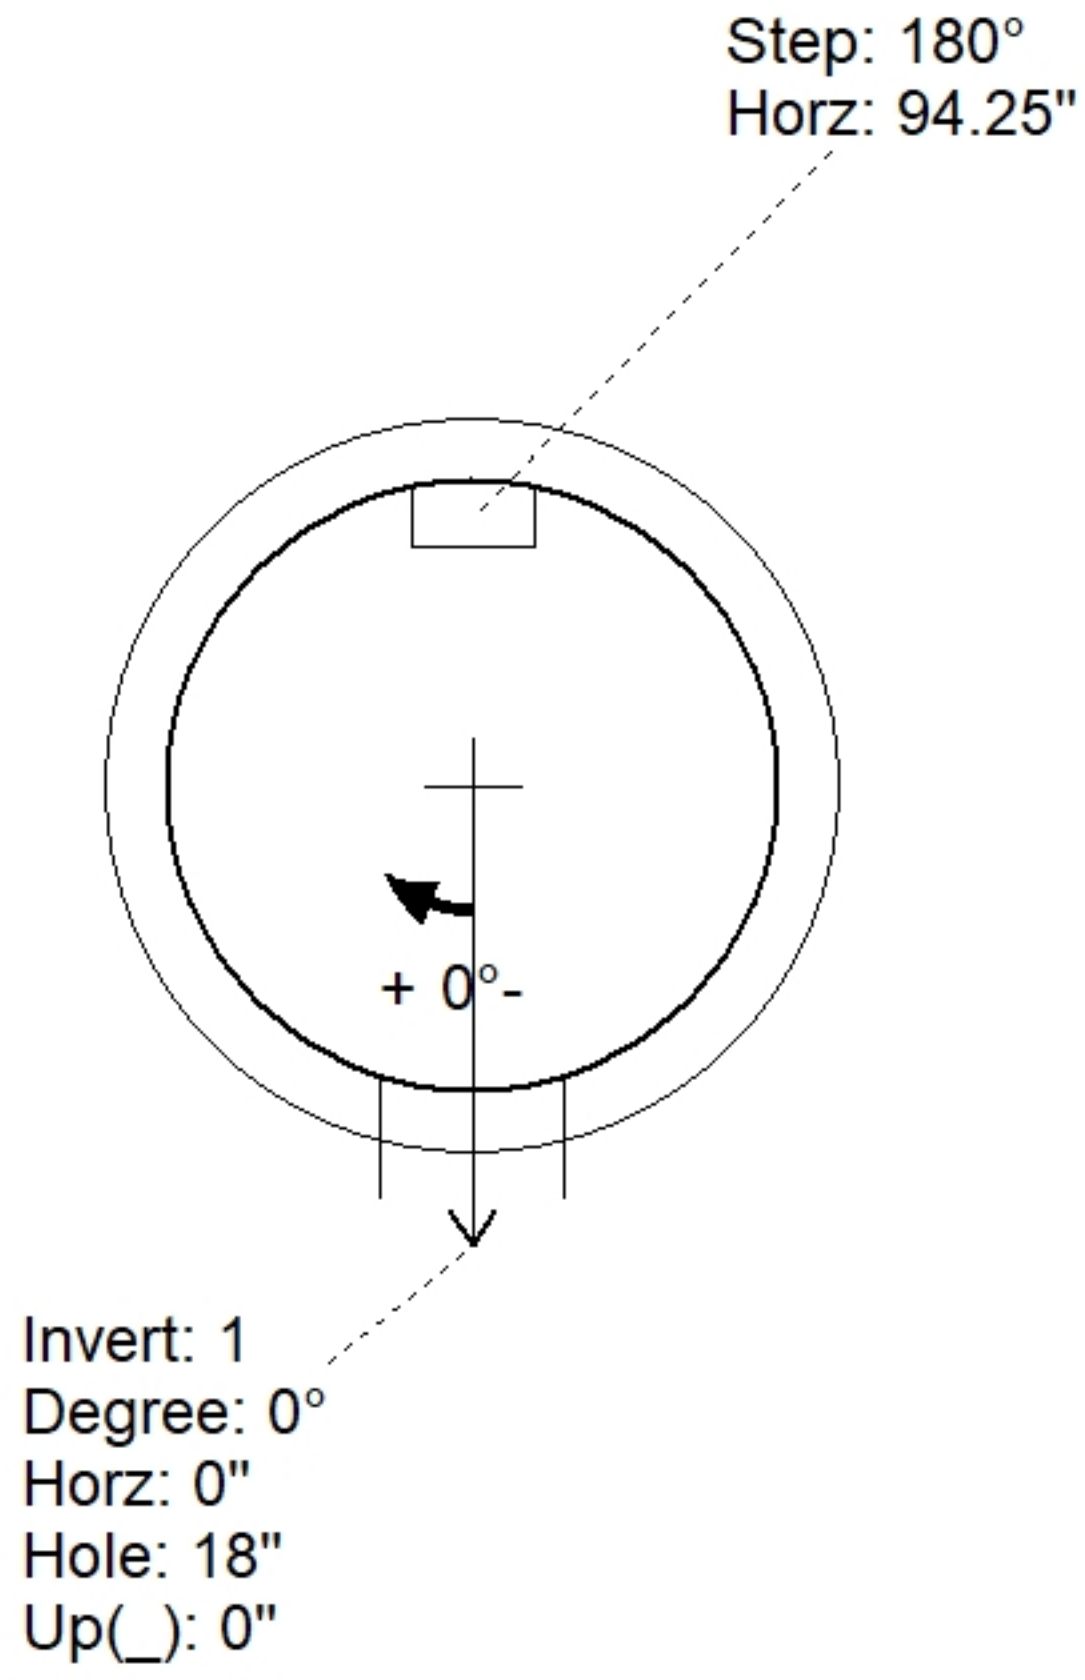
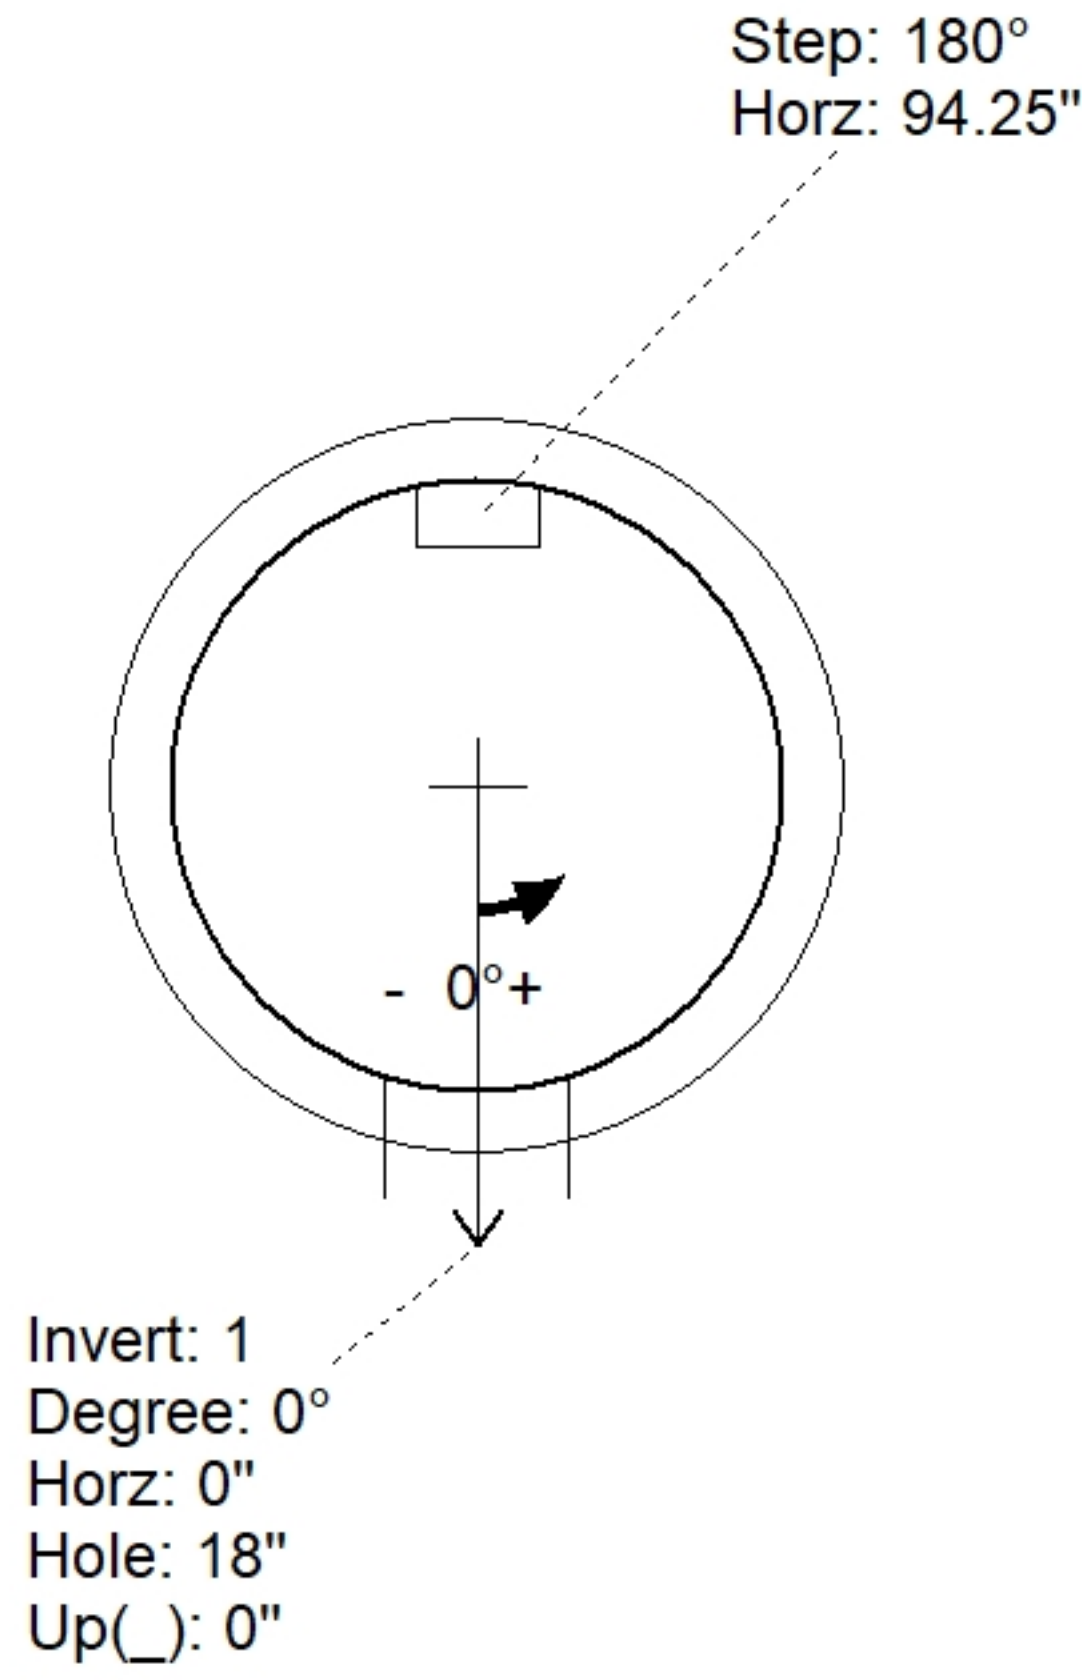
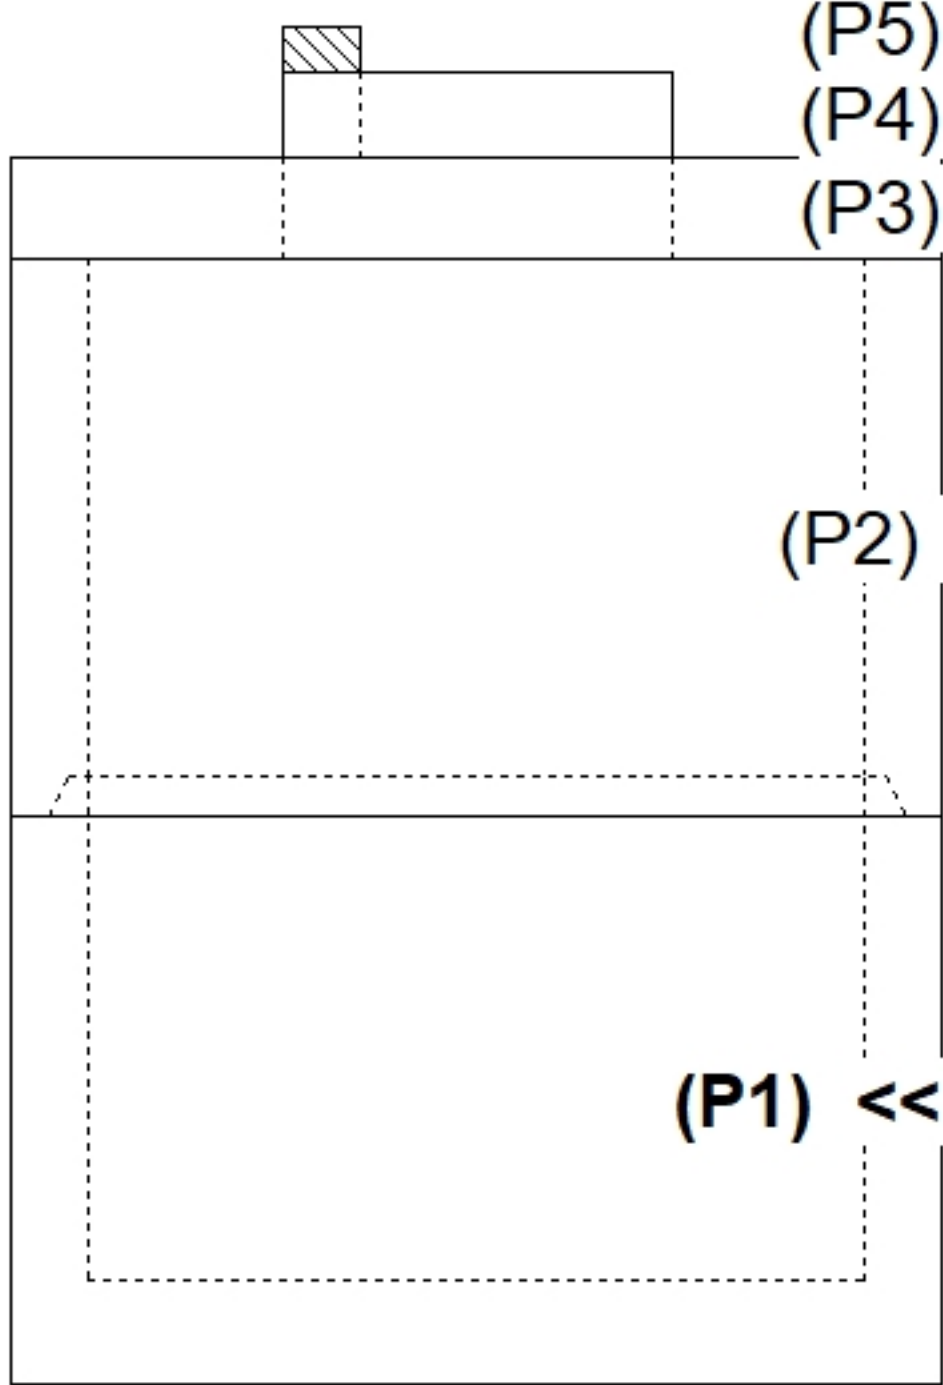
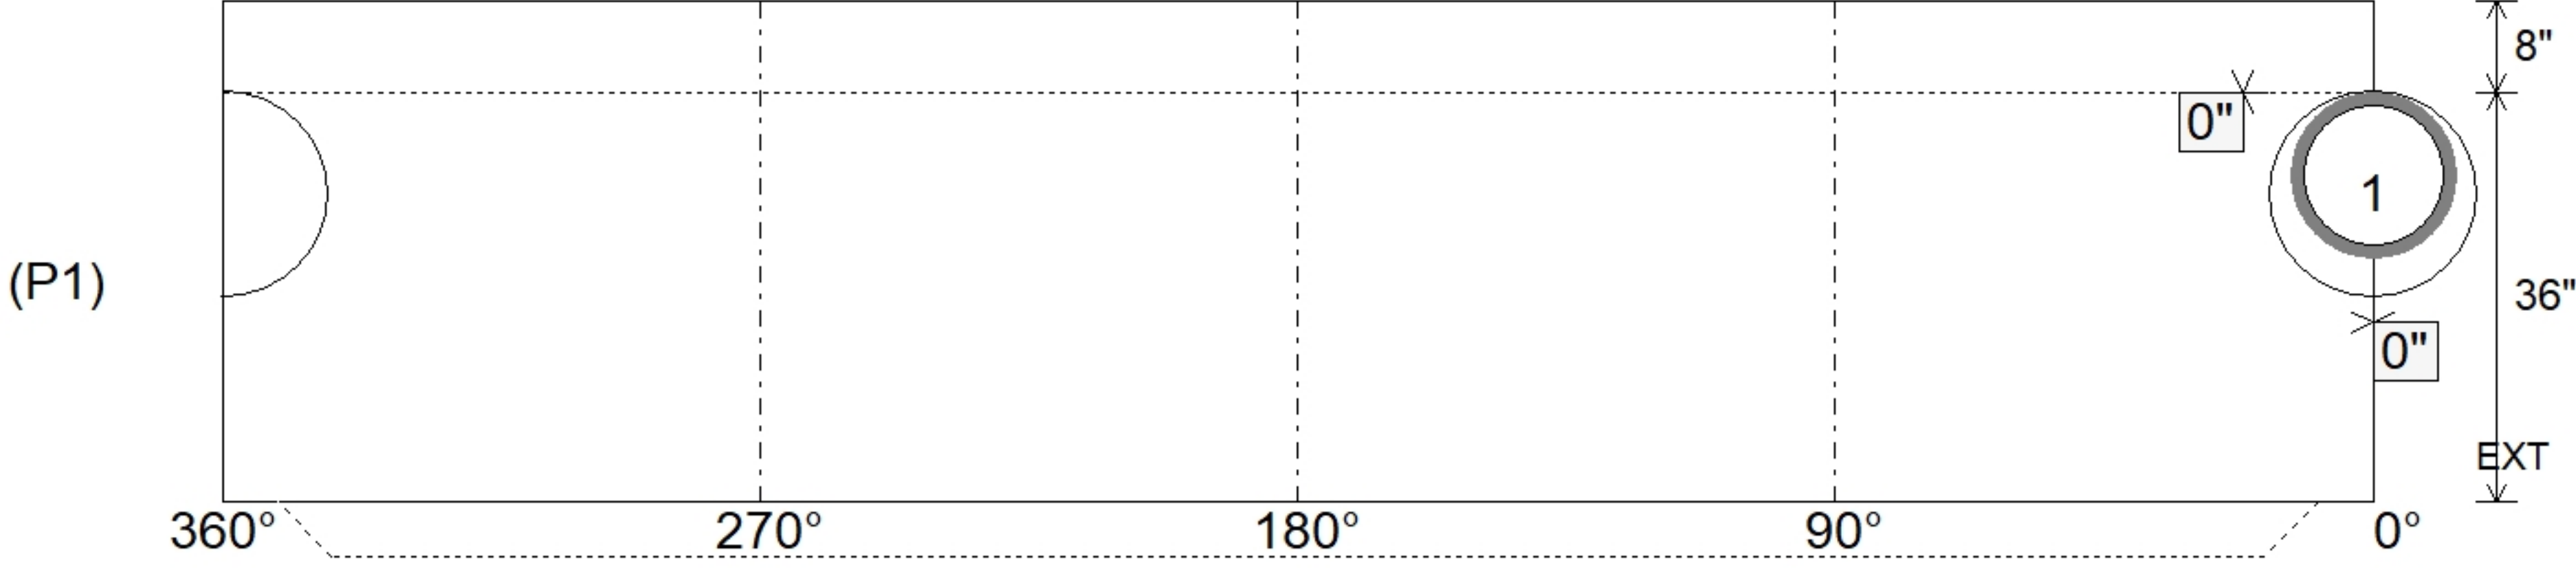


Job Name: 26-1787 - Kroger Expansion Job Location: Murray, KY Contractor: Parker Excavating, LLC.				Plant: 100 7/22/2026 3:24:59 PM		Tech: J. Horsley PC: J. Jarvis						
Structure ID: C3 ST-CI												
P1		MH060BAVF		MH BASE Custom Ht T/n								
P5) 6" x 36" - CASTING - Curb Back/Hood - 3.50" P4) 30" x 36" - CASTING - Frame&Grate F/F - 6.50" P3) 60" - MH FLAT TOP w/30"x36" Hole F/F - 8" P2) 60" - MH RISER Custom Ht F/G - 43" P1) 60" - MH BASE Custom Ht T/n - 36" 1) CASTING - JBS 2064-V SET (F/G/H) 1) 60" - Conseal CS-102 1.00" 1) 60" - Conseal CS-231 1.00" 1) Hole - 18 4) Hole - 6 3) MH Step ML-10-TDS-NCR - 10"						0 lb 0 lb 2008 lb 4432 lb 6362 lb 500 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS 2064 F/G/H). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Structure Total: 13302 lb												
Rim: 503.2' Rim to Invert: 8.02' Slack: 0.39" Sump: 1.15" Step Position: 180°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	495.18'	0°	0"	12" HP STORM	14.5"	Hole 18	18"	18.282"	0"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)  Step: 180° Horz: 94.25" Invert: 1 Degree: 0° Horz: 0" Hole: 18" Up(): 0" UPSIDE-DOWN VIEW (int. dimensions)  Step: 180° Horz: 94.25" Invert: 1 Degree: 0° Horz: 0" Hole: 18" Up(): 0"												
 (P5) (P4) (P3) (P2) (P1) << INSIDE WALL DIMENSIONS  (P1) 360° 270° 180° 90° 0° 8" 36" EXT												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 6362 lb Volume (Net): 1.62cu.yd			
