

Job Name: 26-1787 - Kroger Expansion
 Job Location: Murray, KY
 Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:25:02 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: C6 ST-CI

P1 MH060BAVF

MH BASE Custom Ht F/n

P4) 6" x 36" - CASTING - Curb Back/Hood - 3.50"
 P3) 30" x 36" - CASTING - Frame&Grate F/F - 6.50"
 P2) 60" - MH FLAT TOP w/30"x36" Hole F/F - 8"
 P1) 60" - MH BASE Custom Ht F/n - 59"
 1) CASTING - JBS 2064-V SET (F/G/H)
 1) 60" - Conseal CS-102 1.00"
 1) Hole - 20
 4) Hole - 6
 5) MH Step ML-10-TDS-NCR - 10"

0 lb
 0 lb
 2008 lb
 8675 lb
 500 lb
 0 lb
 0 lb
 0 lb
 0 lb

Structure Total: 11183 lb

Structure Notes:



1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (JBS 2064 F/G/H).
- REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Rim: 501.32' Rim to Invert: 6.38' Slack: 0.86" Sump: 1.3" Step Position: 180°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	494.94'	0°	0"	15" HP STORM	17.7"	Hole 20	20"	20.39"	0"	0"
Invert 2	498.86'	45°	28.25"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.01"	48"	0"
Invert 3	498.86'	135°	84.875"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.01"	48"	0"
Invert 4	498.86'	225°	141.375"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.01"	48"	0"
Invert 5	498.86'	315°	197.875"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.01"	48"	0"
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

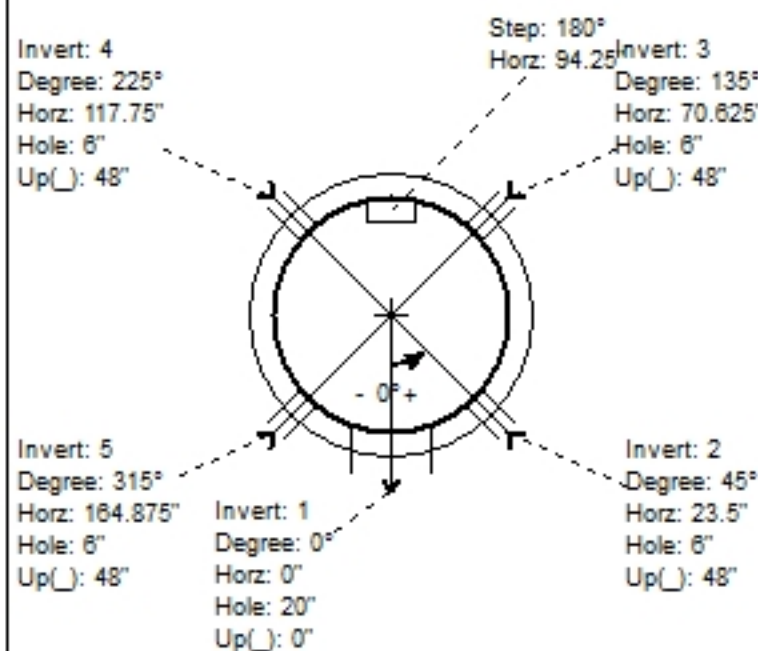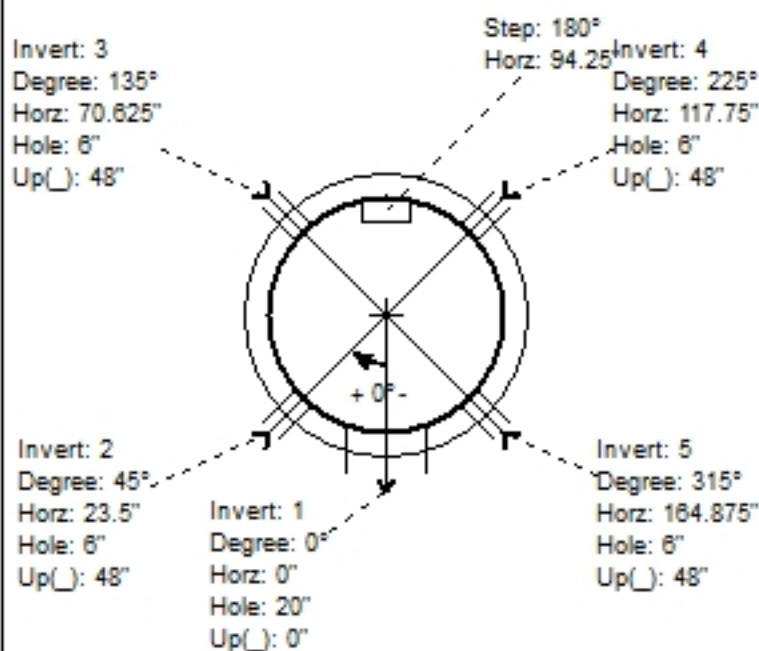

INSIDE WALL DIMENSIONS

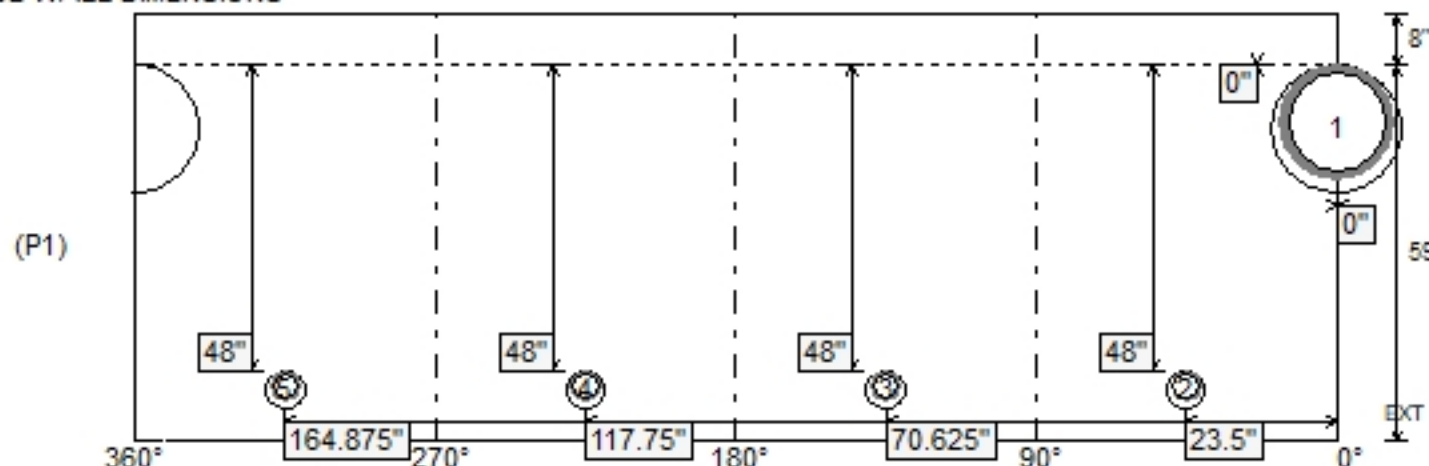

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 6"
 Floor Height: 8"

Height (Int): 59"
 Height (Ext): 67"

Weight (Net): 8675 lb
 Volume (Net): 2.22cu.yd
