

Job Name: 26-1787 - Kroger Expansion
 Job Location: Murray, KY
 Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:25:03 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: C7 ST-CI

P1 BX4872-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

- P5) 6" x 36" - CASTING - Curb Back/Hood - 3.50"
 P4) 30" x 36" - CASTING - Frame&Grate F/F - 6.50"
 P3) 48" x 72" - CB FLAT TOP 8"W w/30"x36" HOLE F/F - 8"
 P2) 48" x 72" - BOX RISER 8inW, Variable Ht F/G - 72"
 P1) 48" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 65"
 1) SECONDARY POUR
 1) CASTING - JBS 2064-V SET (F/G/H)
 2) 48" x 72" - Con Seal CS-102 1.00"
 2) Hole - 30
 1) Hole - 20
 4) Hole - 6
 11) MH Step ML-10-TDS-NCR - 10"

0 lb
 0 lb
 3056 lb
 12846 lb
 14037 lb
 0 lb
 500 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb

Structure Total: 30439 lb

Structure Notes:



- PER ASTM C478 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - CASTING BY ICAST (JBS 2064 F/G)
- REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Rim: 500.38' Rim to Invert: 12.79' Slack: 0.484' Sump: 2.004' Step Position: 180'

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	487.59'	335°	26.875"	24" HP STORM	28"	Hole 30	30"	33.101"	0"	14"
Invert 2	487.59'	25°	27.375"	24" HP STORM	28"	Hole 30	30"	70.986"	0"	21.962"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

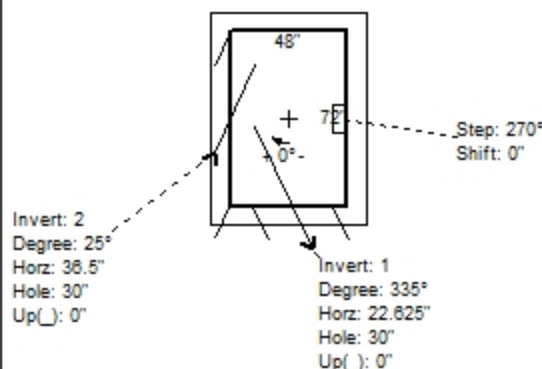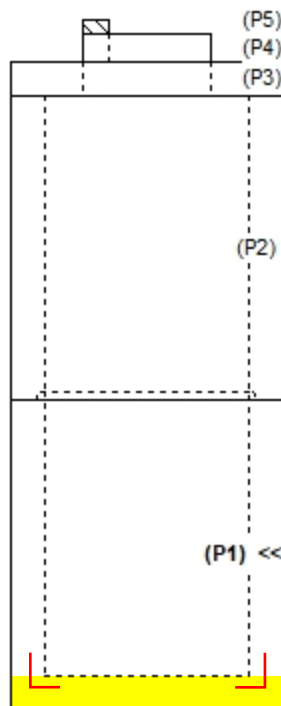

SECONDARY POUR REQUIRED.
 1ST POUR (FLOOR) = 3,780 LBS
 2ND POUR (WALLS) = 10,257 LBS

INSIDE WALL DIMENSIONS

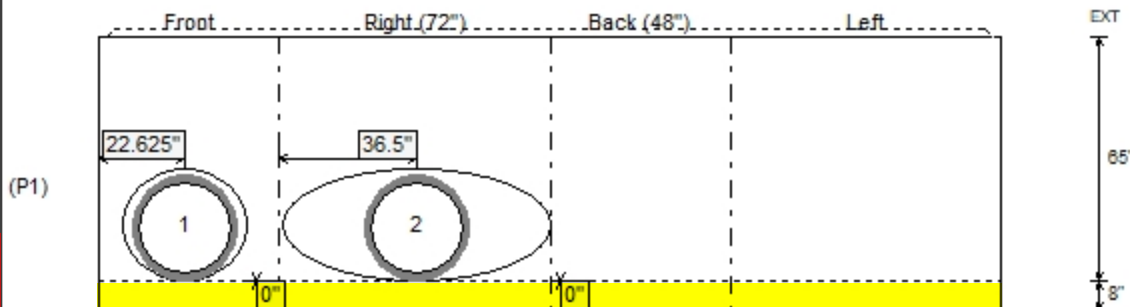

1ST POUR (FLOOR)
 STUB #5 L BARS (18"x36")
 OUT TOP OF FLOOR FOR
 CONNECTING WALLS

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 65"
 Height (Ext): 73"

Weight (Net): 14037 lb
 Volume (Net): 3.59cu.yd

Job Name: 26-1787 - Kroger Expansion
 Job Location: Murray, KY
 Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:25:03 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: C7 ST-CI

P1A BX4872-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

- P5) 6" x 36" - CASTING - Curb Back/Hood - 3.50"
 P4) 30" x 36" - CASTING - Frame&Grate F/F - 6.50"
 P3) 48" x 72" - CB FLAT TOP 8"W w/30"x36" HOLE F/F - 8"
 P2) 48" x 72" - BOX RISER 8inW, Variable Ht F/G - 72"
 P1) 48" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 65"
 1) SECONDARY POUR
 1) CASTING - JBS 2064-V SET (F/G/H)
 2) 48" x 72" - Con Seal CS-102 1.00"
 2) Hole - 30
 1) Hole - 20
 4) Hole - 6
 11) MH Step ML-10-TDS-NCR - 10"

0 lb
 0 lb
 3056 lb
 12846 lb
 14037 lb
 0 lb
 500 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb

Structure Total: 30439 lb

Structure Notes:



- PER ASTM C478 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - CASTING BY ICAST (JBS 2064 F/G)
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Rim: 500.38' Rim to Invert: 12.79' Slack: 0.484' Sump: 2.004' Step Position: 180'

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	487.59'	335°	26.875"	24" HP STORM	28"	Hole 30	30"	33.101"	0"	14"
Invert 2	487.59'	25°	27.375"	24" HP STORM	28"	Hole 30	30"	70.986"	0"	21.962"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

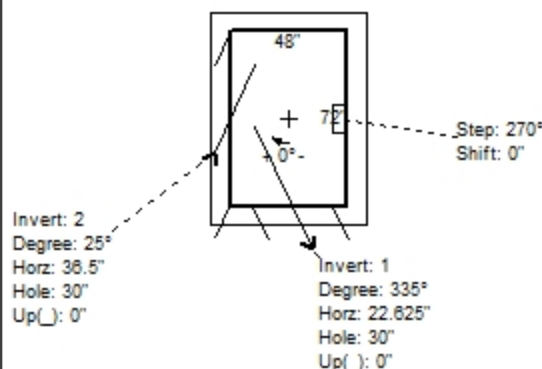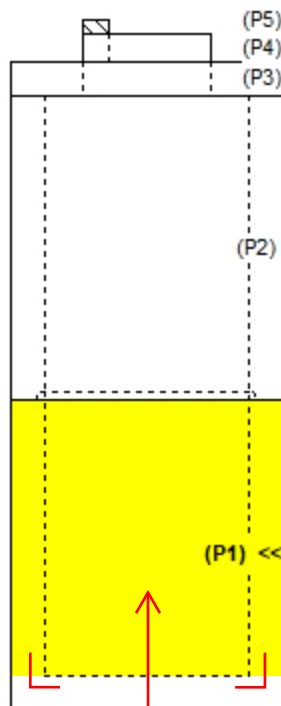

SECONDARY POUR REQUIRED.
 1ST POUR (FLOOR) = 3,780 LBS
 2ND POUR (WALLS) = 10,257 LBS

INSIDE WALL DIMENSIONS

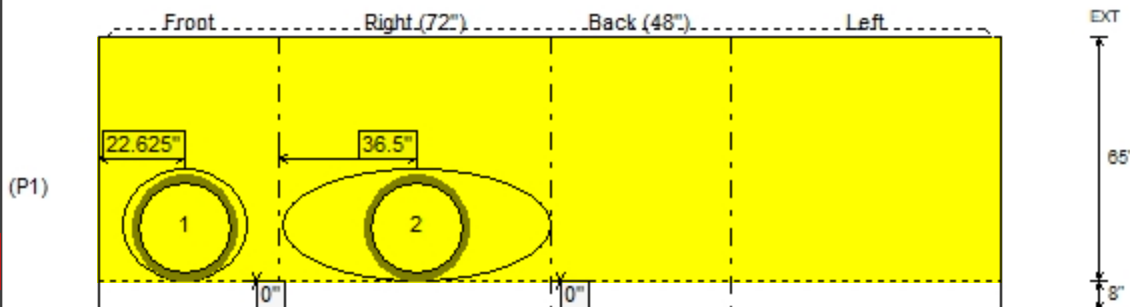

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 65"
 Height (Ext): 73"

Weight (Net): 14037 lb
 Volume (Net): 3.59cu.yd
