

Job Name: 26-1787 - Kroger Expansion
 Job Location: Murray, KY
 Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:25:05 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: D1 ST-IN

P1 BX2448-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P3) 24" x 48" - CASTING HEIGHT - 0"
 P2) 24" x 48" - BX FLAT LID 8inW SPEC. (JBS-3061) F/F - 8"
 P1) 24" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 50"
 1) SECONDARY POUR
 1) CASTING - JBS 3061 F/G
 1) 24" x 48" - Conesal CS-102 1.00"
 1) Hole - 30
 4) Hole - 6

0 lb
 945 lb
 7194 lb
 0 lb
 250 lb
 0 lb
 0 lb
 0 lb

Structure Total: 8389 lb

Structure Notes:


- PER ASTM C913 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - CASTING BY ICAST (JBS 3061 F/G CAST FLUSH).
- REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 499.42' Rim to Invert: 4.74' Slack: 0.836" Sump: 1.956" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	494.68'	0°	20"	24" HP STORM	28"	Hole 30	30"	27"	0"	0"
Invert 2	497.75'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 3	497.75'	90°	32"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 4	497.75'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 5	497.75'	270°	32"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

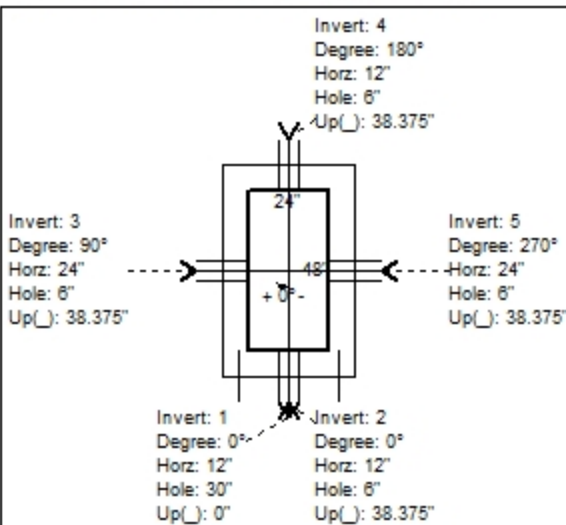

SECONDARY POUR REQUIRED.
 1ST POUR (FLOOR) = 1,719 LBS
 2ND POUR (WALLS) = 5,475 LBS

INSIDE WALL DIMENSIONS

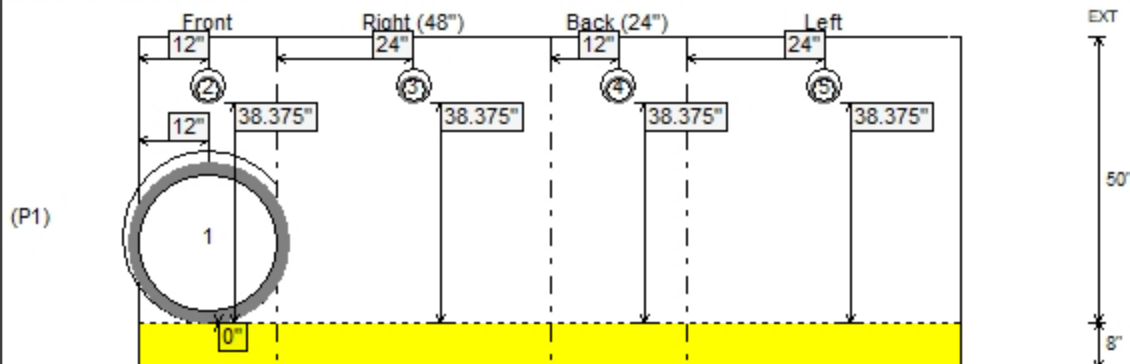

1ST POUR (FLOOR)
 STUB #5 L BARS (14"x24")
 OUT TOP OF FLOOR FOR
 CONNECTING WALLS

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 50"
 Height (Ext): 58"

Weight (Net): 7194 lb
 Volume (Net): 1.84cu.yd

Job Name: 26-1787 - Kroger Expansion
 Job Location: Murray, KY
 Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:25:05 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: D1 ST-IN

P1A BX2448-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P3) 24" x 48" - CASTING HEIGHT - 0"
 P2) 24" x 48" - BX FLAT LID 8inW SPEC. (JBS-3061) F/F - 8"
 P1) 24" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 50"
 1) SECONDARY POUR
 1) CASTING - JBS 3061 F/G
 1) 24" x 48" - Conesal CS-102 1.00"
 1) Hole - 30
 4) Hole - 6

0 lb
 945 lb
 7194 lb
 0 lb
 250 lb
 0 lb
 0 lb
 0 lb

Structure Total: 8389 lb

Structure Notes:


- PER ASTM C913 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - CASTING BY ICAST (JBS 3061 F/G CAST FLUSH).
- REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 499.42' Rim to Invert: 4.74' Slack: 0.836" Sump: 1.956" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	494.68'	0°	20"	24" HP STORM	28"	Hole 30	30"	27"	0"	0"
Invert 2	497.75'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 3	497.75'	90°	32"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 4	497.75'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 5	497.75'	270°	32"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	38.375"	0"
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

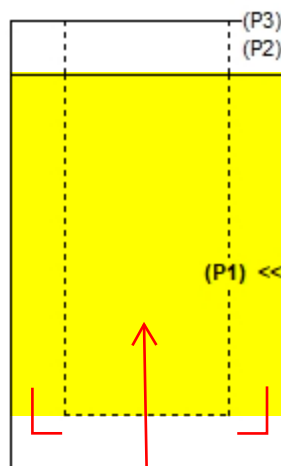


2ND POUR (FLOOR)

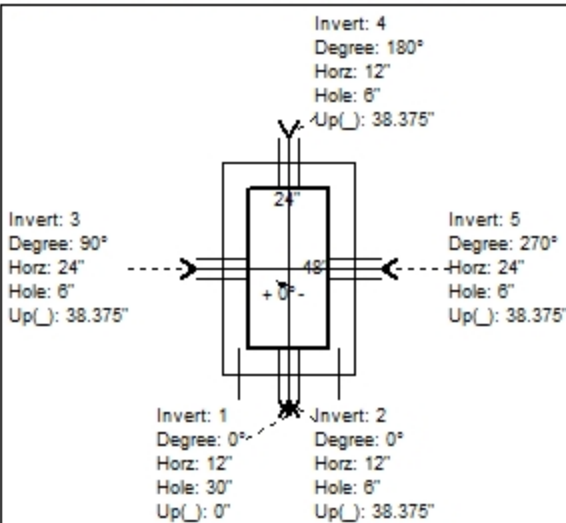

SECONDARY POUR REQUIRED.
 1ST POUR (FLOOR) = 1,719 LBS
 2ND POUR (WALLS) = 5,475 LBS

INSIDE WALL DIMENSIONS

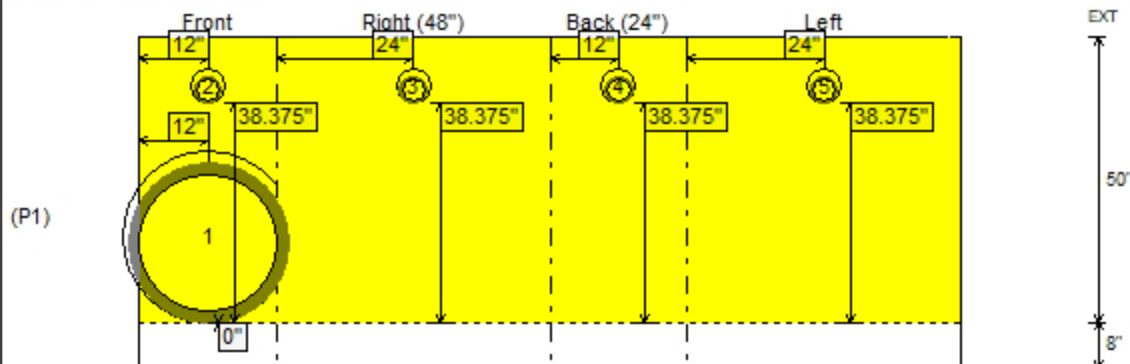

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 50"
 Height (Ext): 58"

Weight (Net): 7194 lb
 Volume (Net): 1.84cu.yd
