

Job Name: 26-1787 - Kroger Expansion
Job Location: Murray, KY
Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:26:57 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: D1 ST-IN

P2 BX024048-08LD08S

BX FLAT LID 8inW SPEC. (JBS-3061) F/F



P3) 24" x 48" - CASTING HEIGHT - 0"
P2) 24" x 48" - BX FLAT LID 8inW SPEC. (JBS-3061) F/F - 8"
P1) 24" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 50"
1) SECONDARY POUR
1) CASTING - JBS 3061 F/G
1) 24" x 48" - Conseal CS-102 1.00"
1) Hole - 30
4) Hole - 6

0 lb
945 lb
7194 lb
0 lb
250 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 8389 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (JBS 3061 F/G CAST FLUSH).
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

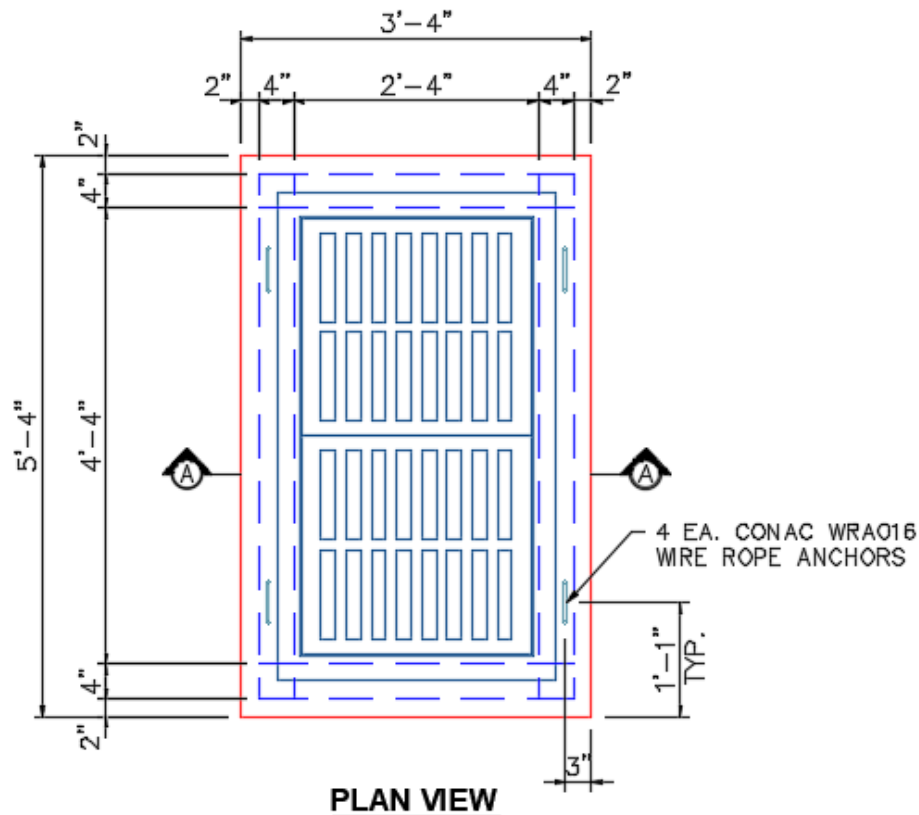

SECTION A-A

#5 BAR CUT LIST

2 EA. @ 60" LG.
2 EA. @ 36" LG

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 945 lb
Volume (Net): 0.24cu.yd
