

Job Name: 26-1800 - Georgetown Community Park
Job Location: Georgetown, IN
Contractor: Song Construction

Plant: 100
7/24/2026 12:15:13 PM

Tech: Jared - A
PC: Jay Ross Jarvis



Structure ID: San. MH 2 SS-MH



P2 MH048CN30

ECC CONE w/ 24" HOLE

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE - 30"
P1) 48" - MH BASE Custom Ht - 33"
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) CASTING - HOE MC-375 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
5) MH Step ML-10-TDS-NCR - 10"

- 0 lb
2050 lb
3588 lb
0 lb
1440 lb
0 lb
271 lb
0 lb
0 lb
0 lb
8 lb
0 lb
- Structure Notes: .
1. HOE MC-375 F/C SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 7357 lb

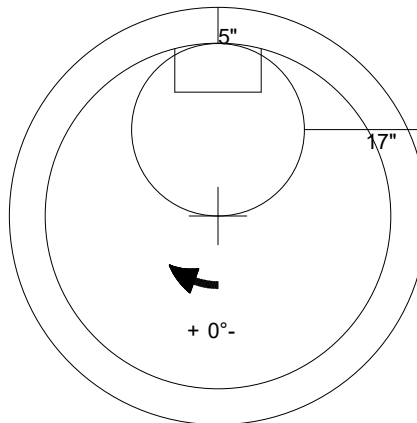

48" - ECC CONE w/ 24" HOLE - 30" - (P2)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 30"

Weight (Net): 2050 lb
Volume (Net): 0.41cu.yd
