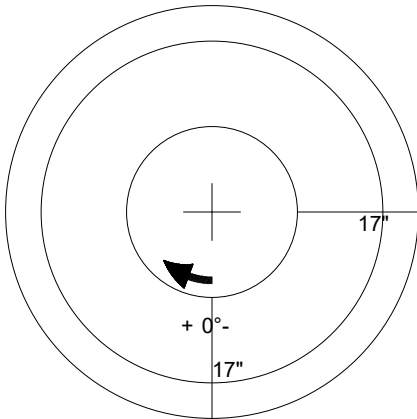



Job Name: 26-1814 - Brownsville Sewer System Additions		Plant: 100	Tech: Jared - F	
Job Location: Cave City, KY Contractor: Luttrell & Sons, LLC		7/31/2026 1:28:56 PM	PC: A. Chambers	
Structure ID: 0+10 SS-MH				
P3 MH048CCN24		CON CONE w/24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE F/G - 24" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"		0 lb 2252 lb 2515 lb 3330 lb 0 lb 1440 lb 0 lb 271 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 9824 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 2252 lb Volume (Net): 0.57cu.yd
