




Job Name: 26-1814 - Brownsville Sewer System Additions Job Location: Cave City, KY Contractor: Luttrell & Sons, LLC					Plant: 100 8/6/2026 9:03:02 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: 0+68 SS-MH											
P1 MH048BA18			MH BASE T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE F/G - 36" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2252 lb 4982 lb 2540 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 11501 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 550' Rim to Invert: 11' Slack: 1" Sump: 2" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	539'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

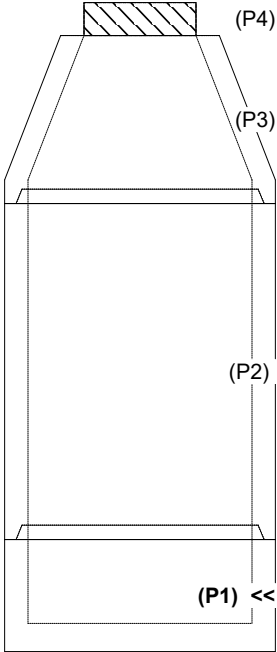


RIGHT-SIDE UP VIEW (int. dimensions)

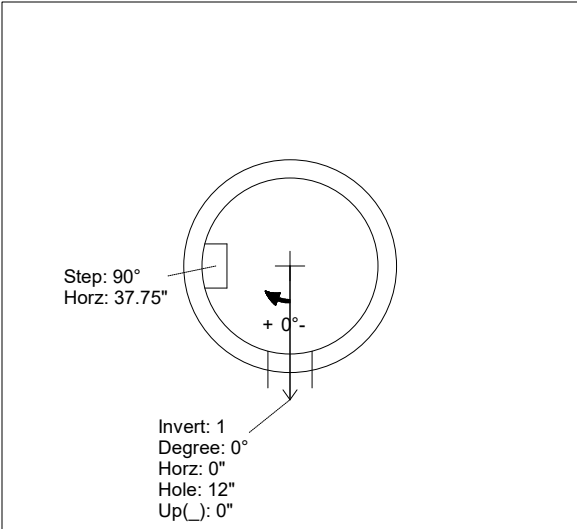

UPSIDE-DOWN VIEW (int. dimensions)

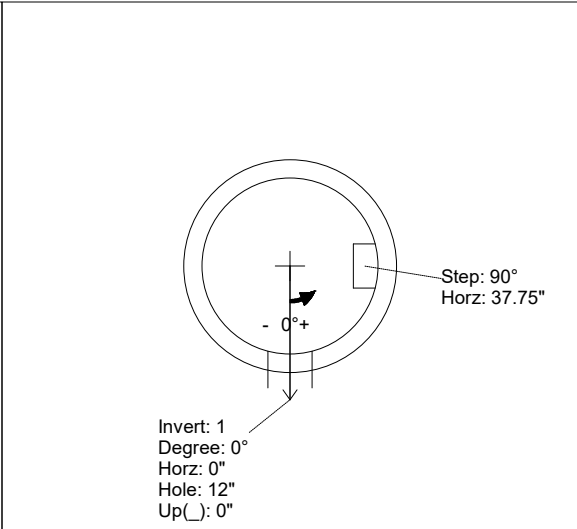

INSIDE WALL DIMENSIONS

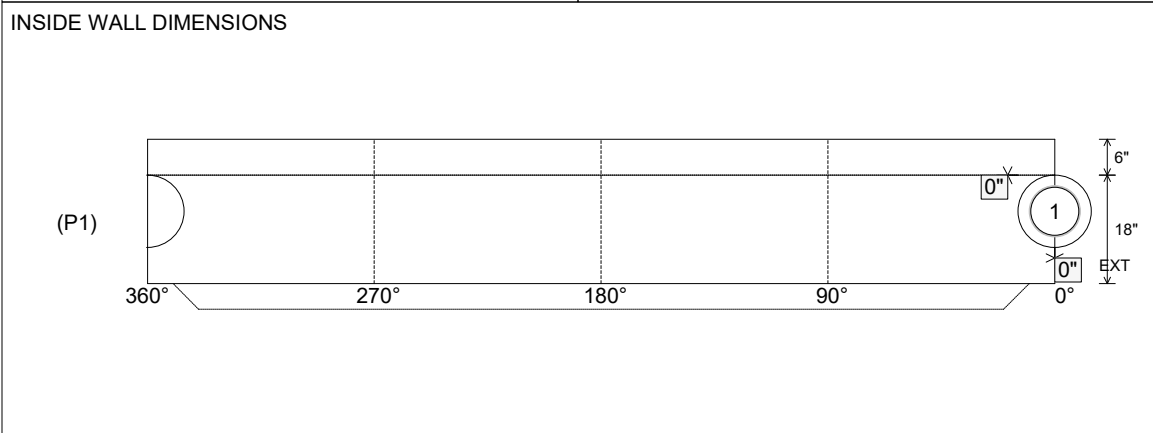


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2540 lb Volume (Net): 0.65cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-1814 - Brownsville Sewer System Additions Job Location: Cave City, KY Contractor: Luttrell & Sons, LLC					Plant: 100 8/6/2026 9:03:02 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: 0+68 SS-MH											
P1 MH048BA18		MH BASE T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE F/G - 36" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2252 lb 4982 lb 2540 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 11501 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 550'		Rim to Invert: 11'		Slack: 1"		Sump: 2"		Step Position: 90°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	539'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)


FOR INVERT ONLY

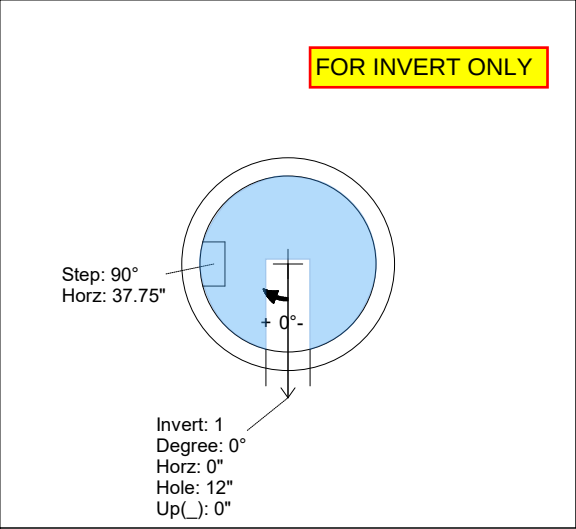

UPSIDE-DOWN VIEW (int. dimensions)

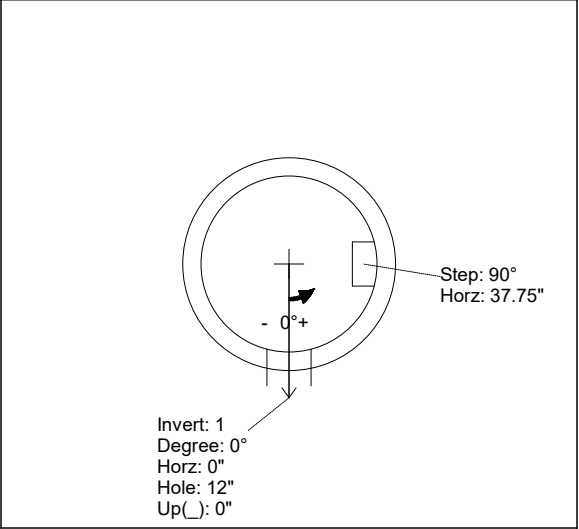

INSIDE WALL DIMENSIONS

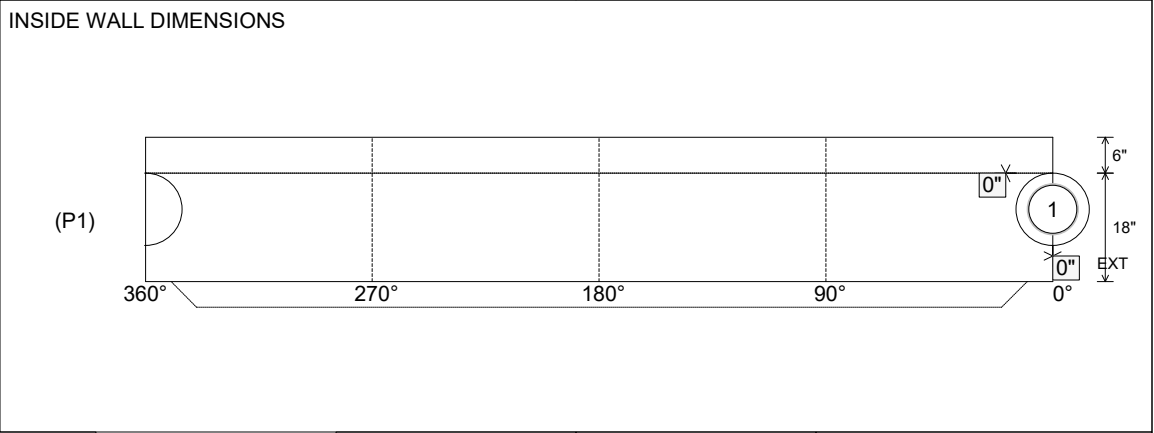

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2540 lb Volume (Net): 0.65cu.yd
----------------------------------	---------------------------------	--	--	--
