

**Contractor: Luttrell & Sons, LLC**

TECH: Jared - F

Plant: 100



Size: 72" x 72"

Rim to Invert: 2.87'


Floor Height: 8"

Slack: 0"

- FLOOR (As .47) #5 BARS AT 12" C.C.E.W.



0 lb

Structure Total: 23242 lb

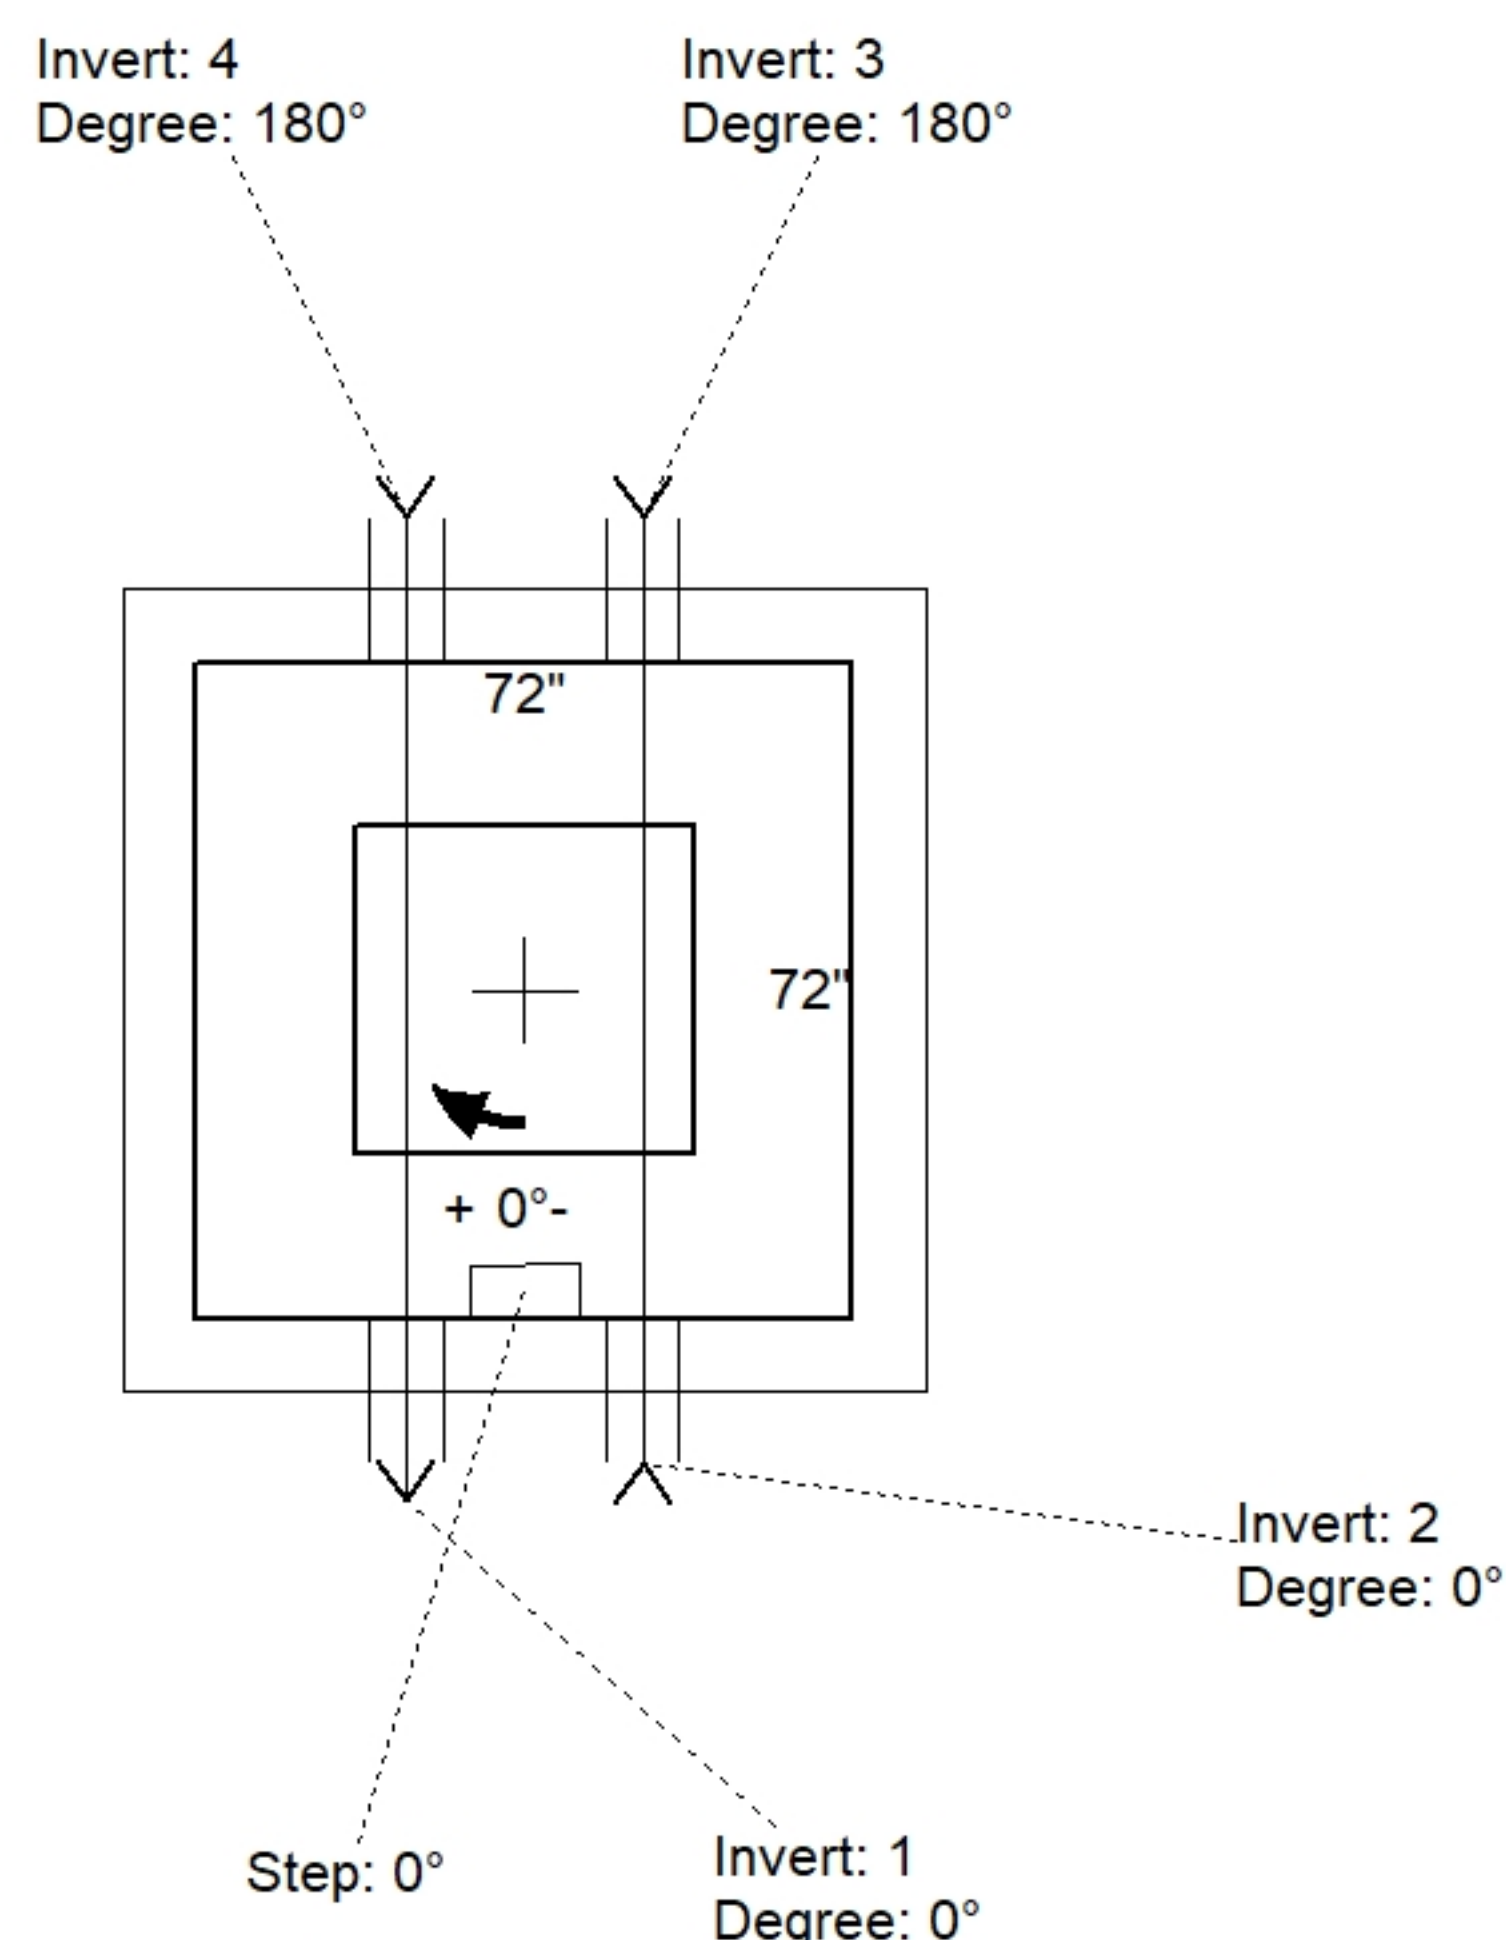

| Position | Elev    | Angle | Pipe         | Pipe OD | Hole | Connector       | Up (↓) | Ref |
|----------|---------|-------|--------------|---------|------|-----------------|--------|-----|
| Rim      | 496.25' |       |              |         |      |                 |        |     |
| Reducer  |         |       |              |         |      |                 |        |     |
| Invert 1 | 493.38' | 0°    | 4" PVC SDR35 | 4.25"   | 8"   | PSX 8QRS-S NYLO | 35.56" | P1  |
| Invert 2 | 493.38' | 0°    | 4" PVC SDR35 | 4.25"   | 8"   | PSX 8QRS-S NYLO | 35.56" | P1  |
| Invert 3 | 493.38' | 180°  | 4" PVC SDR35 | 4.25"   | 8"   | PSX 8QRS-S NYLO | 35.56" | P1  |
| Invert 4 | 493.38' | 180°  | 4" PVC SDR35 | 4.25"   | 8"   | PSX 8QRS-S NYLO | 35.56" | P1  |
| Invert 5 |         |       |              |         |      |                 |        |     |
| Invert 6 |         |       |              |         |      |                 |        |     |
| Invert 7 |         |       |              |         |      |                 |        |     |
| Invert 8 |         |       |              |         |      |                 |        |     |

### Default - Interior Dimensions

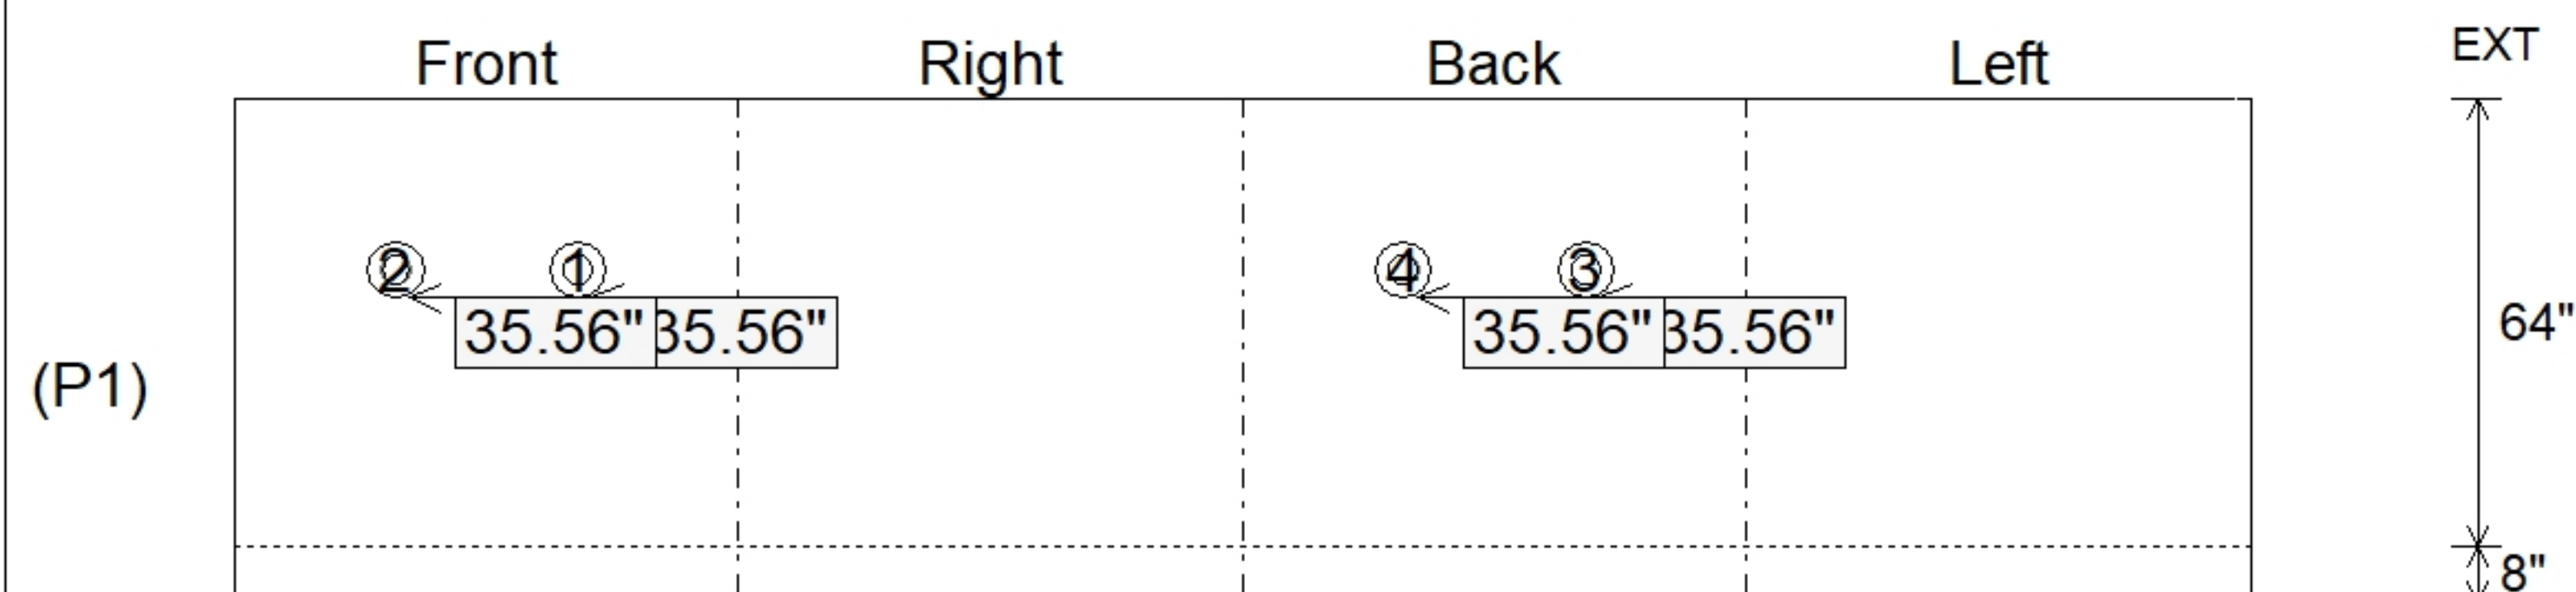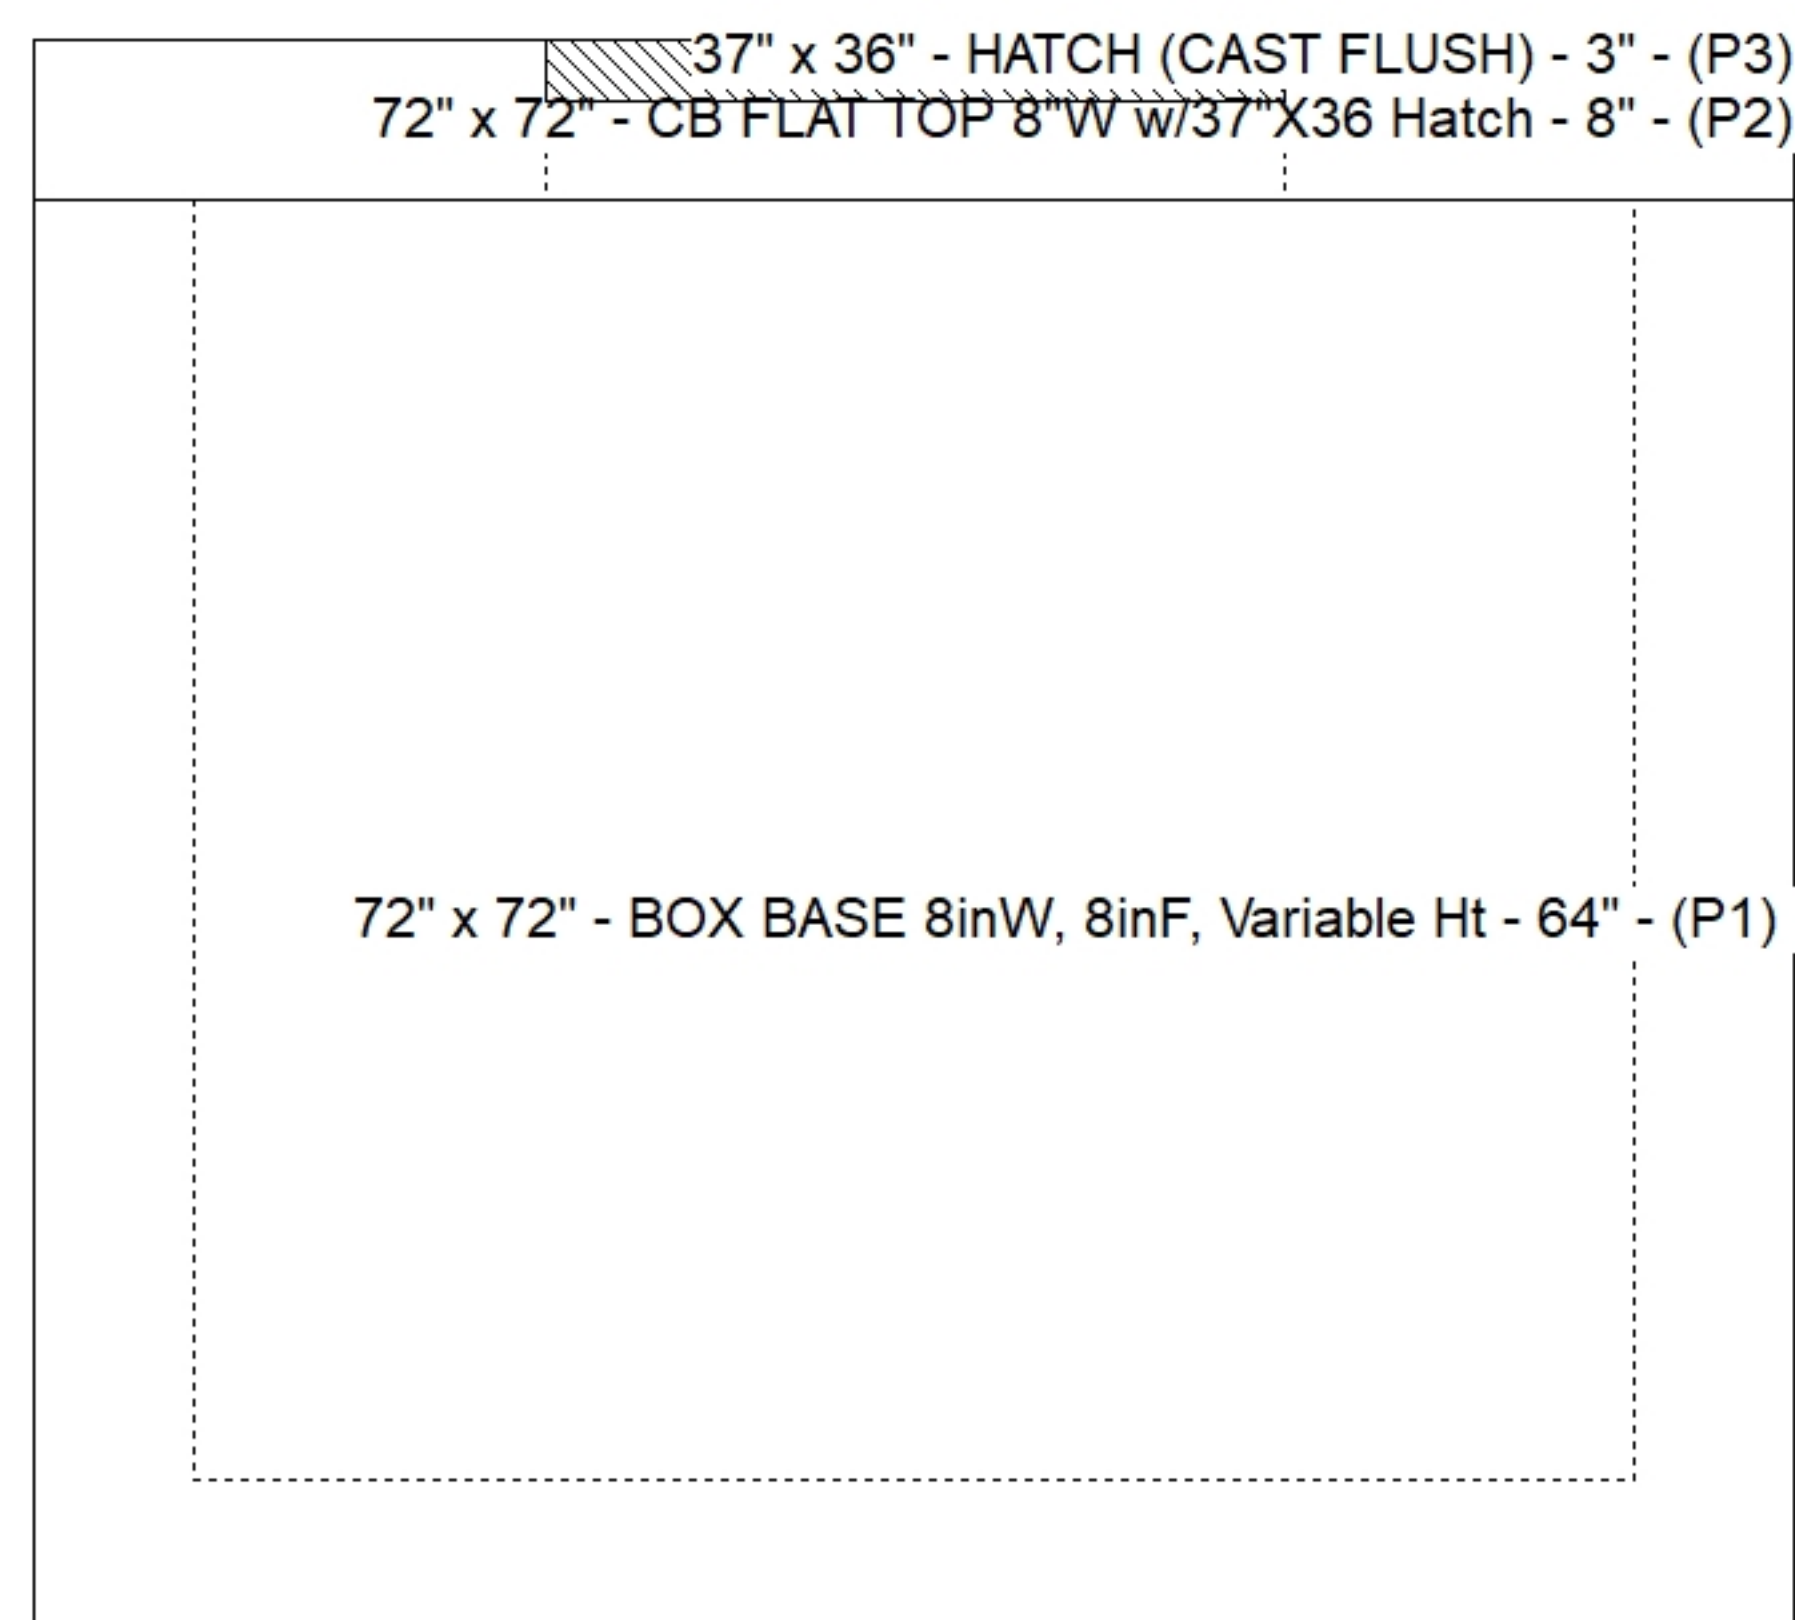

SUBMITTAL  
APPROVED BY:
