
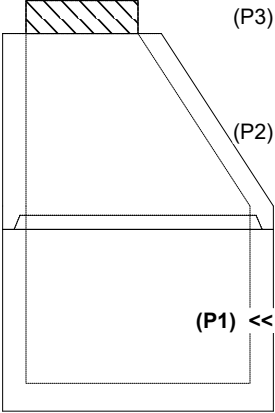
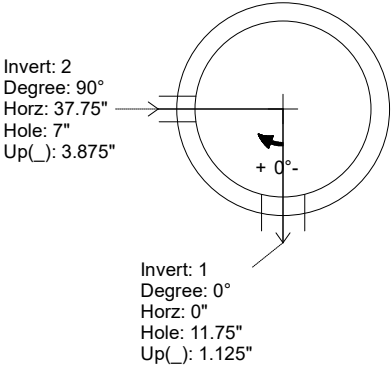
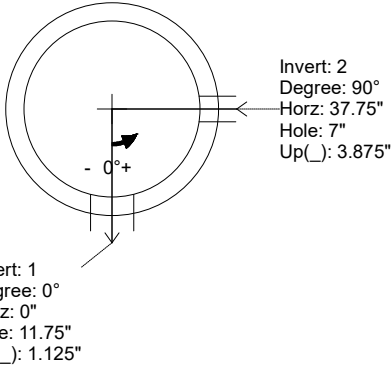
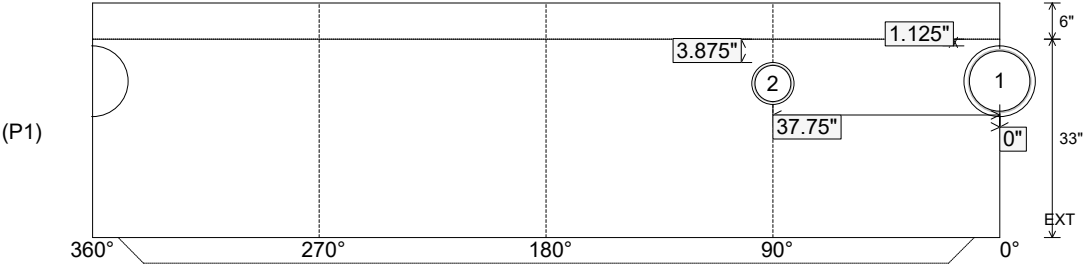


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:44 PM		Tech: Jared - F PC: E. Bradley			
Structure ID: T6 SS-MH										
P1 MH048BAVF			MH BASE Custom Ht T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 42" P1) 48" - MH BASE Custom Ht T/n - 33" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 0350 1) A-Lok - 0200					0 lb 3000 lb 3573 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 1 lb 1 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 932.54' Rim to Invert: 6.83' Slack: 1.96" Sump: 2" Step Position: 0°					Structure Total: 8286 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	925.71'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"
Invert 2	925.91'	90°	45.5"	6" PVC SDR35	6.25"	A-Lok 0200	7"	7.025"	3.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions) INSIDE WALL DIMENSIONS										
   										
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 33" Height (Ext): 39"		Weight (Net): 3573 lb Volume (Net): 0.91cu.yd	


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:44 PM		Tech: Jared - F PC: E. Bradley			
Structure ID: T6 SS-MH										
P1 MH048BAVF		MH BASE Custom Ht T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 42" P1) 48" - MH BASE Custom Ht T/n - 33" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 0350 1) A-Lok - 0200					0 lb 3000 lb 3573 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 1 lb 1 lb ----- 1 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 932.54' Rim to Invert: 6.83' Slack: 1.96" Sump: 2" Step Position: 0°					Structure Total: 8286 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	925.71'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"
Invert 2	925.91'	90°	45.5"	6" PVC SDR35	6.25"	A-Lok 0200	7"	7.025"	3.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


FOR INVERT ONLY

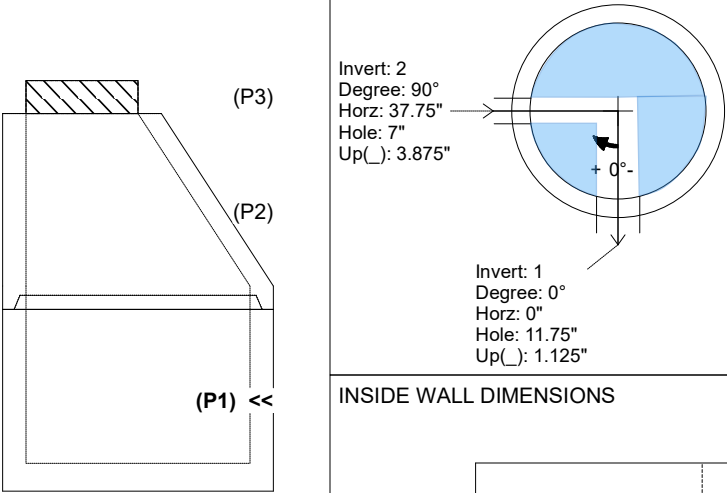

UPSIDE-DOWN VIEW (int. dimensions)

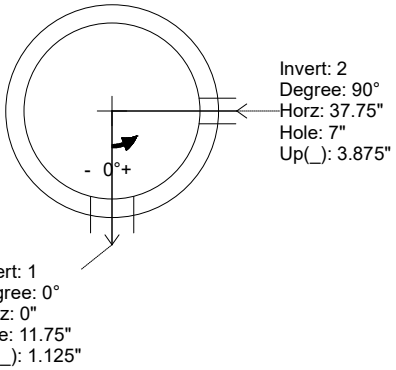

INSIDE WALL DIMENSIONS

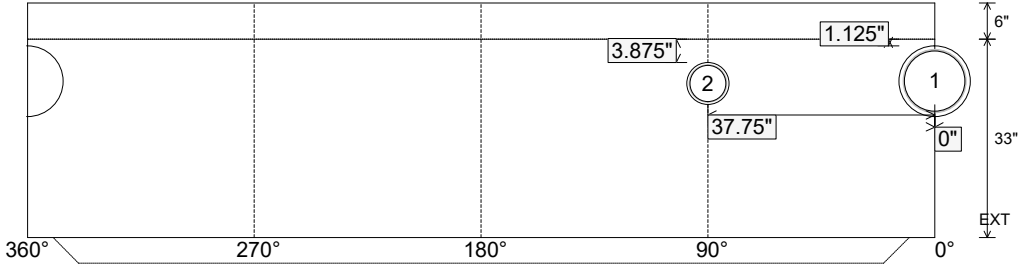

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 33" Height (Ext): 39"	Weight (Net): 3573 lb Volume (Net): 0.91cu.yd
----------------------------------	---------------------------------	--	--	--
