

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100




Slack: 1.04"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 72" - MH FLAT TOP w/24"x36" Hole - 15"
- P1) 72" - MH BASE Custom Ht - 79"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 72" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 2) Hole - 56
- 1) Hole - 24
- 6) MH Step ML-10-TDS-NCR - 10"

0 lb
4530 lb
11913 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 16885 lb

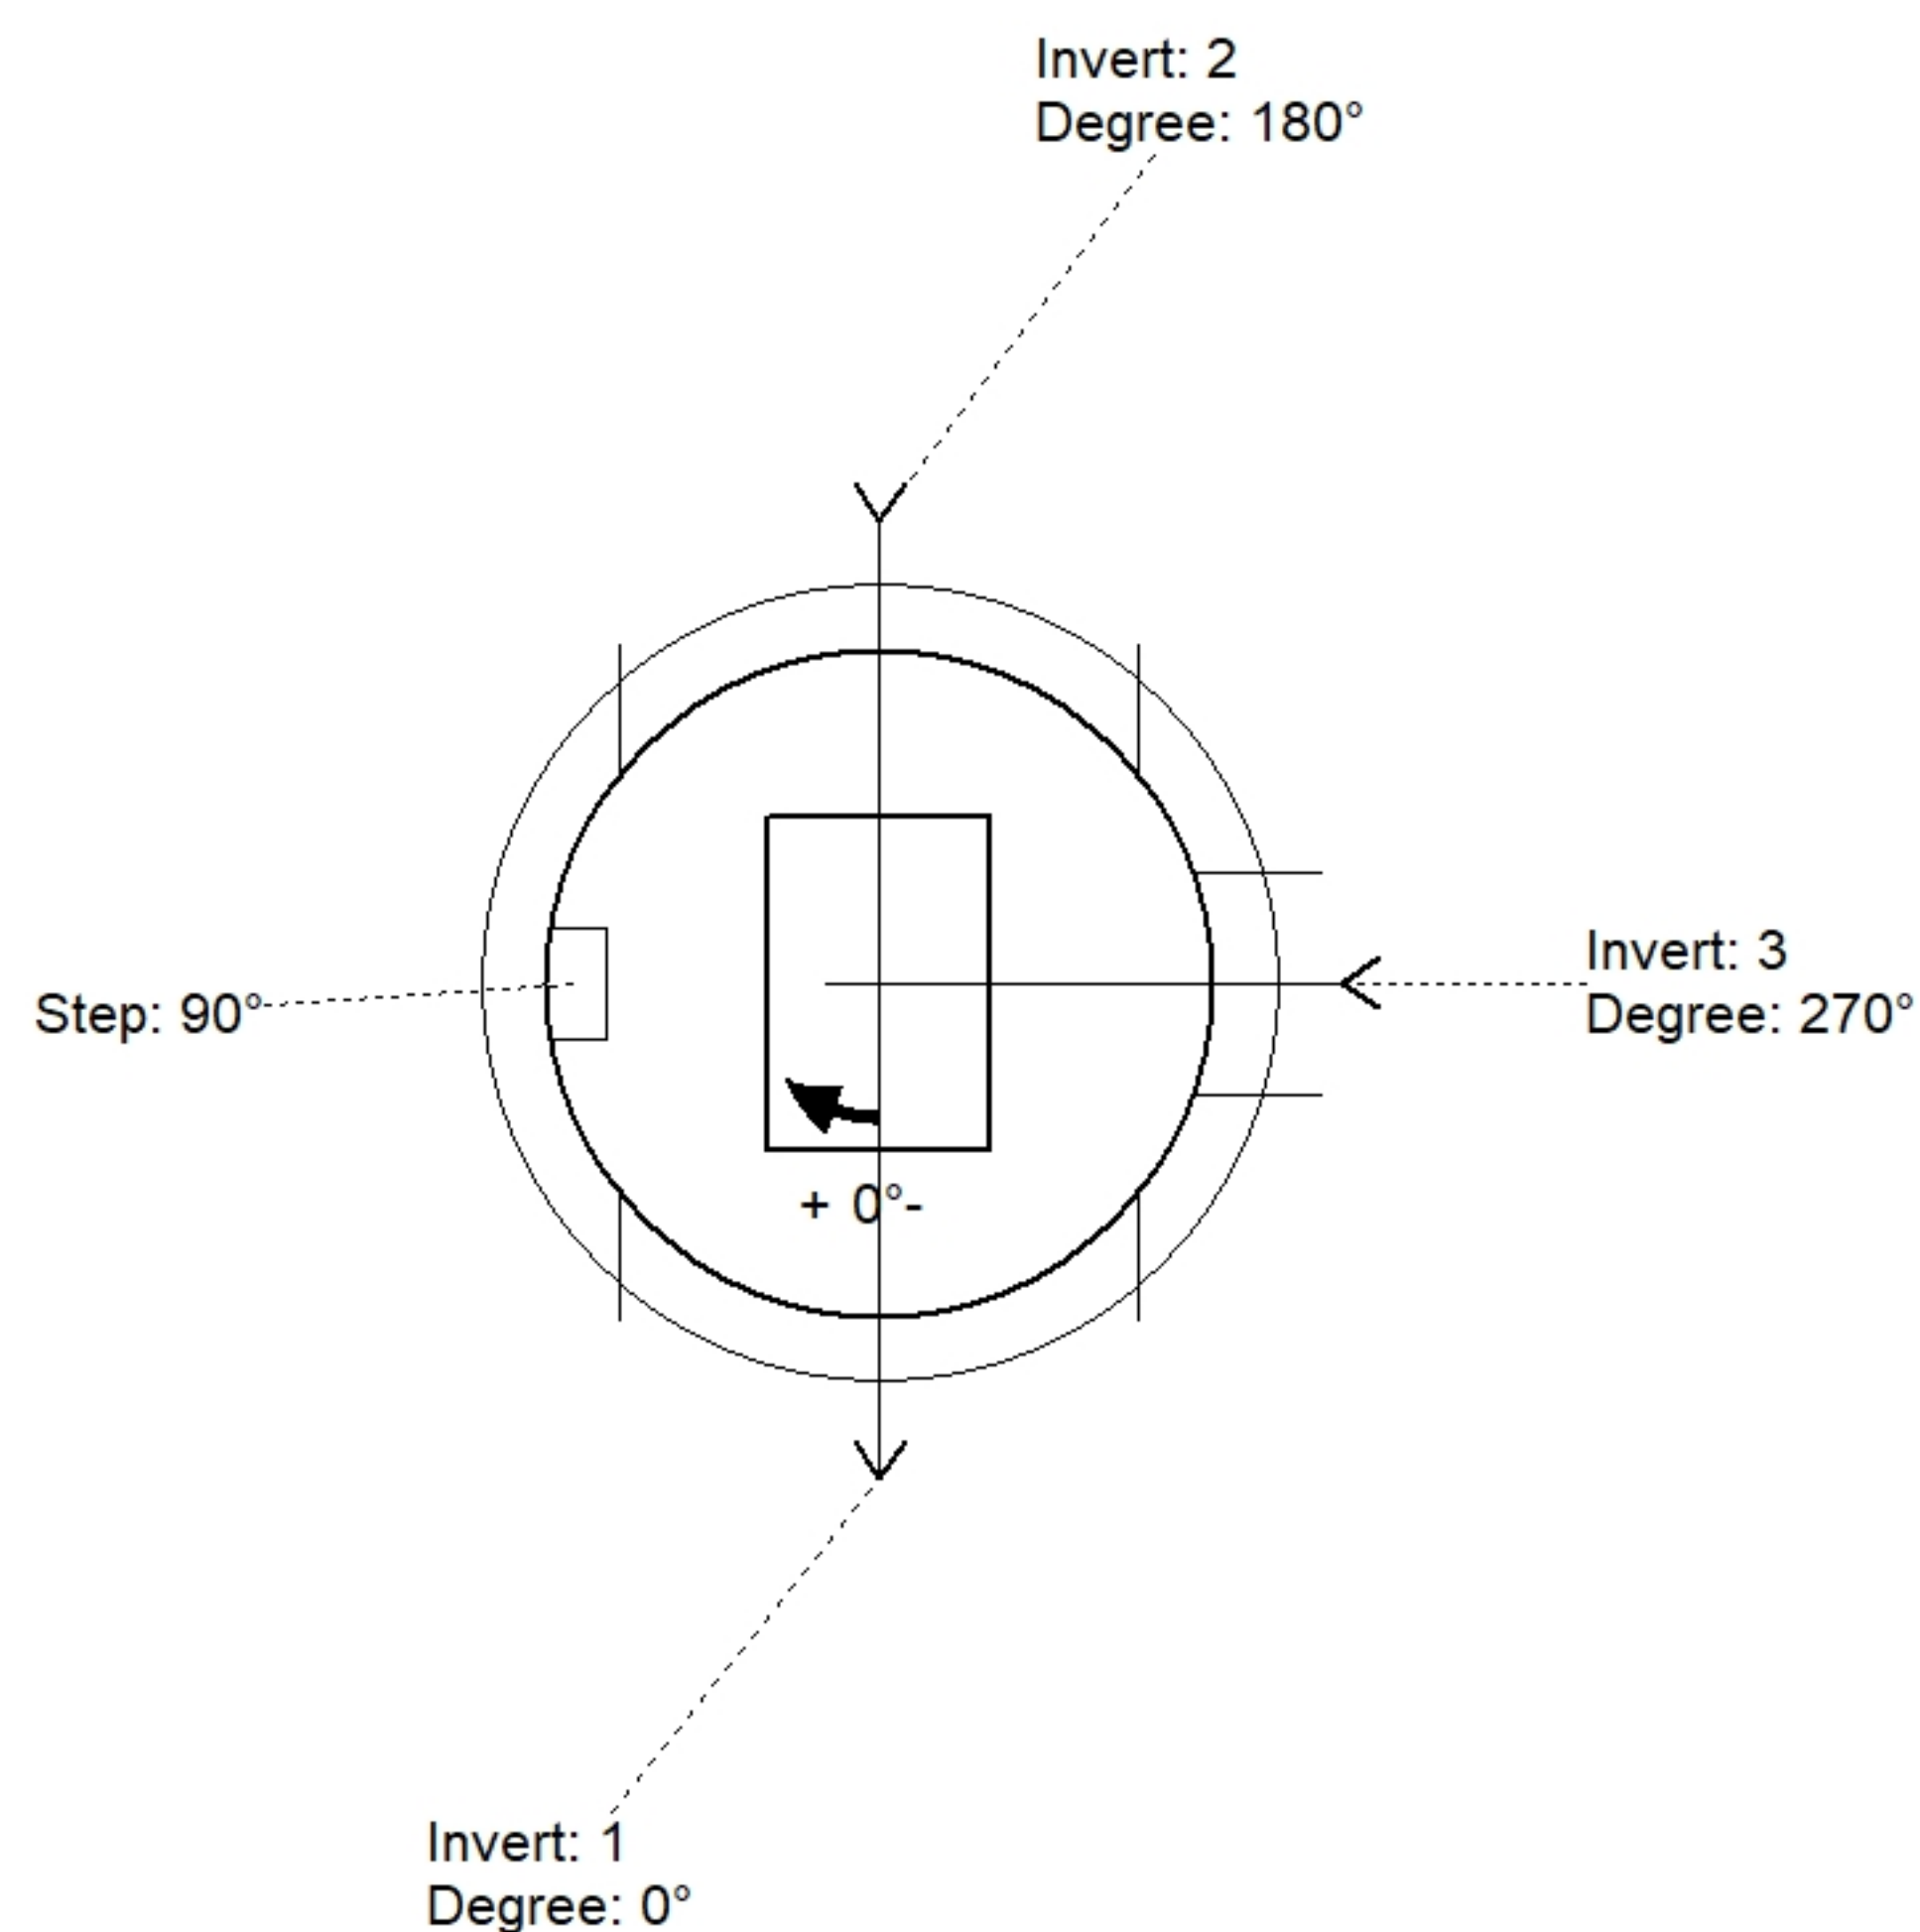

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⎵)	Ref
Rim	932.92'							
Reducer								
Invert 1	924.75'	0°	48" HDPE	53.5"	56"	Hole 56	0.05"	P1
Invert 2	924.75'	180°	48" HDPE	53.5"	56"	Hole 56	0.05"	P1
Invert 3	926.99'	270°	18" HDPE	21.2"	24"	Hole 24	28.28"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

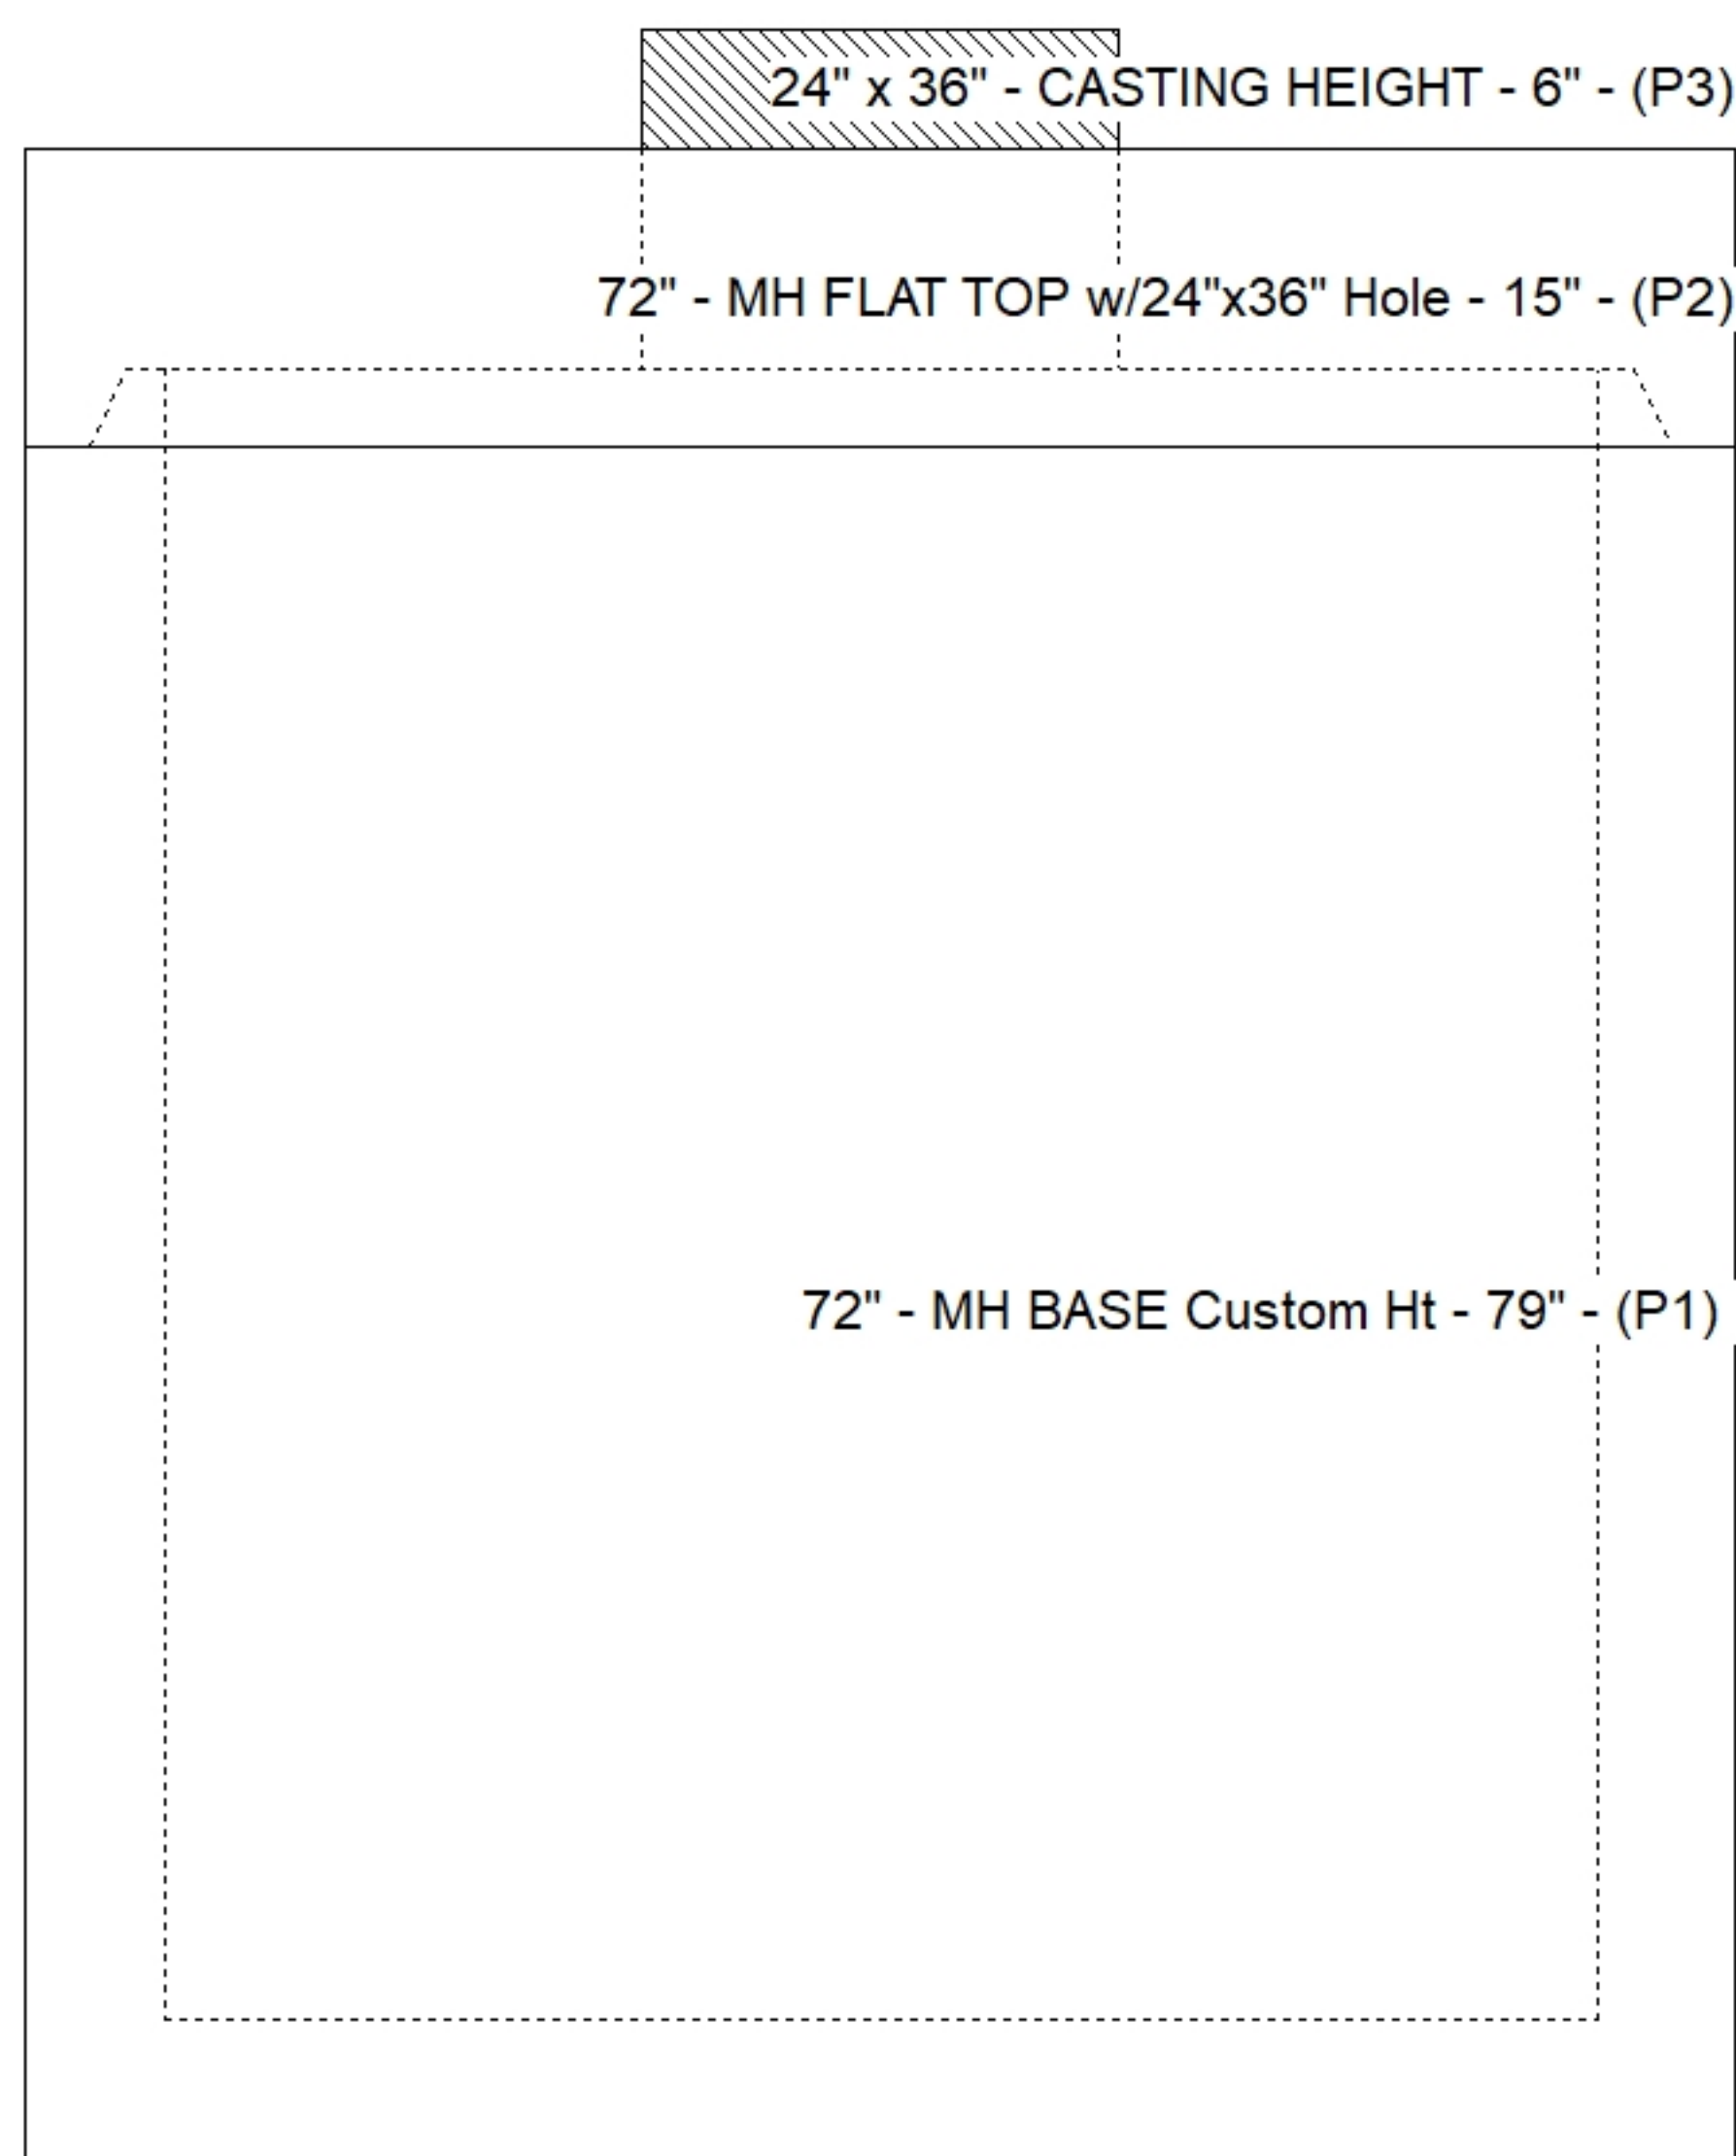

Default - Interior Dimensions

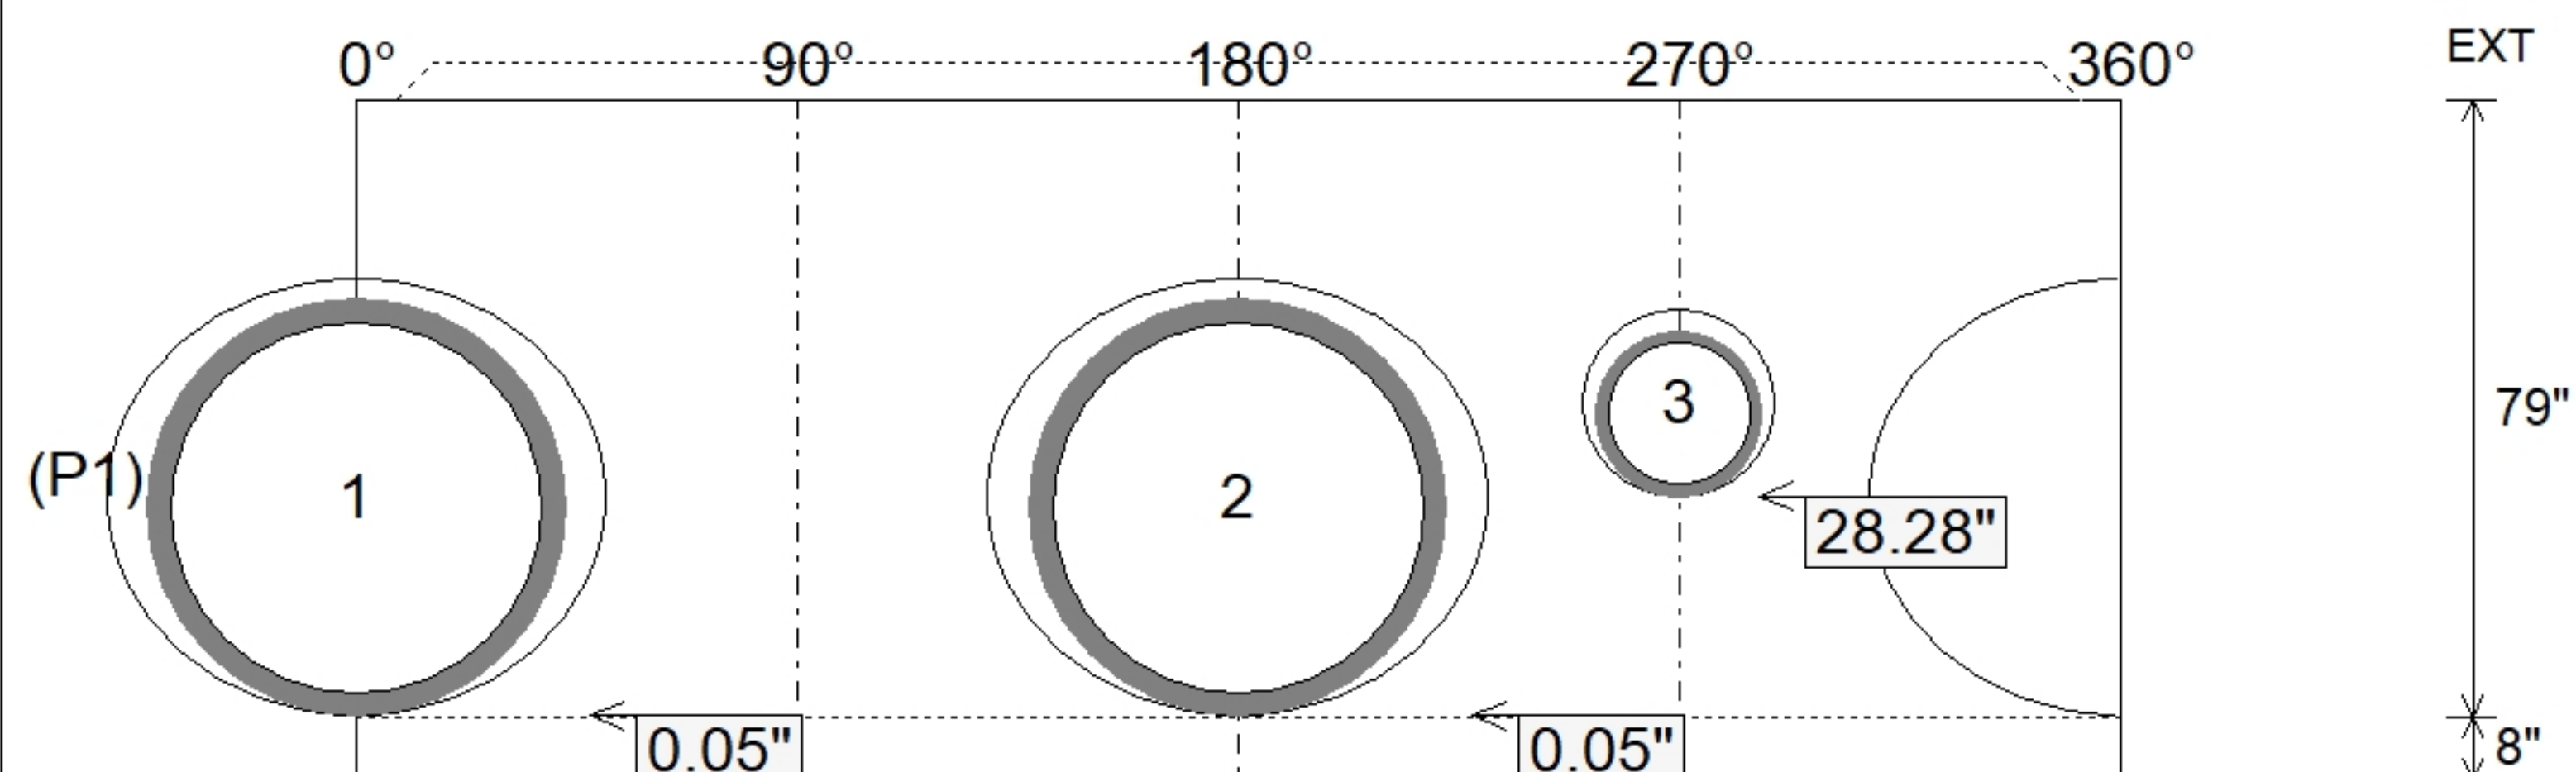

Submittal Drawing
9/29/2026 8:25:56 AM

SUBMITTAL
APPROVED BY:
