

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5.59'

Floor Height: 6"

Slack: 1.705"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE Custom Ht - 49"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 24
4) MH Step ML-10-TDS-NCR - 10"

0 lb
1300 lb
4454 lb
442 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 6196 lb

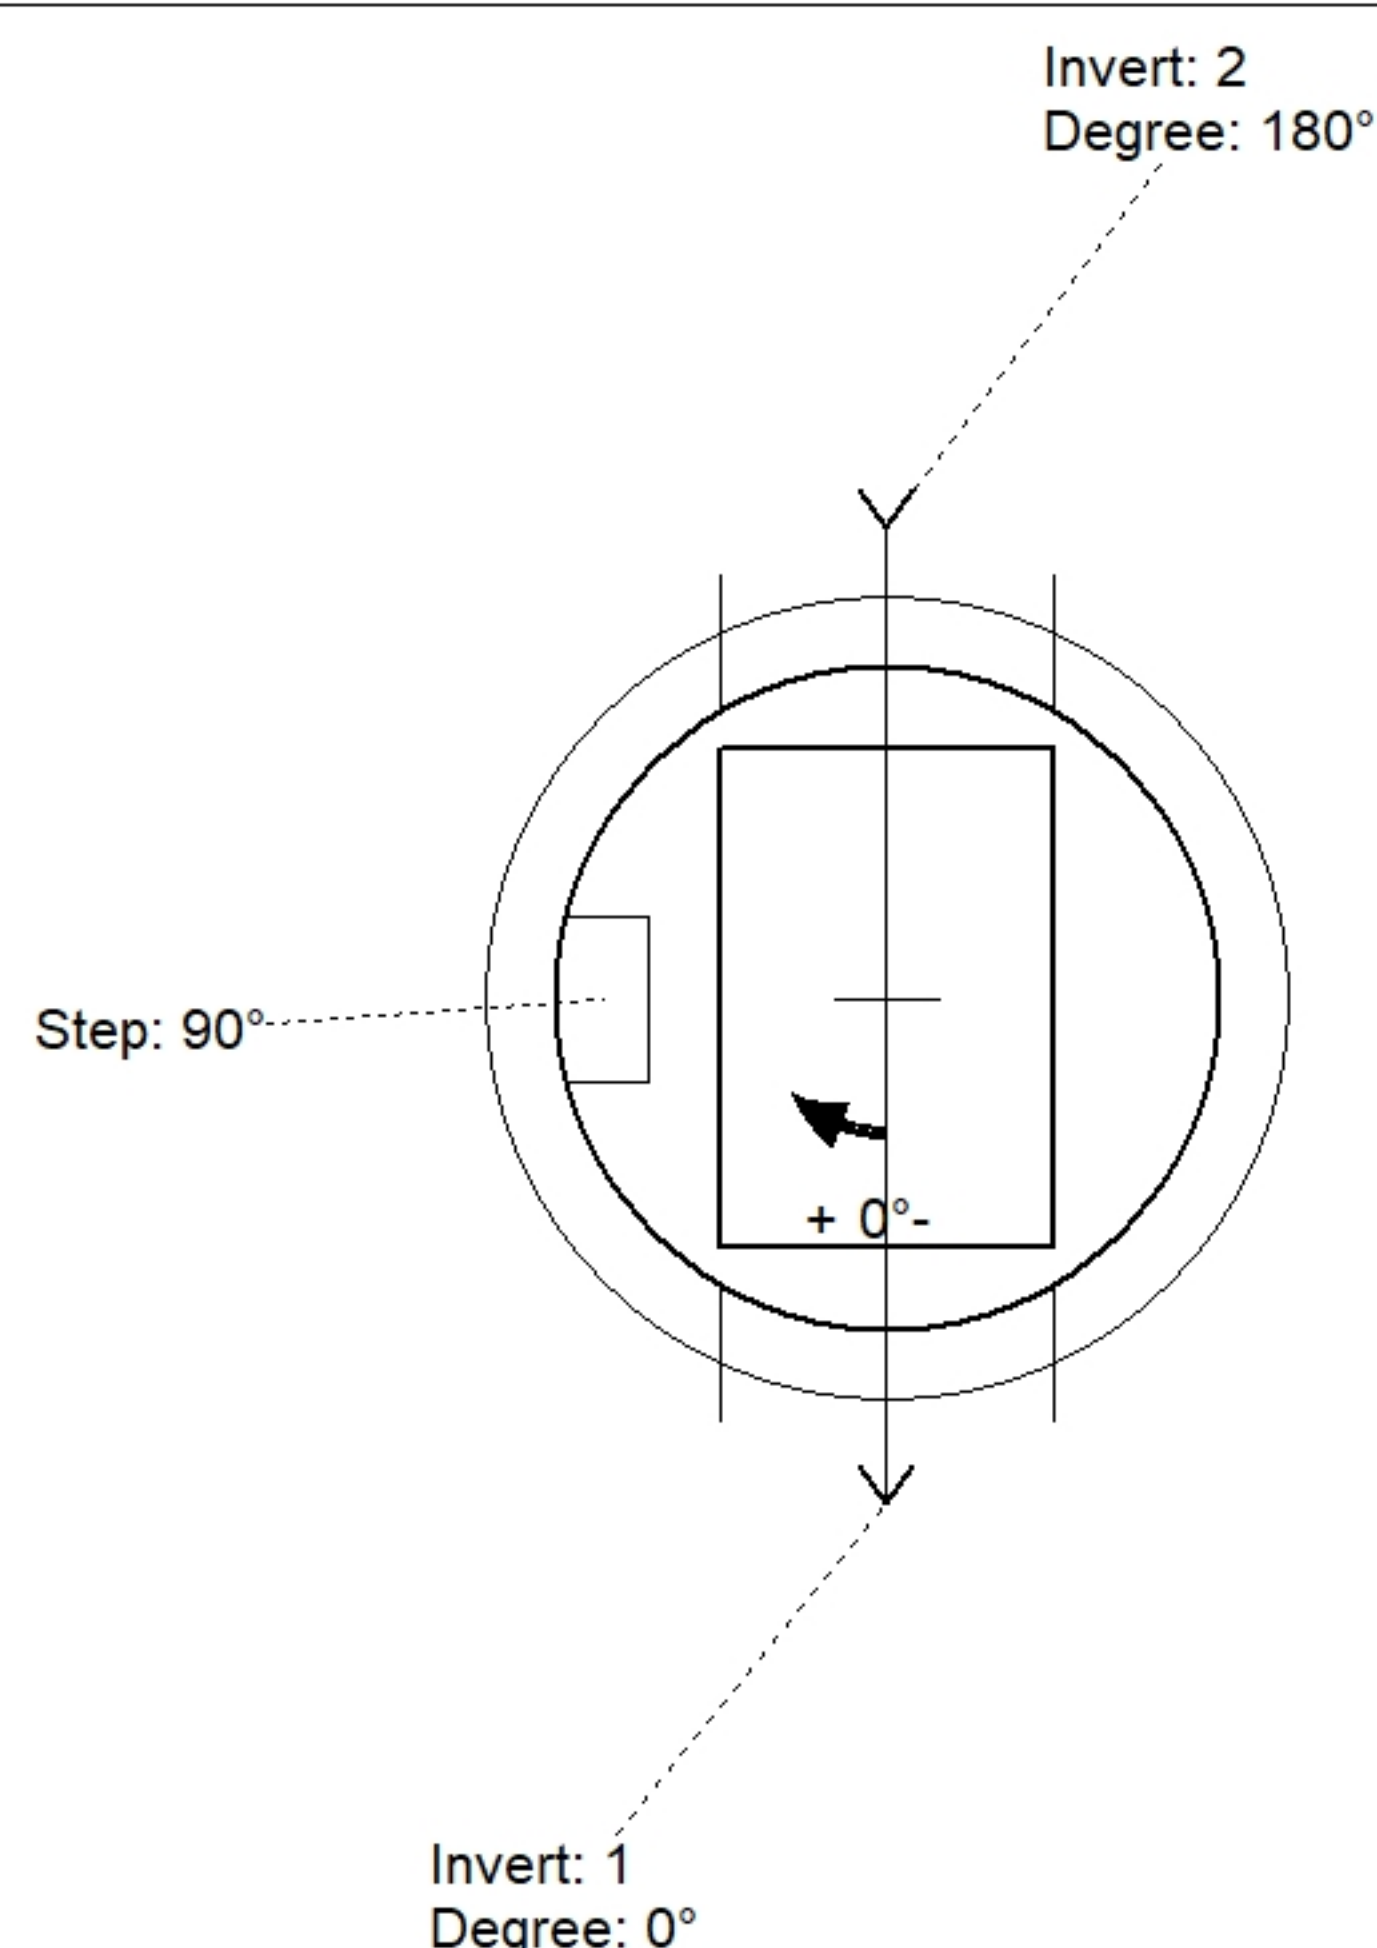

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	933.41'							
Reducer								
Invert 1	927.82'	0°	18" HDPE	21.2"	24"	Hole 24	0.025"	P1
Invert 2	927.82'	180°	18" HDPE	21.2"	24"	Hole 24	0.025"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

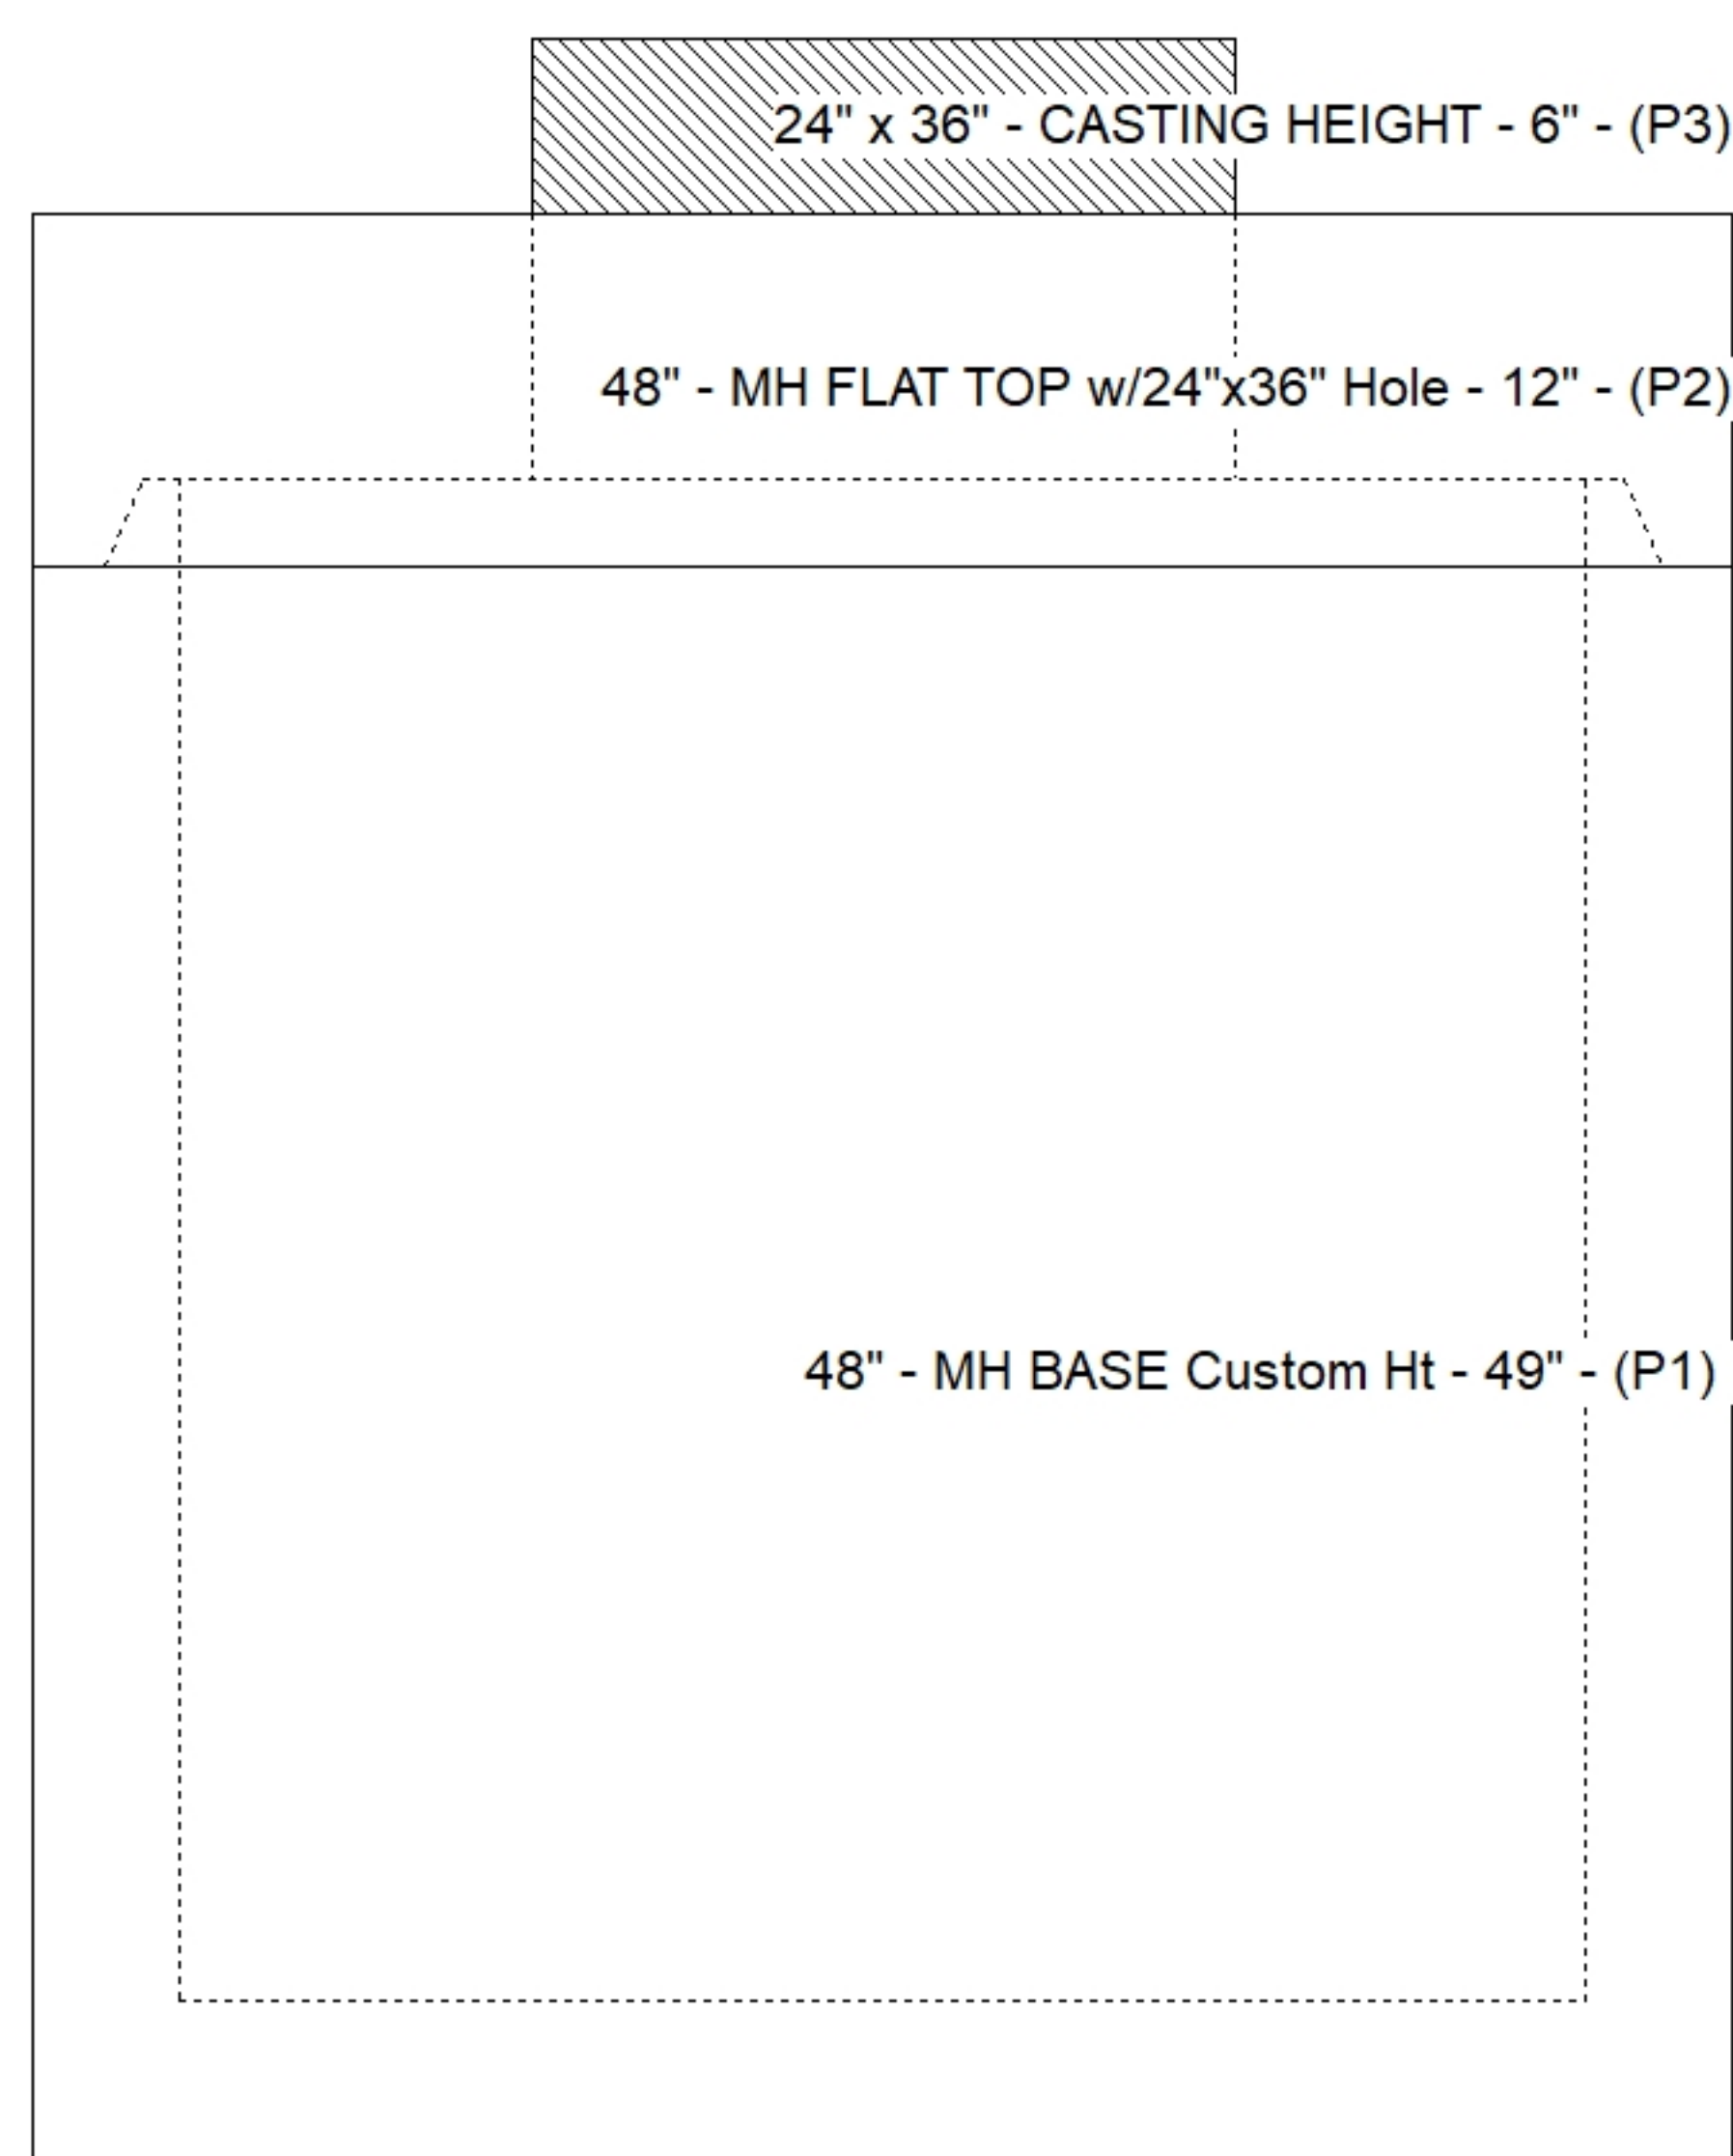

Default - Interior Dimensions

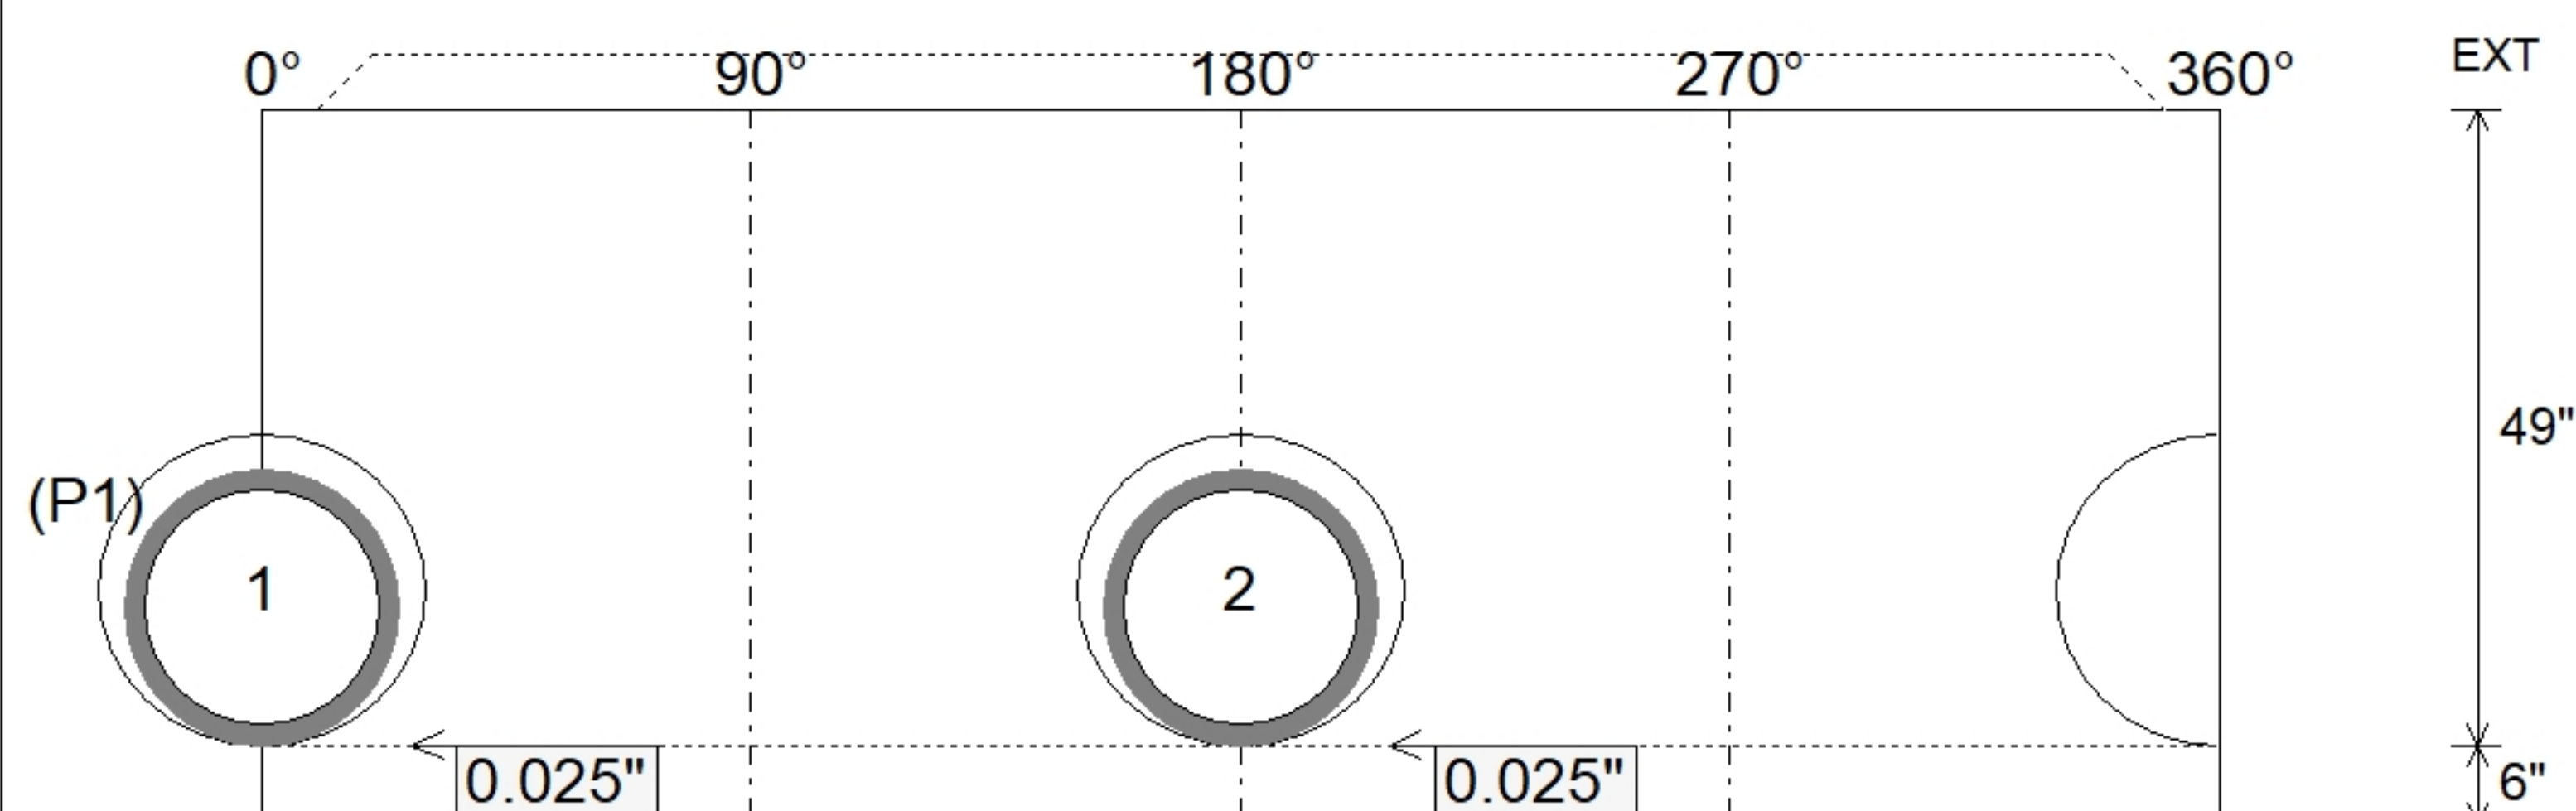

Submittal Drawing
9/29/2026 8:25:55 AM

SUBMITTAL
APPROVED BY:
