

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 3.3'

Floor Height: 8"


Slack: 1.225"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 34"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 24

0 lb
4638 lb
442 lb
0 lb
0 lb

Structure Total: 5080 lb

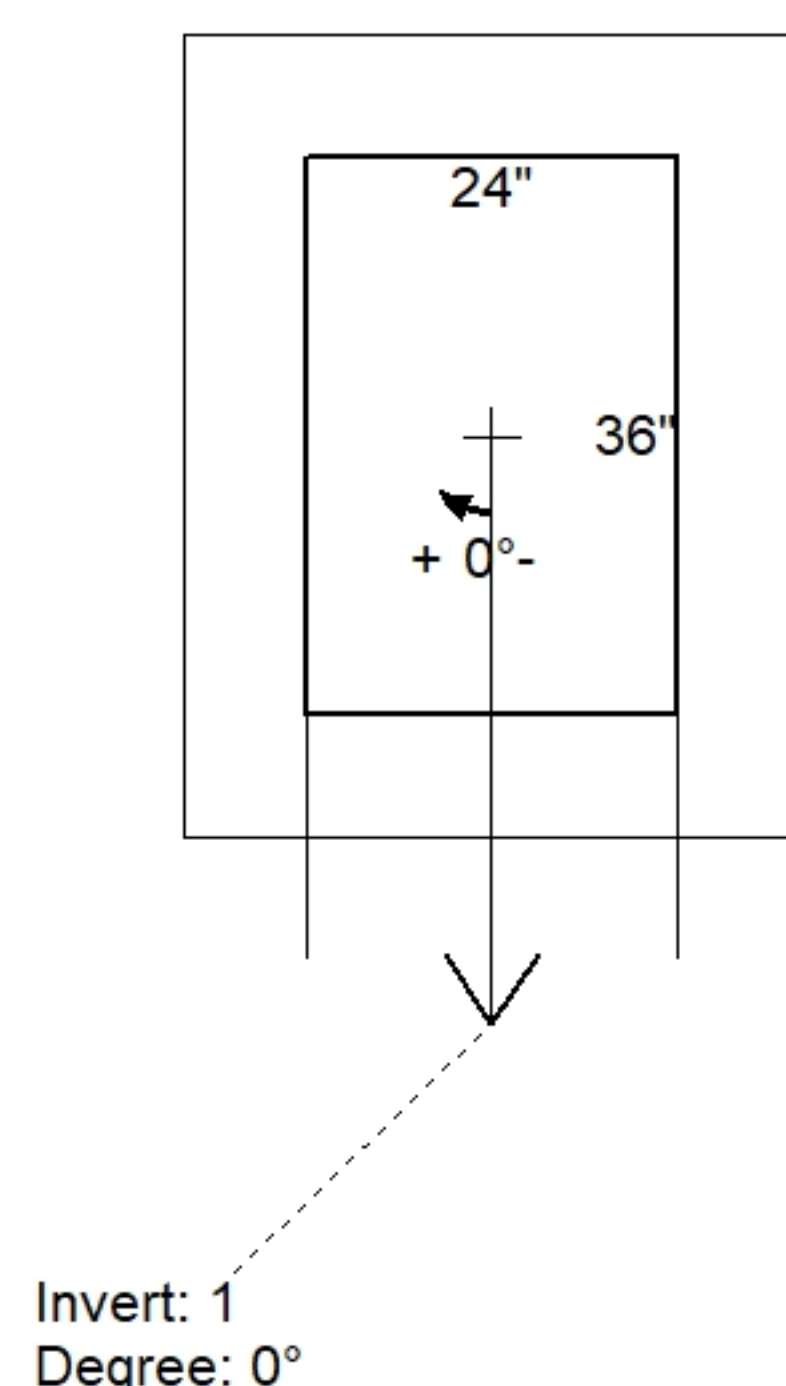


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	933.15'							
Reducer								
Invert 1	929.85'	0°	18" HDPE	21.2"	24"	Hole 24	0.025"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 34" - (P1)

Default - Interior Dimensions

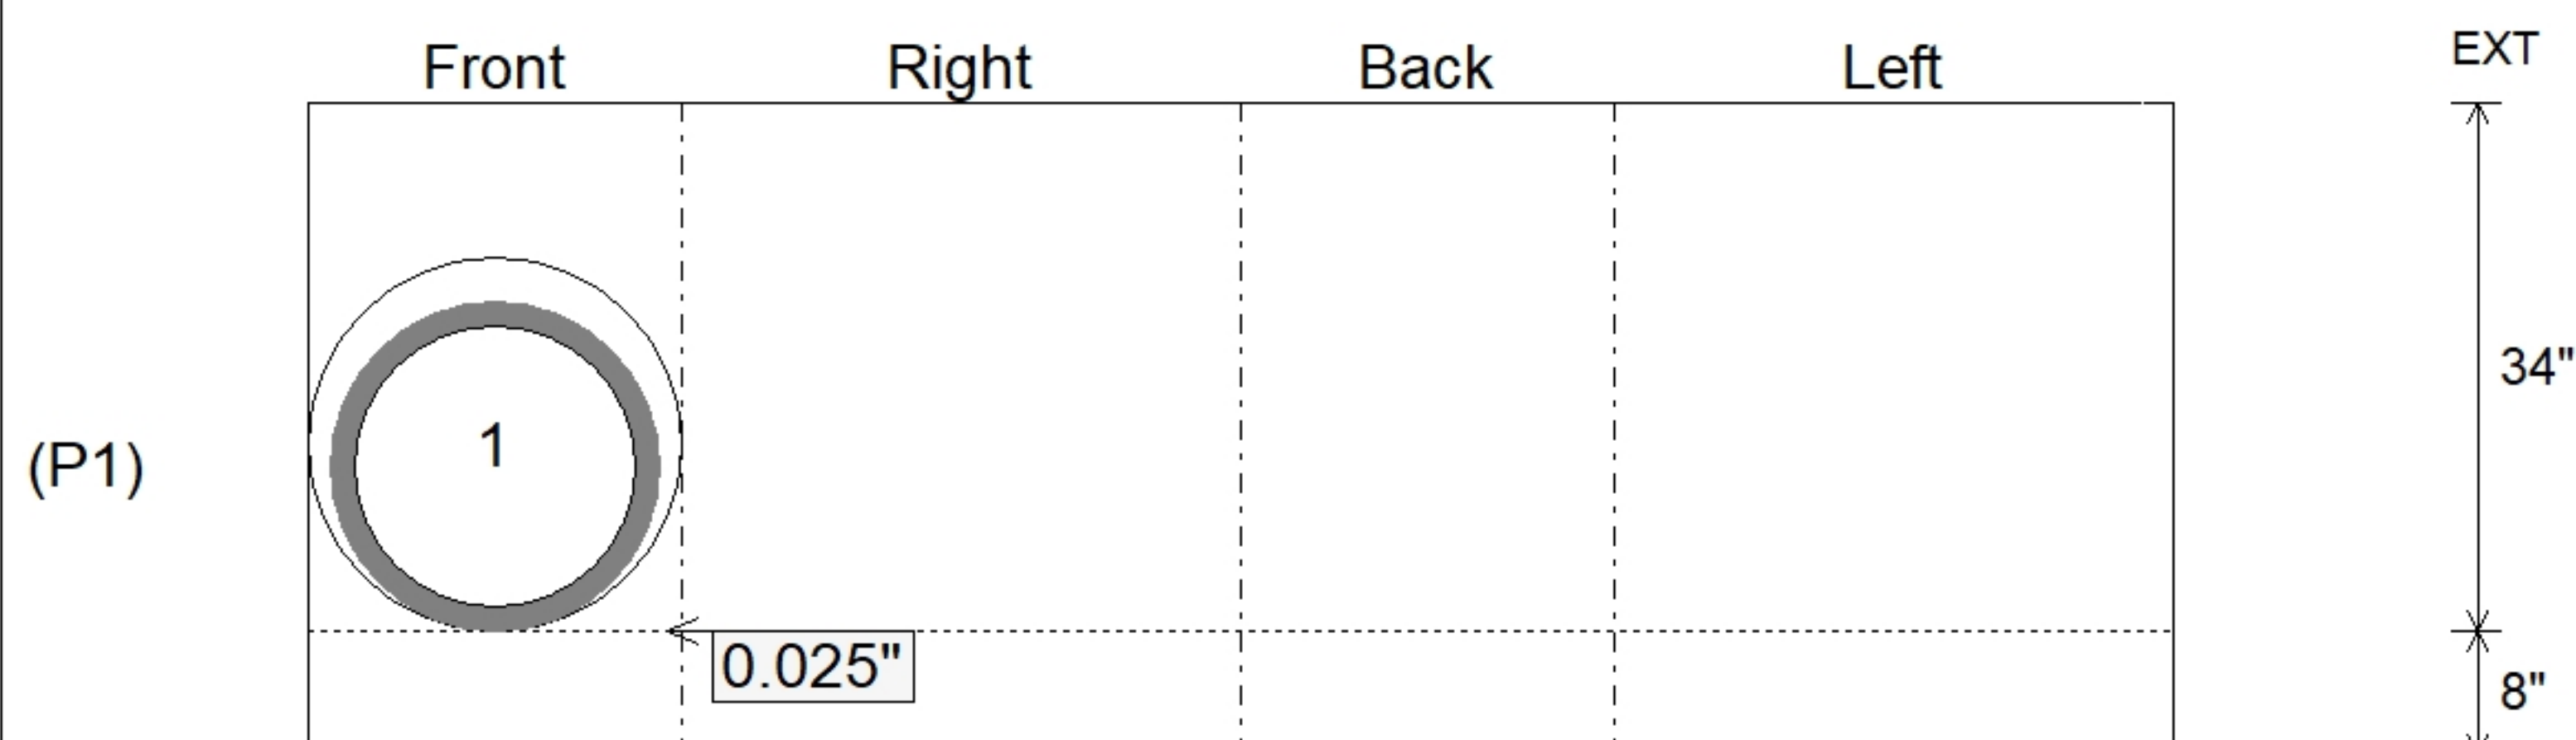

Submittal Drawing
9/29/2026 8:25:55 AM

SUBMITTAL
APPROVED BY:
