

Contractor: KY Earthworks

TECH:	Jared - F
-------	-----------

Plant: 100




Slack: 1.43"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 72" - MH FLAT TOP w/24"x36" Hole - 10"
- P1) 72" - MH BASE - 60"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 72" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 56
- 2) Hole - 24
- 1) Hole - 50
- 5) MH Step ML-10-TDS-NCR - 10"



0 lb
4149 lb
9237 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 13828 lb

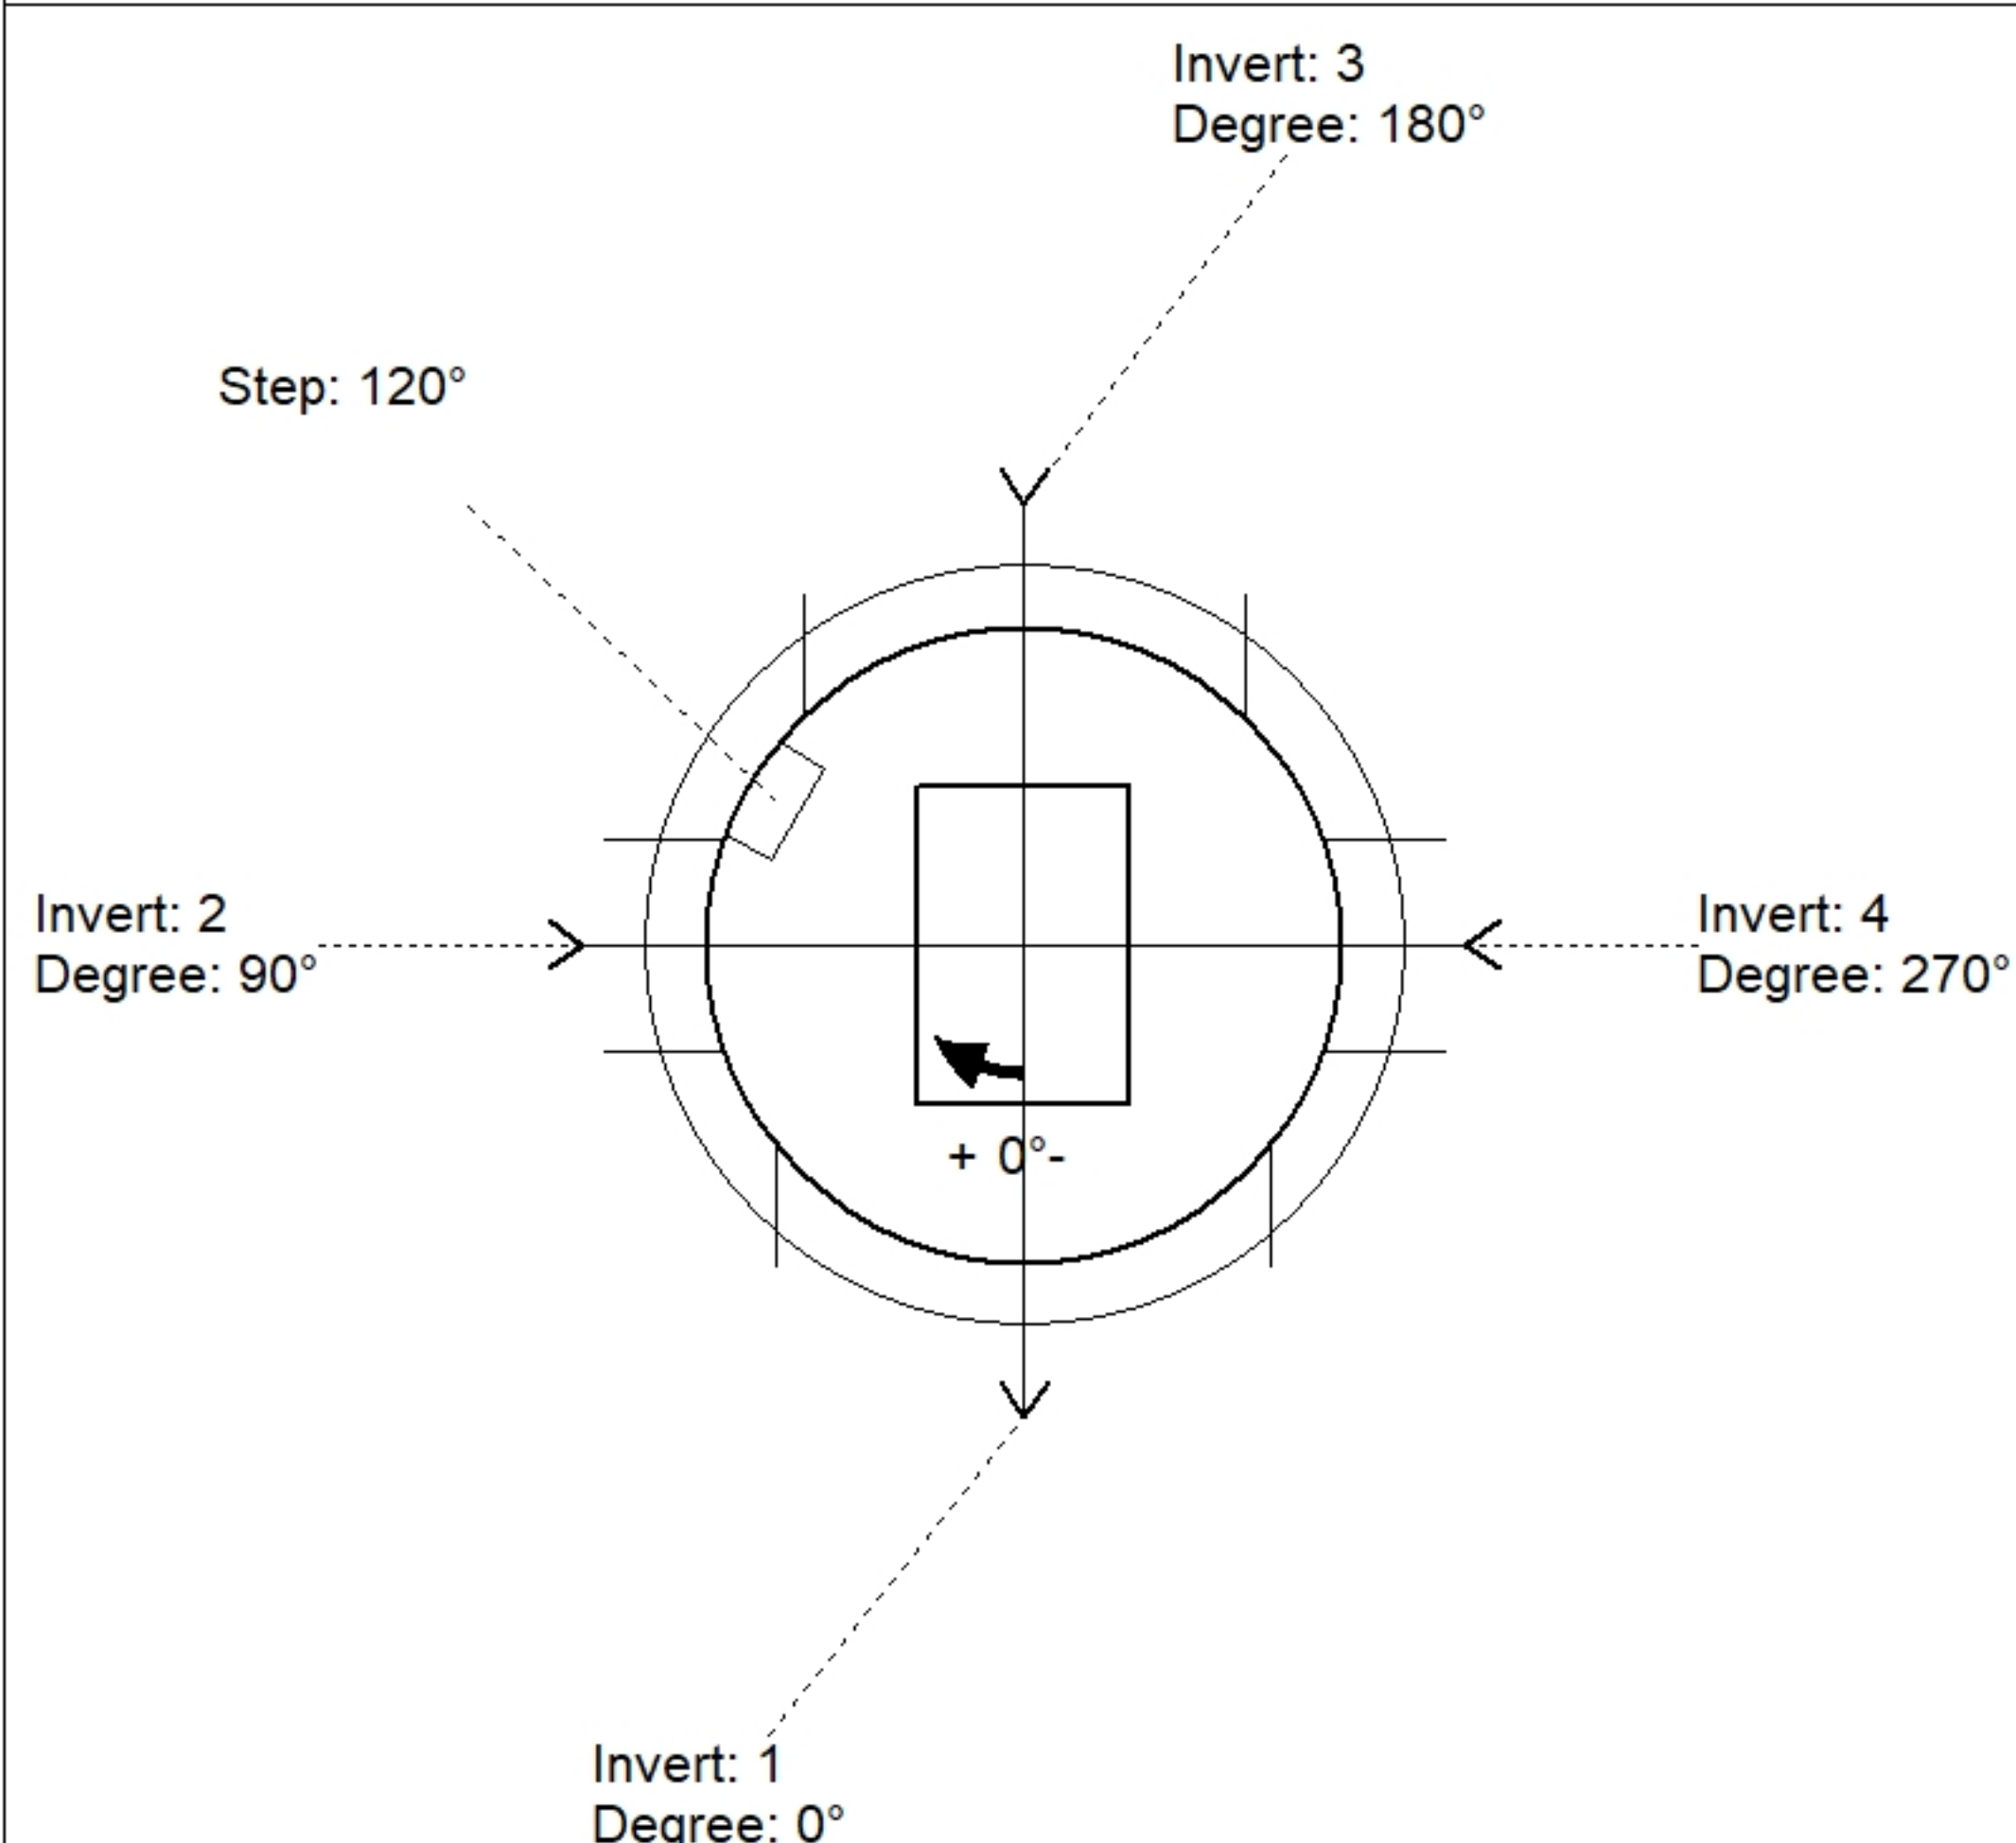

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	931.56'							
Reducer								
Invert 1	925.37'	0°	48" HDPE	53.5"	56"	Hole 56	0.2"	P1
Invert 2	926.5'	90°	18" HDPE	21.2"	24"	Hole 24	15.11"	P1
Invert 3	925.37'	180°	42" HDPE	47.7"	50"	Hole 50	0"	P1
Invert 4	926.67'	270°	18" HDPE	21.2"	24"	Hole 24	17.15"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

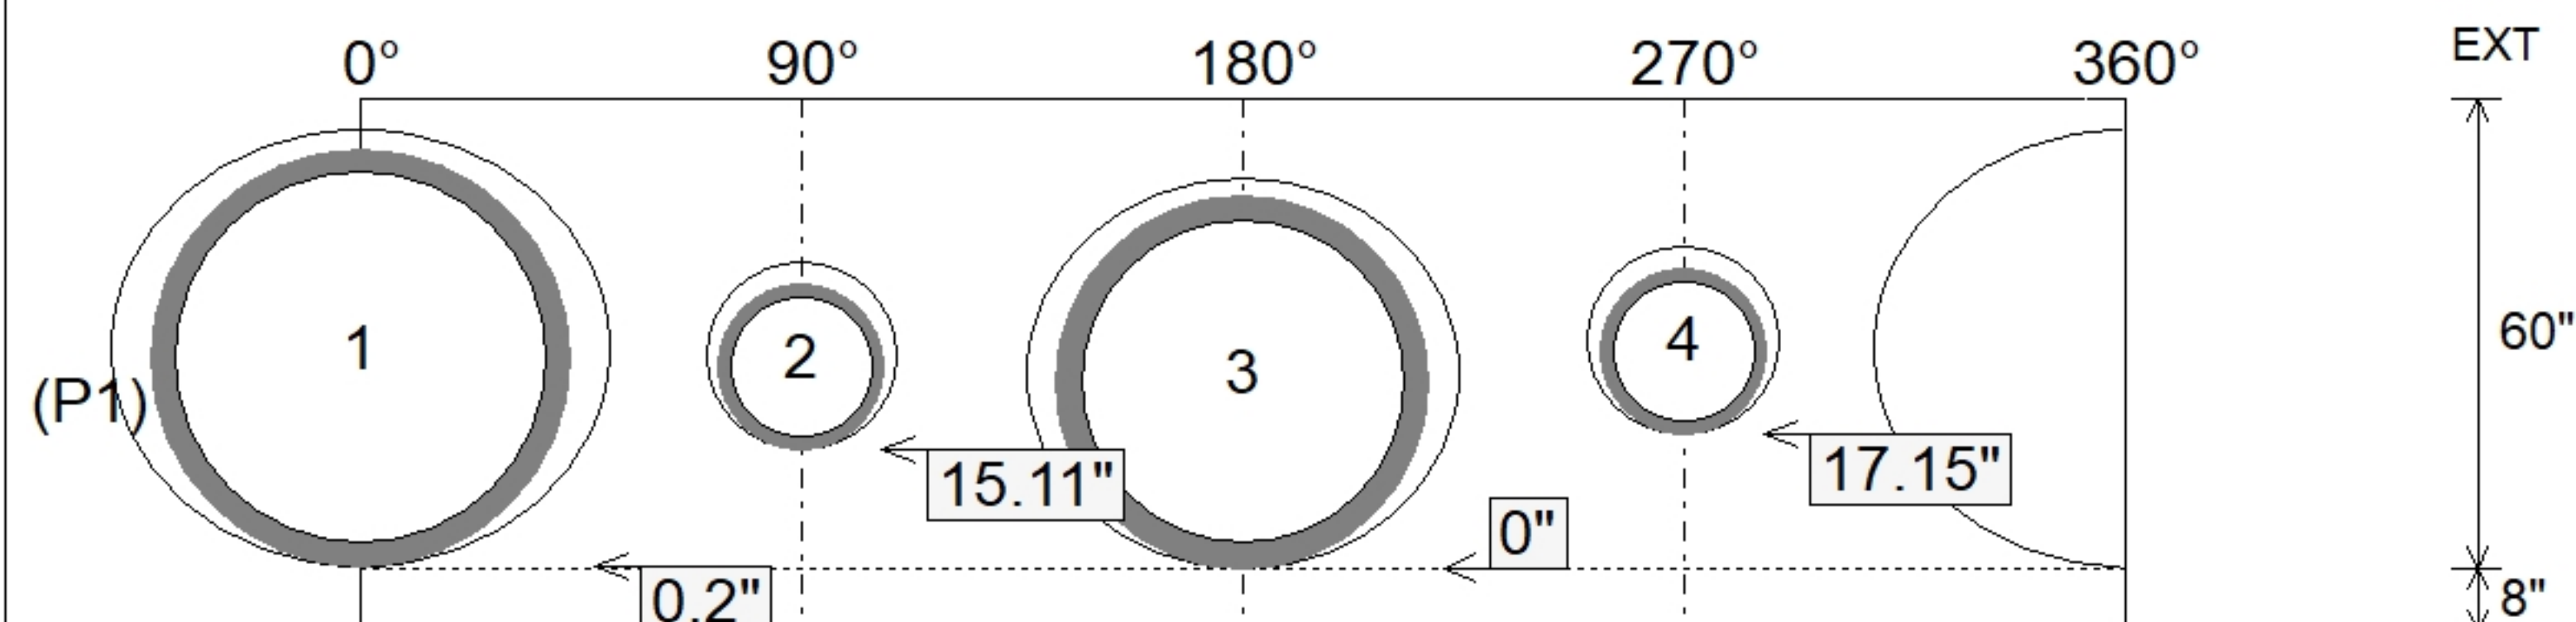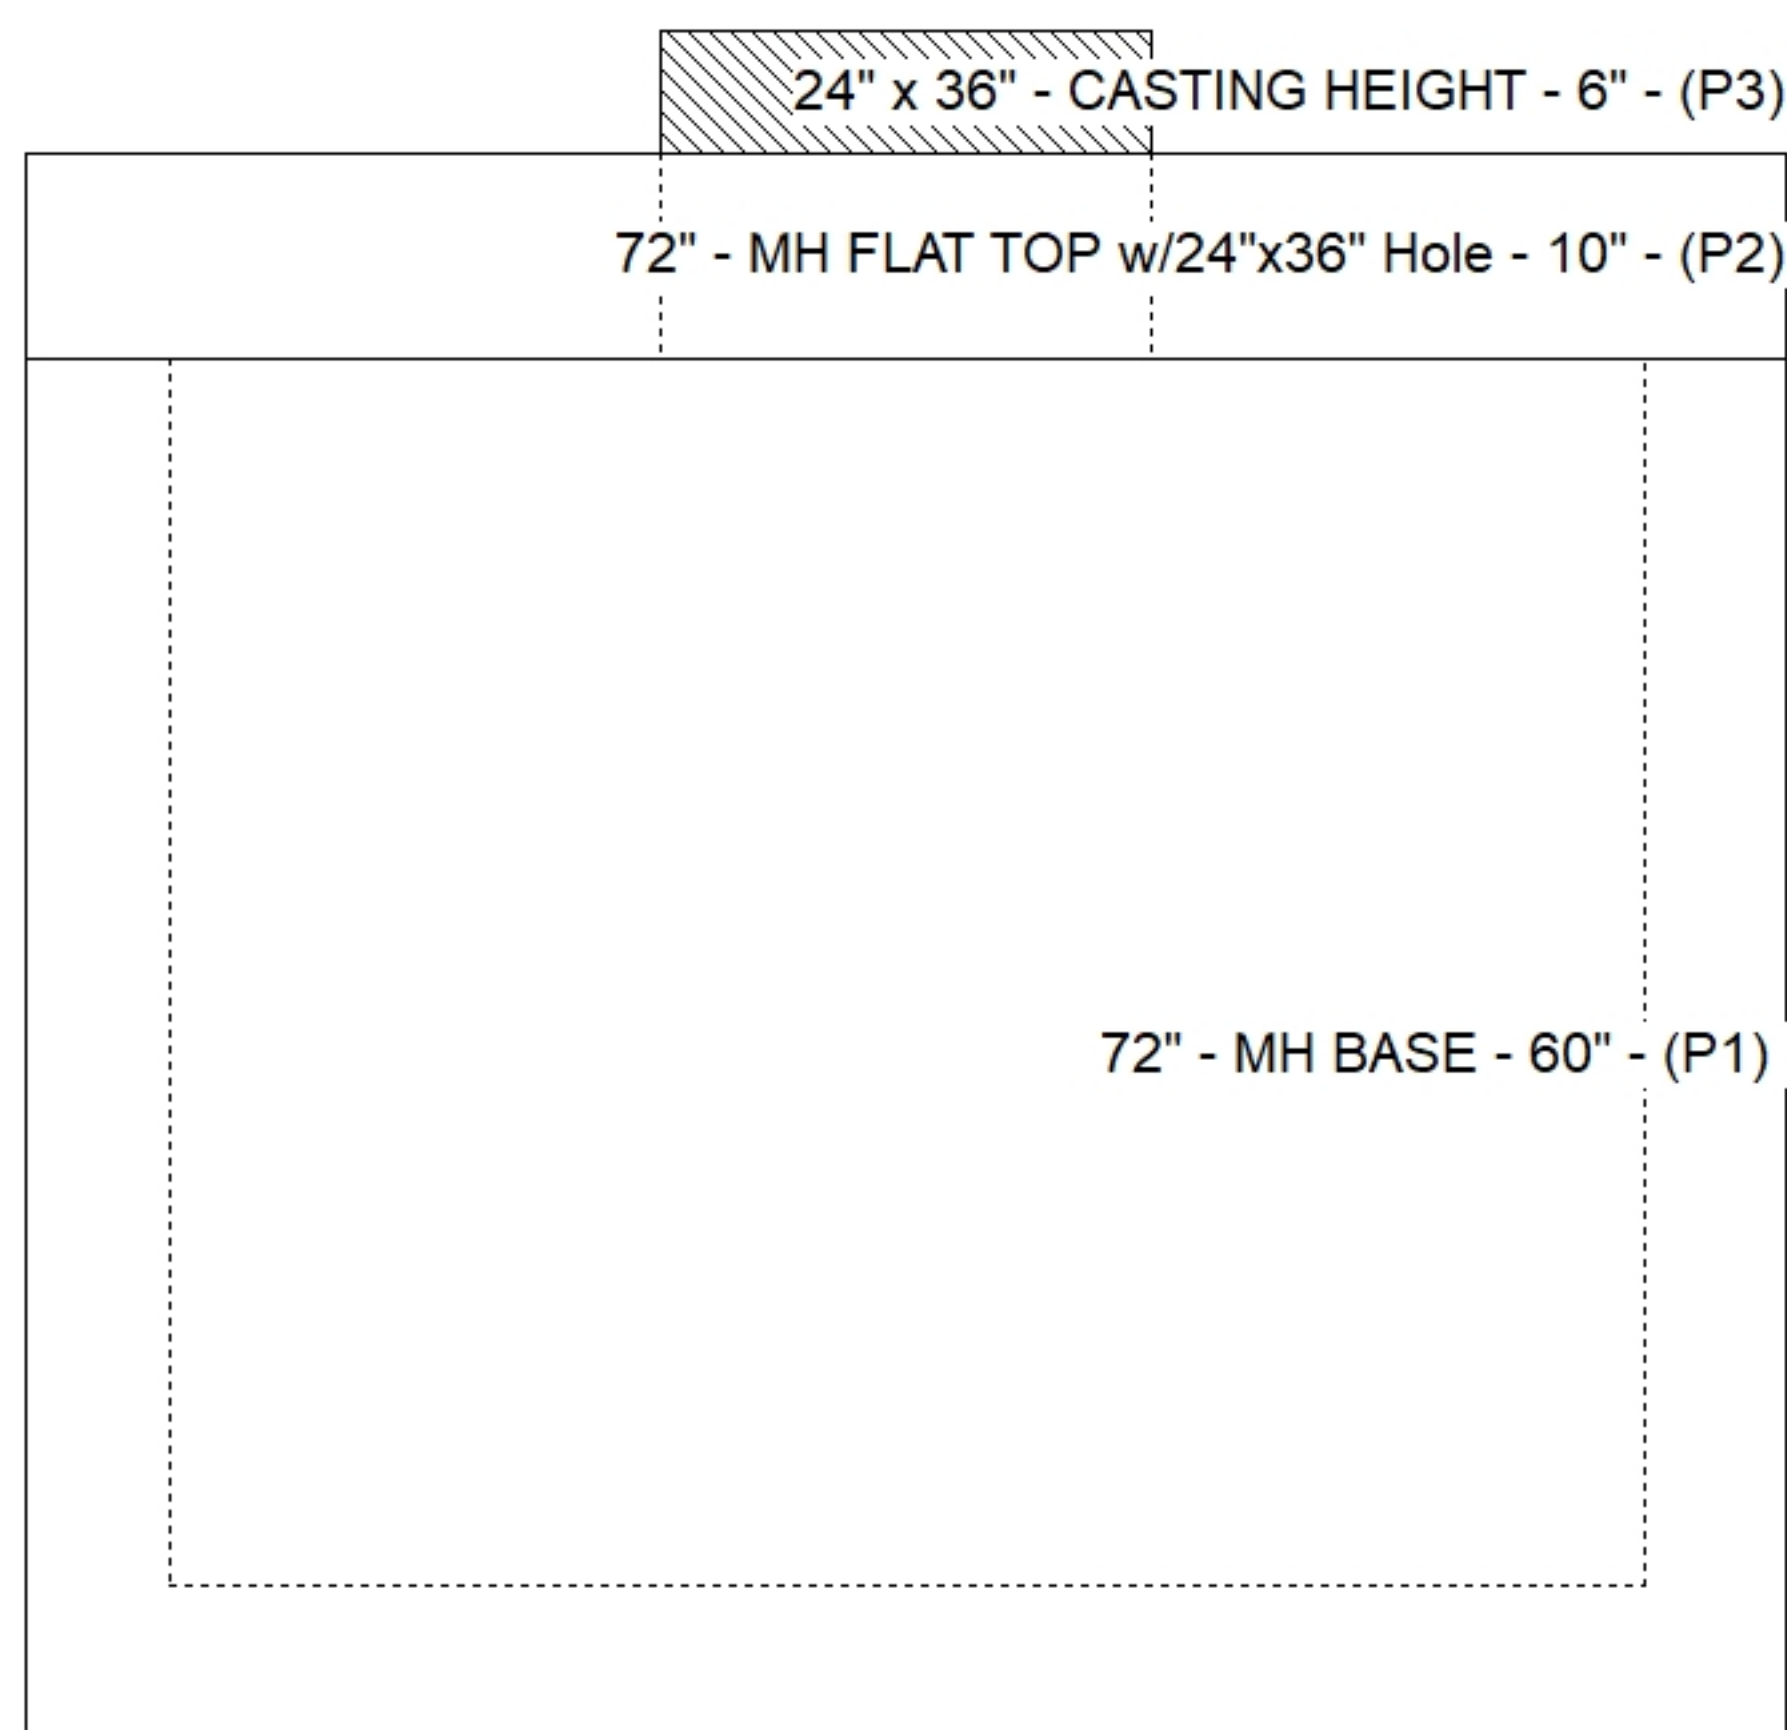

Submittal Drawing
9/29/2026 8:25:54 AM

SUBMITTAL
APPROVED BY:
