

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 72"

Rim to Invert: 5.78'

Floor Height: 8"


Slack: 1.51"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 72" - MH FLAT TOP w/24"x36" Hole - 10"
P1) 72" - MH BASE Custom Ht - 55"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 72" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 50
2) Hole - 24
4) MH Step ML-10-TDS-NCR - 10"

0 lb
4149 lb
8871 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 13463 lb

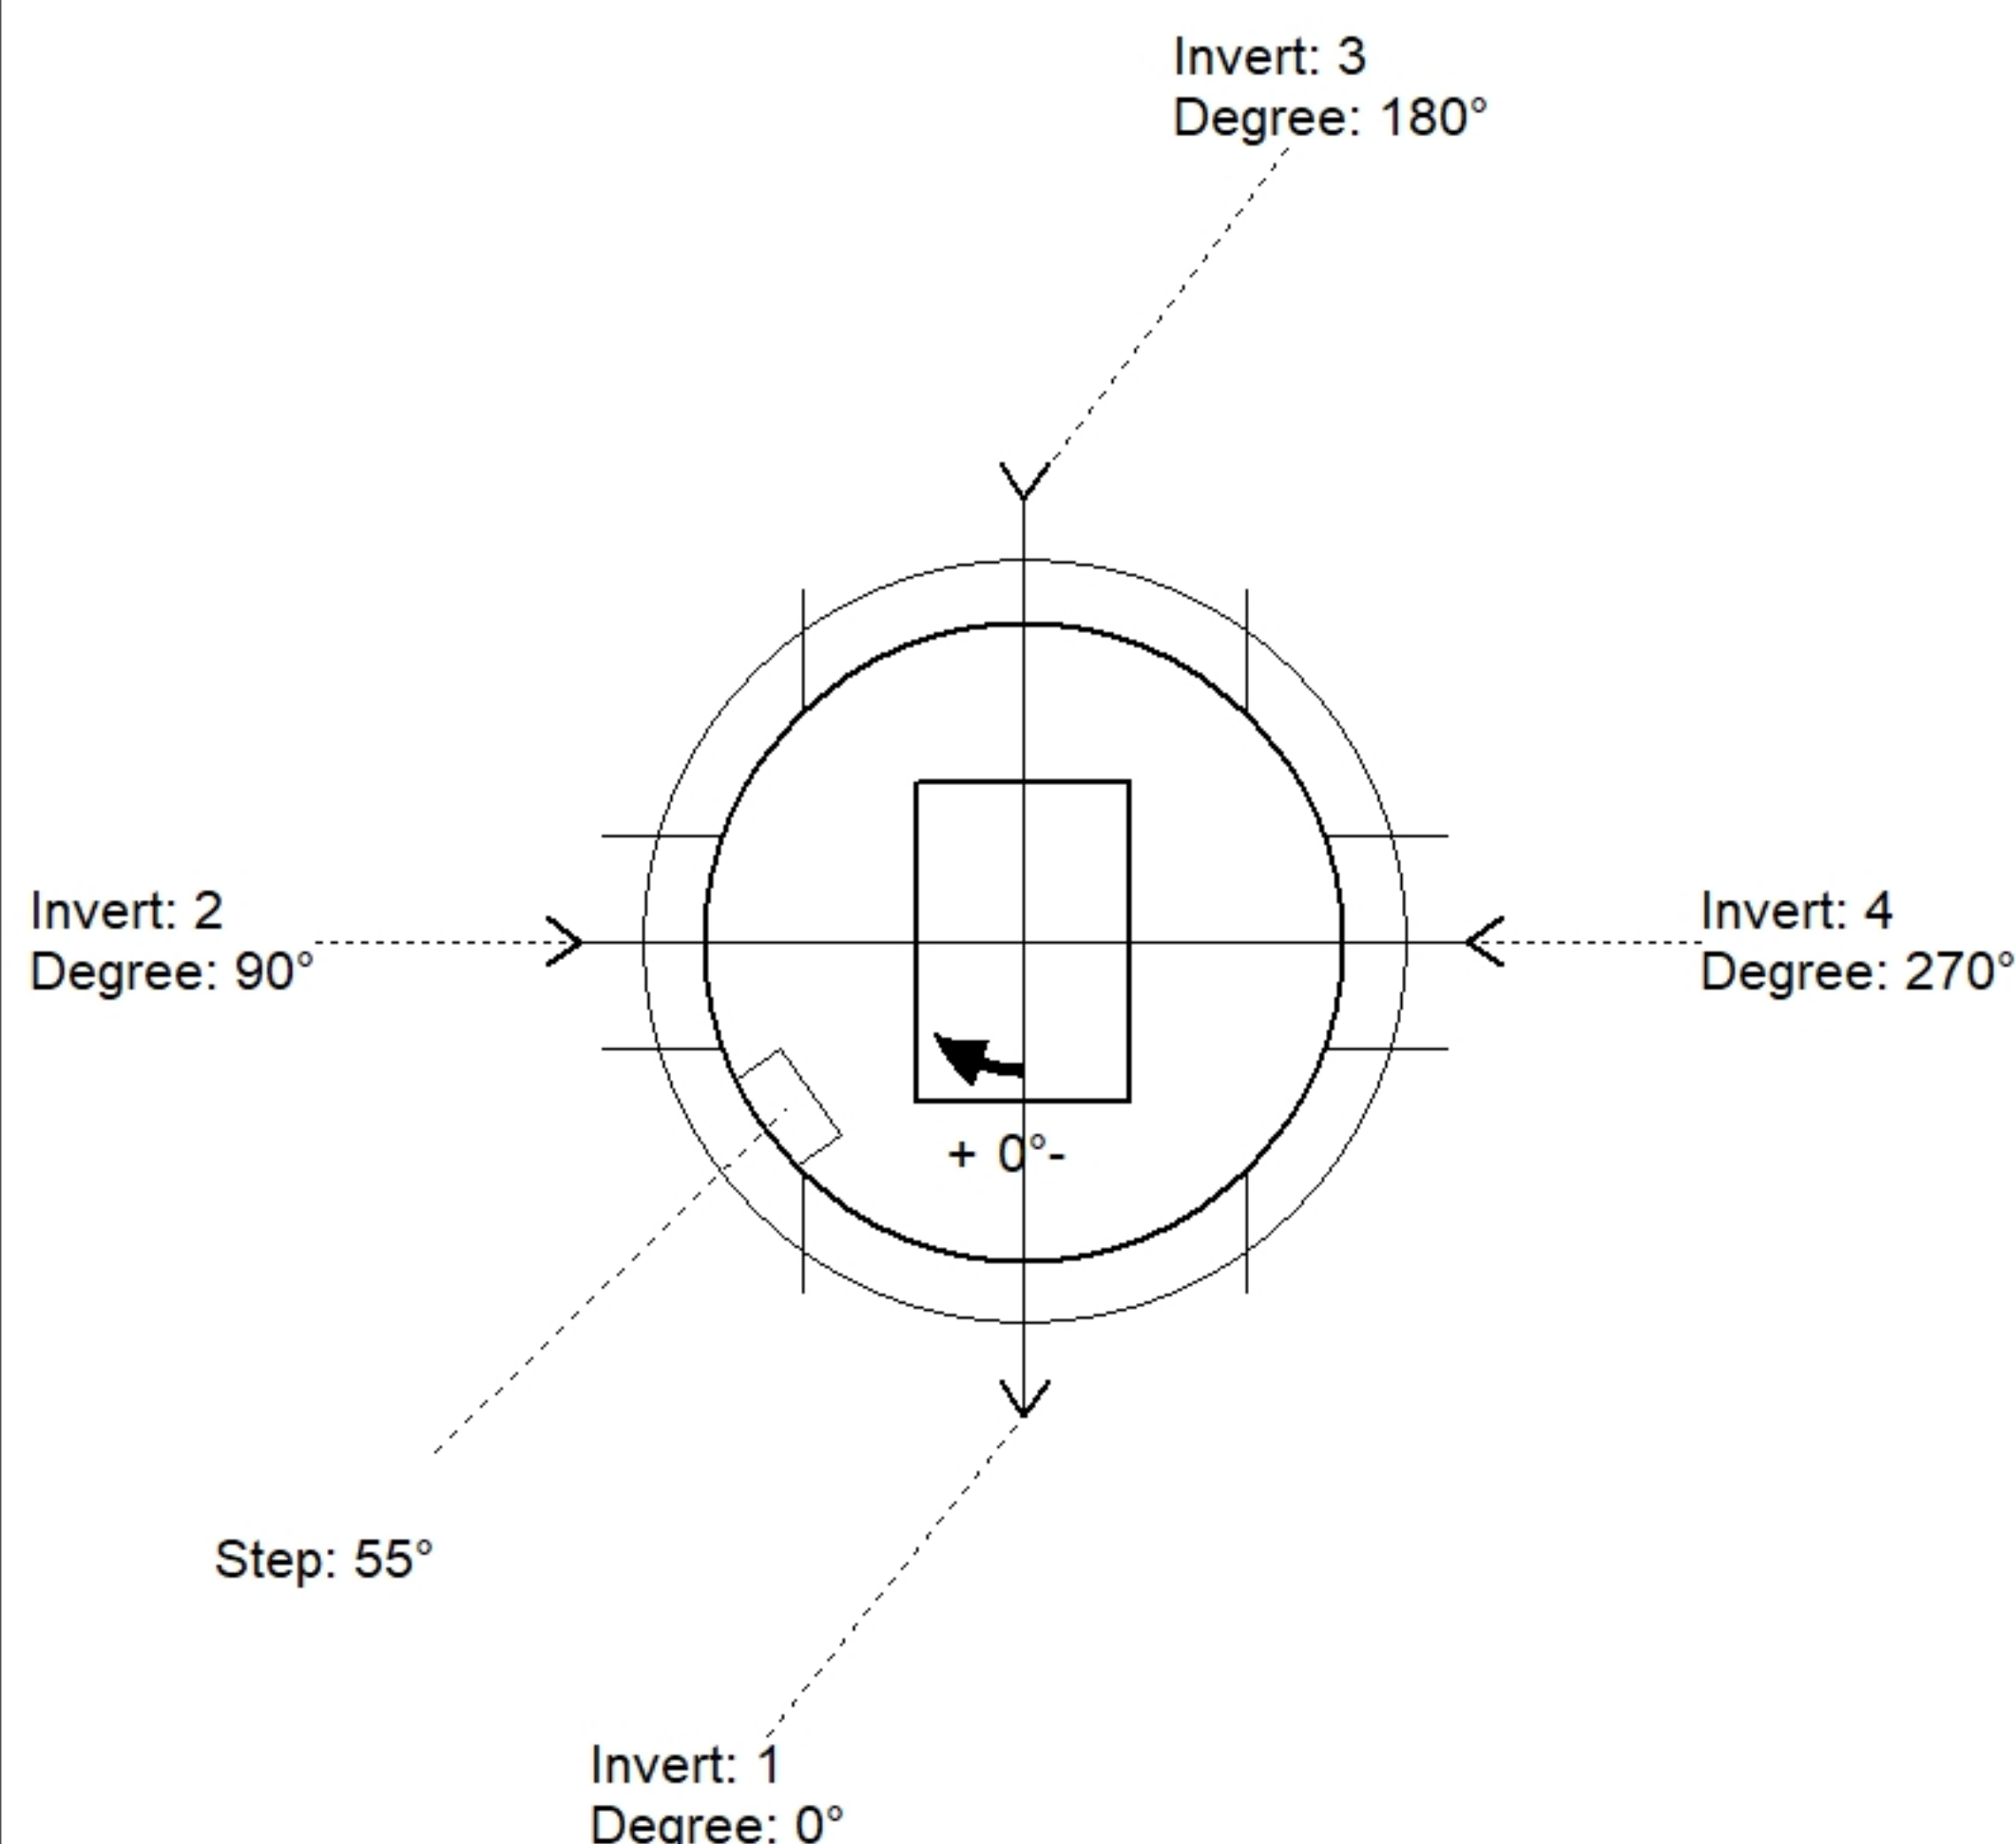

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	932.19'							
Reducer								
Invert 1	926.41'	0°	42" HDPE	47.7"	50"	Hole 50	0"	P1
Invert 2	927.5'	90°	18" HDPE	21.2"	24"	Hole 24	14.63"	P1
Invert 3	926.41'	180°	42" HDPE	47.7"	50"	Hole 50	0"	P1
Invert 4	927.5'	270°	18" HDPE	21.2"	24"	Hole 24	14.63"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

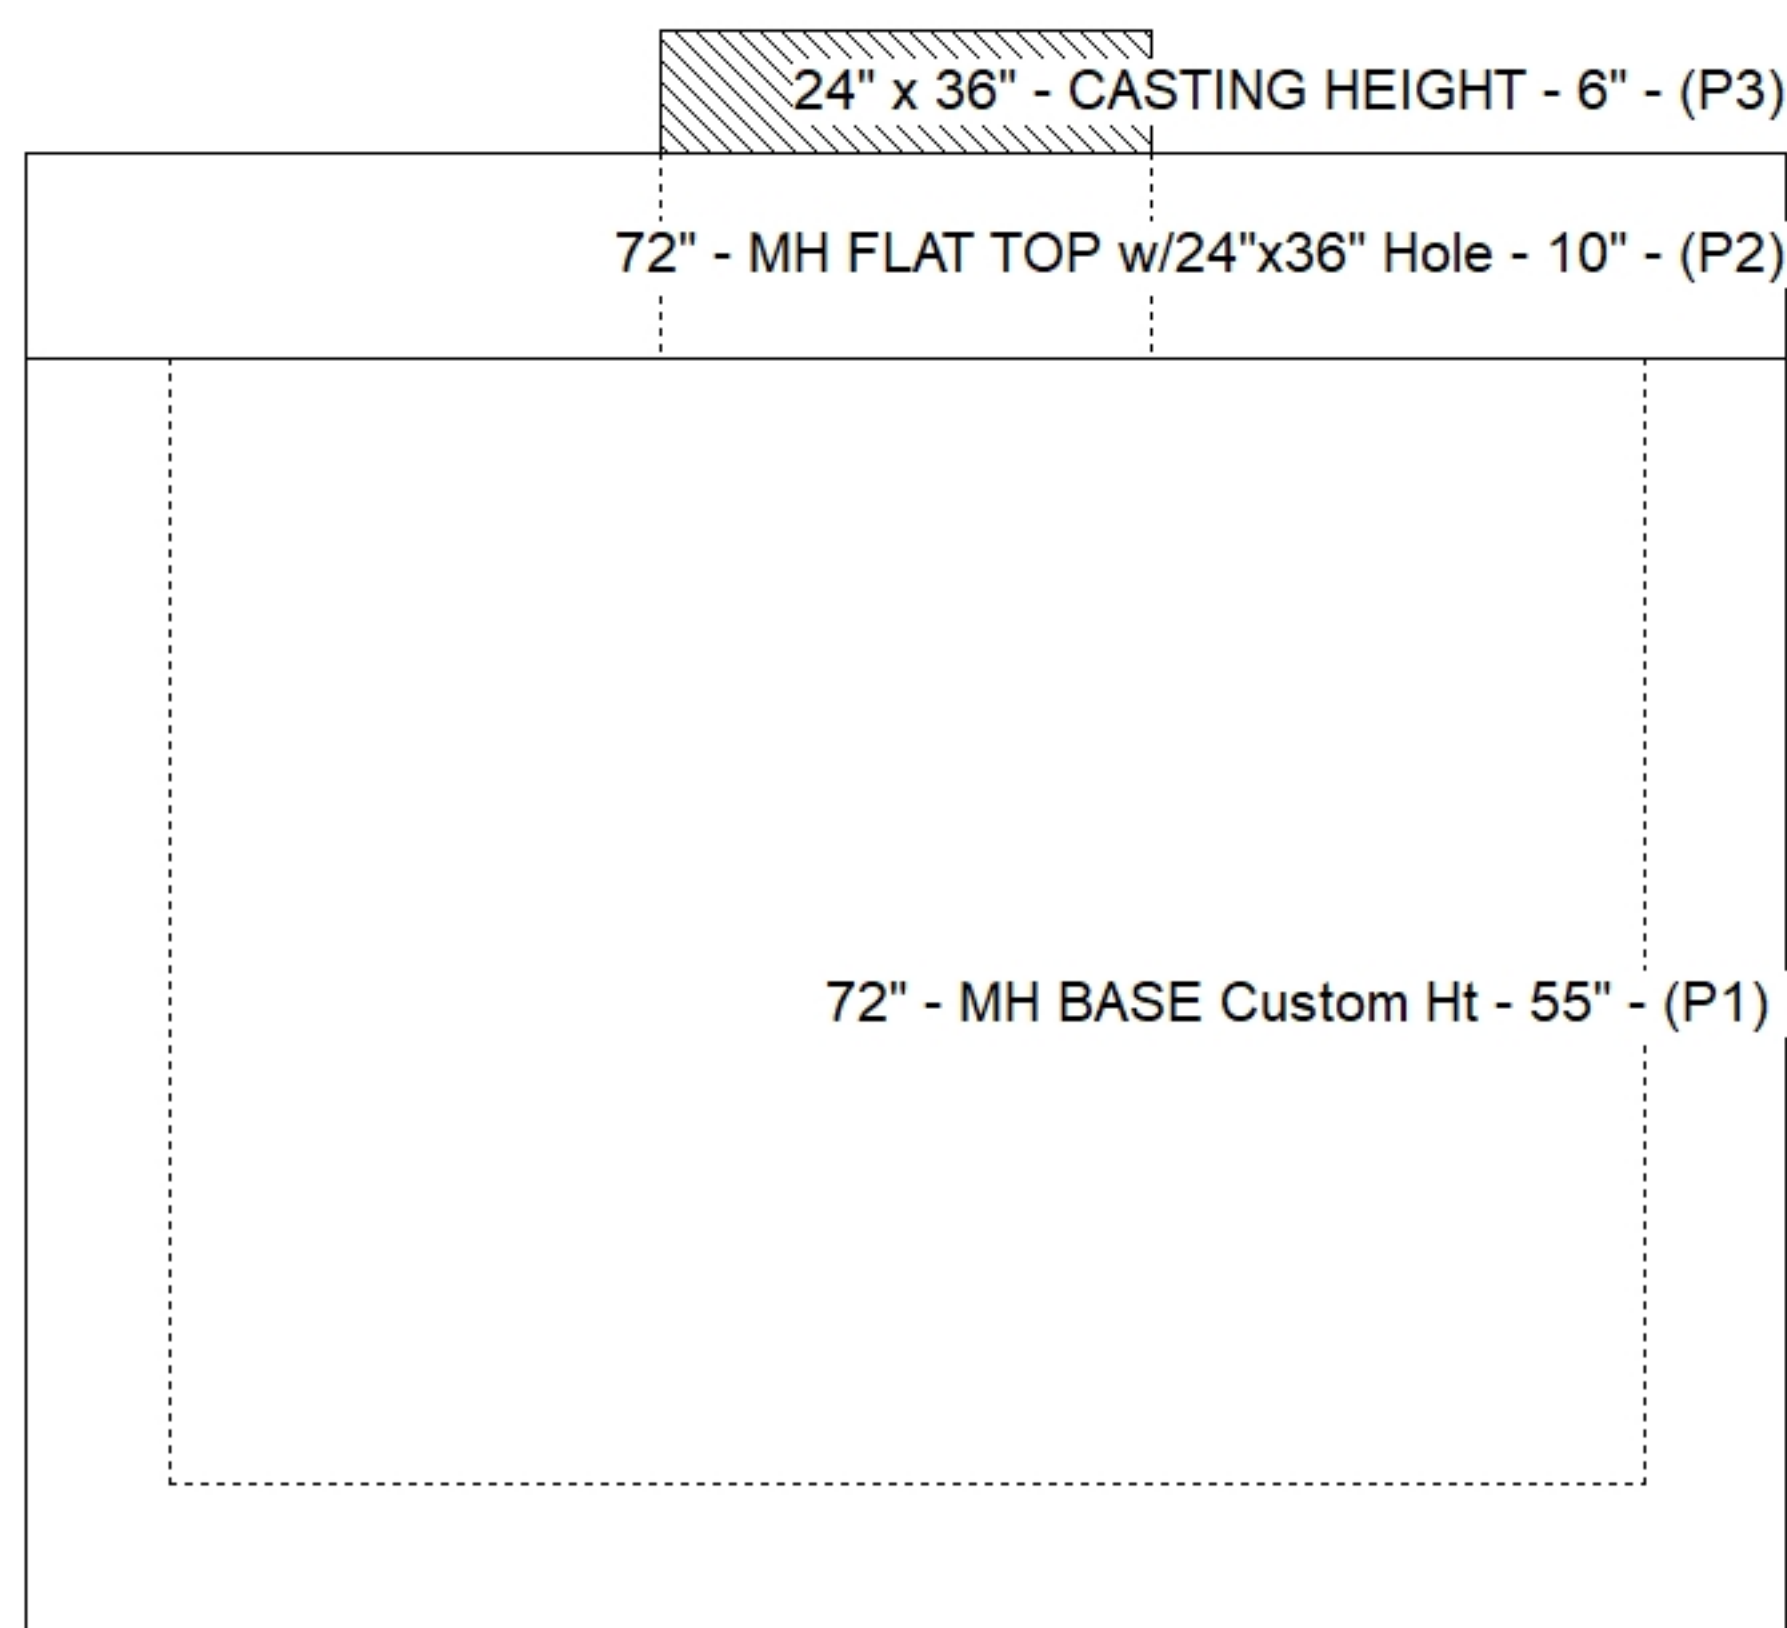

Default - Interior Dimensions

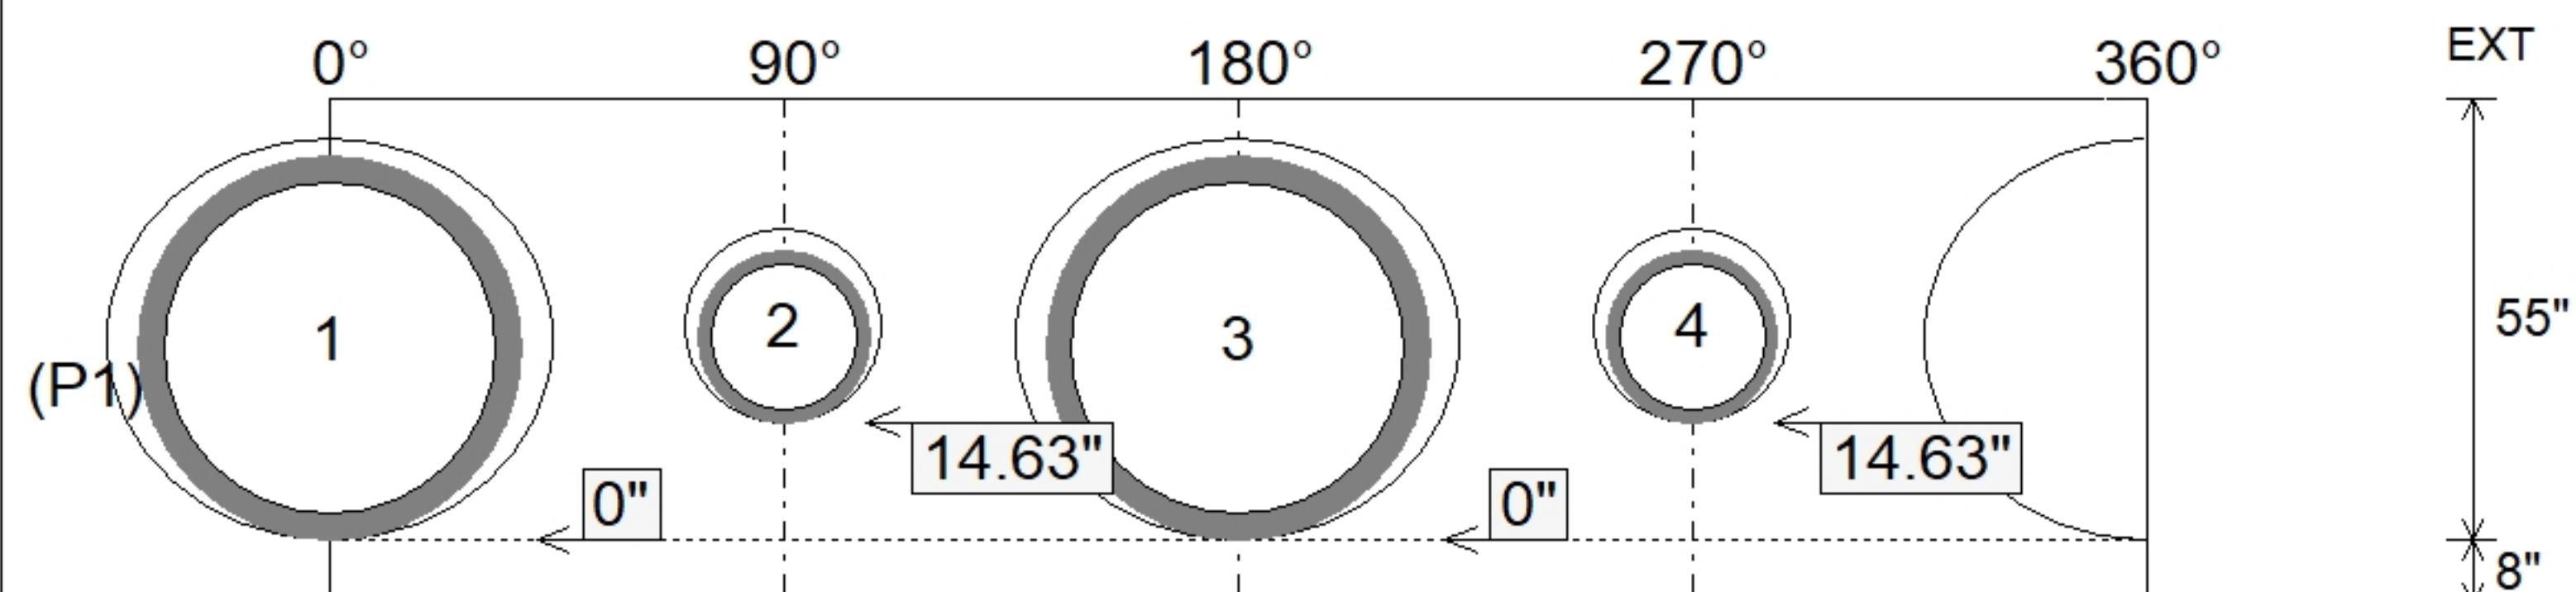

Submittal Drawing
9/29/2026 8:25:54 AM

SUBMITTAL
APPROVED BY:
